


SCHEDULE 2: CONTRACT PROGRAMME

The Manufacturer shall provide a detailed Contract Programme in accordance with Clause 8 of this Agreement and this Schedule 2.

Please refer to the PDF document titled "18102016 – Contract Programme".

ID	Task Name	Duration	Start	Finish	Predecessor/Resource Names
1	Complete project	491 days?	Mon 31/10/16	Thu 15/11/18	
2	SYSTEM DESIGN	109.25 days	Mon 31/10/16	Fri 31/03/17	
3	SDR01 Engineering Plan	24.25 days	Mon 31/10/16	Fri 02/12/16	
15	SDR02 Product Specification	50 days	Fri 11/11/16	Fri 20/01/17	
16	SDR02 PrdSpec_ArchDescr HW	20 days	Mon 14/11/16	Fri 09/12/16	7 HW Senior Engineer, Technical Manager
17	SDR02 PrdSpec_ArchDescr SW	30 days	Fri 18/11/16	Fri 30/12/16	8 SW Senior Engineer
18	SDR02 PrdSpec_TechStrucDescr HW	20 days	Mon 12/12/16	Fri 06/01/17	16 HW Senior Engineer, Technical Manager
19	SDR02 PrdSpec_TechStrucDescr SW	10 days	Fri 30/12/16	Fri 13/01/17	17 SW Senior Engineer
20	SDR02 PrdSpec_TechStruc_vs_TSR	10 days	Fri 30/12/16	Fri 13/01/17	16,17 Project Manager
21	SDR02 PrdSpec_Criteria_DagnCompliance	5 days	Fri 13/01/17	Fri 20/01/17	20 Project Manager
22	SDR02 PrdSpec_IntWght_nonMetCmpts	10 days	Fri 11/11/16	Fri 25/11/16	14 Quality Manager
23	SDR03 RAM Strategy Plan	5 days	Fri 11/11/16	Fri 18/11/16	13 RAM manager
24	SDR04 Engineering Safety Management Plan	5 days	Fri 04/11/16	Fri 11/11/16	Safety Manager
25	SDR05 HF Integration Plan	5 days	Fri 25/11/16	Fri 02/12/16	22 Quality Manager
26	SDR06 EMC Strategy	5 days	Mon 09/01/17	Fri 13/01/17	
27	SDR06 EMC Strtg_LineNoiseSgnlEgmnrt	1 day	Mon 09/01/17	Mon 09/01/17	18 Technical Manager
28	SDR06 EMC Strtg_NeighborRfals	1 day	Tue 10/01/17	Tue 10/01/17	27 Technical Manager
29	SDR06 EMC Strtg_NeighborOthers	1 day	Wed 11/01/17	Wed 11/01/17	28 Technical Manager
30	SDR06 EMC Strtg_Compbt_InTrain	1 day	Thu 12/01/17	Thu 12/01/17	29 Technical Manager
31	SDR06 EMC Strtg_ConnectRadio	1 day	Fri 13/01/17	Fri 13/01/17	30 Technical Manager
32	SDR07 EMC Control Plan	10 days	Fri 10/02/17	Fri 24/02/17	19 HW Senior Engineer
33	SDR08 Interface Control Document	10 days	Fri 30/12/16	Fri 13/01/17	16,17 SW Engineer
34	SDR09 Project Assurance Plan	5 days	Fri 02/12/16	Fri 09/12/16	25 Quality Manager
35	SDR10 Quality Plan	8 days	Fri 09/12/16	Wed 21/12/16	
36	SDR10 QPlan_KeyParamt_Authr_Respnc	1 day	Fri 09/12/16	Mon 12/12/16	34 Quality Manager
37	SDR10 QPlan_OrignstrChart	1 day	Mon 12/12/16	Tue 13/12/16	36 Quality Manager
38	SDR10 QPlan_CntrlMethods_Mat_ServcProc	1 day	Tue 13/12/16	Wed 14/12/16	37 Quality Manager
39	SDR10 QPlan_MethdStrct_Brkd_SwW_OC_ALL	1 day	Wed 14/12/16	Thu 15/12/16	38 Quality Manager
40	SDR10 QPlan_RecordsQA_TL_LUL	1 day	Thu 15/12/16	Fri 16/12/16	39 Quality Manager
41	SDR10 QPlan_AI_Facility	1 day	Fri 16/12/16	Mon 19/12/16	40 Quality Manager
42	SDR10 QPlan_Specific_Design_Prod_OC	1 day	Mon 19/12/16	Tue 20/12/16	41 Quality Manager
43	SDR10 QPlan_ID_Plan_Staf_Tmg_Certif	1 day	Tue 20/12/16	Wed 21/12/16	42 Quality Manager
44	SDR11 Configuration Management Plan	3 days	Wed 21/12/16	Mon 26/12/16	43 Quality Manager
45	SDR12 Requirements Management Plan	24 days	Mon 26/12/16	Fri 27/01/17	
46	SDR12 ReqMgmtPlan_TRS_ID_Record	5 days	Mon 26/12/16	Mon 02/01/17	44 Quality Manager
47	SDR12 ReqMgmtPlan_TRS_ID_Record SW	10 days	Fri 13/01/17	Fri 27/01/17	19 SW Senior Engineer
48	SDR12 ReqMgmtPlan_TRS_ID_Record HW	10 days	Mon 09/01/17	Fri 20/01/17	18 HW Senior Engineer
49	SDR12 ReqMgmtPlan_TRS_ID_Record	10 days	Mon 02/01/17	Mon 16/01/17	46 Quality Manager
50	SDR12 ReqMgmtPlan_TRS_ID_Record	1 day	Mon 16/01/17	Tue 17/01/17	49 Quality Manager
51	SDR13 Programme Plan	3 days	Fri 20/01/17	Wed 25/01/17	21 Project Manager
52	SDR14 Initial Test Plan	30 days	Fri 30/12/16	Fri 10/02/17	16,17 Senior Test Engineer
53	SDR15 Initial Production Plan	22 days	Wed 25/01/17	Fri 24/02/17	
54	SDR15 InPrdPlan_PP1_ProdPlanning	4 days	Wed 25/01/17	Tue 31/01/17	51 Production Manager
55	SDR15 InPrdPlan_PP2_FcbsAlloc	2 days	Tue 31/01/17	Thu 02/02/17	54 Production Manager
56	SDR15 InPrdPlan_PP3_ProdEngChgs	2 days	Thu 02/02/17	Mon 06/02/17	55 Production Manager
57	SDR15 InPrdPlan_PP4_Note_Fabr_ToolsEq	2 days	Mon 06/02/17	Wed 08/02/17	56 Production Manager
58	SDR15 InPrdPlan_PP5_OrdLongLT	2 days	Wed 08/02/17	Fri 10/02/17	57 Production Manager
59	SDR15 InPrdPlan_PP6_RoutineTel	10 days	Fri 10/02/17	Fri 24/02/17	58 Production Manager
60	SDR16 Manufacturer's Risk Register	5 days	Fri 04/11/16	Fri 11/11/16	Production Manager
61	SDR17 Software Management Plan	10 days	Fri 27/01/17	Fri 10/02/17	19 SW Senior Engineer
62	SDR18 Software Design Development Document	53 days	Tue 17/01/17	Fri 31/03/17	
63	SDR18 SW DgnDevD_SWacts_DRatage	5 days	Fri 10/02/17	Fri 17/02/17	61 SW Senior Engineer
64	SDR18 SW DgnDevD_SWacts_Dntage PLC	20 days	Fri 17/02/17	Fri 17/03/17	63 PLC Engineer
65	SDR18 SW DgnDevD_SWacts_Dntage SW	30 days	Fri 17/02/17	Fri 31/03/17	63 SW Engineer
66	SDR18 SW DgnDevD_SWacts_DRatage	10 days	Fri 17/02/17	Fri 03/03/17	63 Safety Manager
67	SDR19 Initial Obsolescence Management Plan	1 day	Tue 17/01/17	Wed 18/01/17	50 Quality Manager
68	SDR 20 Wiring Condition Survey Report	5 days	Mon 23/01/17	Fri 27/01/17	48 HW Senior Engineer
69	SDR21 Link Spec Validation Report	5 days	Mon 16/01/17	Fri 20/01/17	31 HW Engineer 1
70	SDR22 Functional Test Report	10 days	Mon 23/01/17	Fri 03/02/17	69 HW Engineer 1
71	SDR23 Simulator Specification	10 days	Mon 06/02/17	Fri 17/02/17	70 HW Engineer 1
72	SDR24 System Security Assessment	10 days	Fri 30/12/16	Fri 13/01/17	16,17 Security Consultant
73	SYSTEM DESIGN REVIEW	3 days	Fri 31/03/17	Wed 05/04/17	2,3,15,21,31
74	SDR Approved Payment 1%	0 days	Wed 05/04/17	Wed 05/04/17	73
75	1 day?	1 day?	Mon 31/10/16	Mon 31/10/16	
76	PDR PRELIMINARY DESIGN	108 days	Fri 31/03/17	Thu 28/09/17	
77	PDR01 Updated Product Specification HW	10 days	Wed 05/04/17	Wed 19/04/17	73 HW Senior Engineer, Technical Manager
78	PDR01 Updated Product Specification SW	10 days	Wed 05/04/17	Wed 19/04/17	73 SW Senior Engineer
79	PDR02 Completed RAM Strategy Plan	10 days	Wed 05/04/17	Wed 19/04/17	73 RAM manager
80	PDR03 Completed Engineering Safety Management Plan	20 days	Mon 12/06/17	Mon 07/09/17	73 Safety Manager
81	PDR04 Completed HF Integration Plan	5 days	Wed 05/04/17	Wed 12/04/17	73 Quality Manager
82	PDR05 EMC Test Specification	15 days	Wed 05/04/17	Wed 26/04/17	73 HW Engineer 1, HW Engineer 2
83	PDR06 Updated Interface Control Document	5 days	Wed 19/04/17	Wed 26/04/17	77 HW Senior Engineer
84	PDR07 Interface Definition Documents	3 days	Wed 26/04/17	Mon 01/05/17	82 HW Engineer 1
85	PDR08 Updated Quality Plan	2 days	Wed 12/04/17	Fri 14/04/17	81 Quality Manager
86	PDR09 Updated Configuration Management Plan	1 day	Fri 14/04/17	Mon 17/04/17	85 Quality Manager
87	PDR10 Updated Manufacturer's Risk Register	10 days	Wed 05/04/17	Wed 19/04/17	73 Production Manager
88	PDR11 Preliminary Declaration of Design Performance	15 days	Wed 05/04/17	Wed 26/04/17	73 Senior Test Engineer
89	PDR12 General assembly and component drawings/models	10 days	Wed 05/04/17	Wed 19/04/17	73 Mechanical engineer
90	PDR13 Concept Design Calculations	15 days	Wed 26/04/17	Wed 17/05/17	83 Project Manager
91	PDR14 System Integration, Unit and Train Test Specification	20 days	Wed 26/04/17	Wed 24/05/17	86 Senior Test Engineer
92	PDR15 System Integration, Unit and Train Test Plan	20 days	Wed 24/05/17	Wed 21/06/17	91 Senior Test Engineer

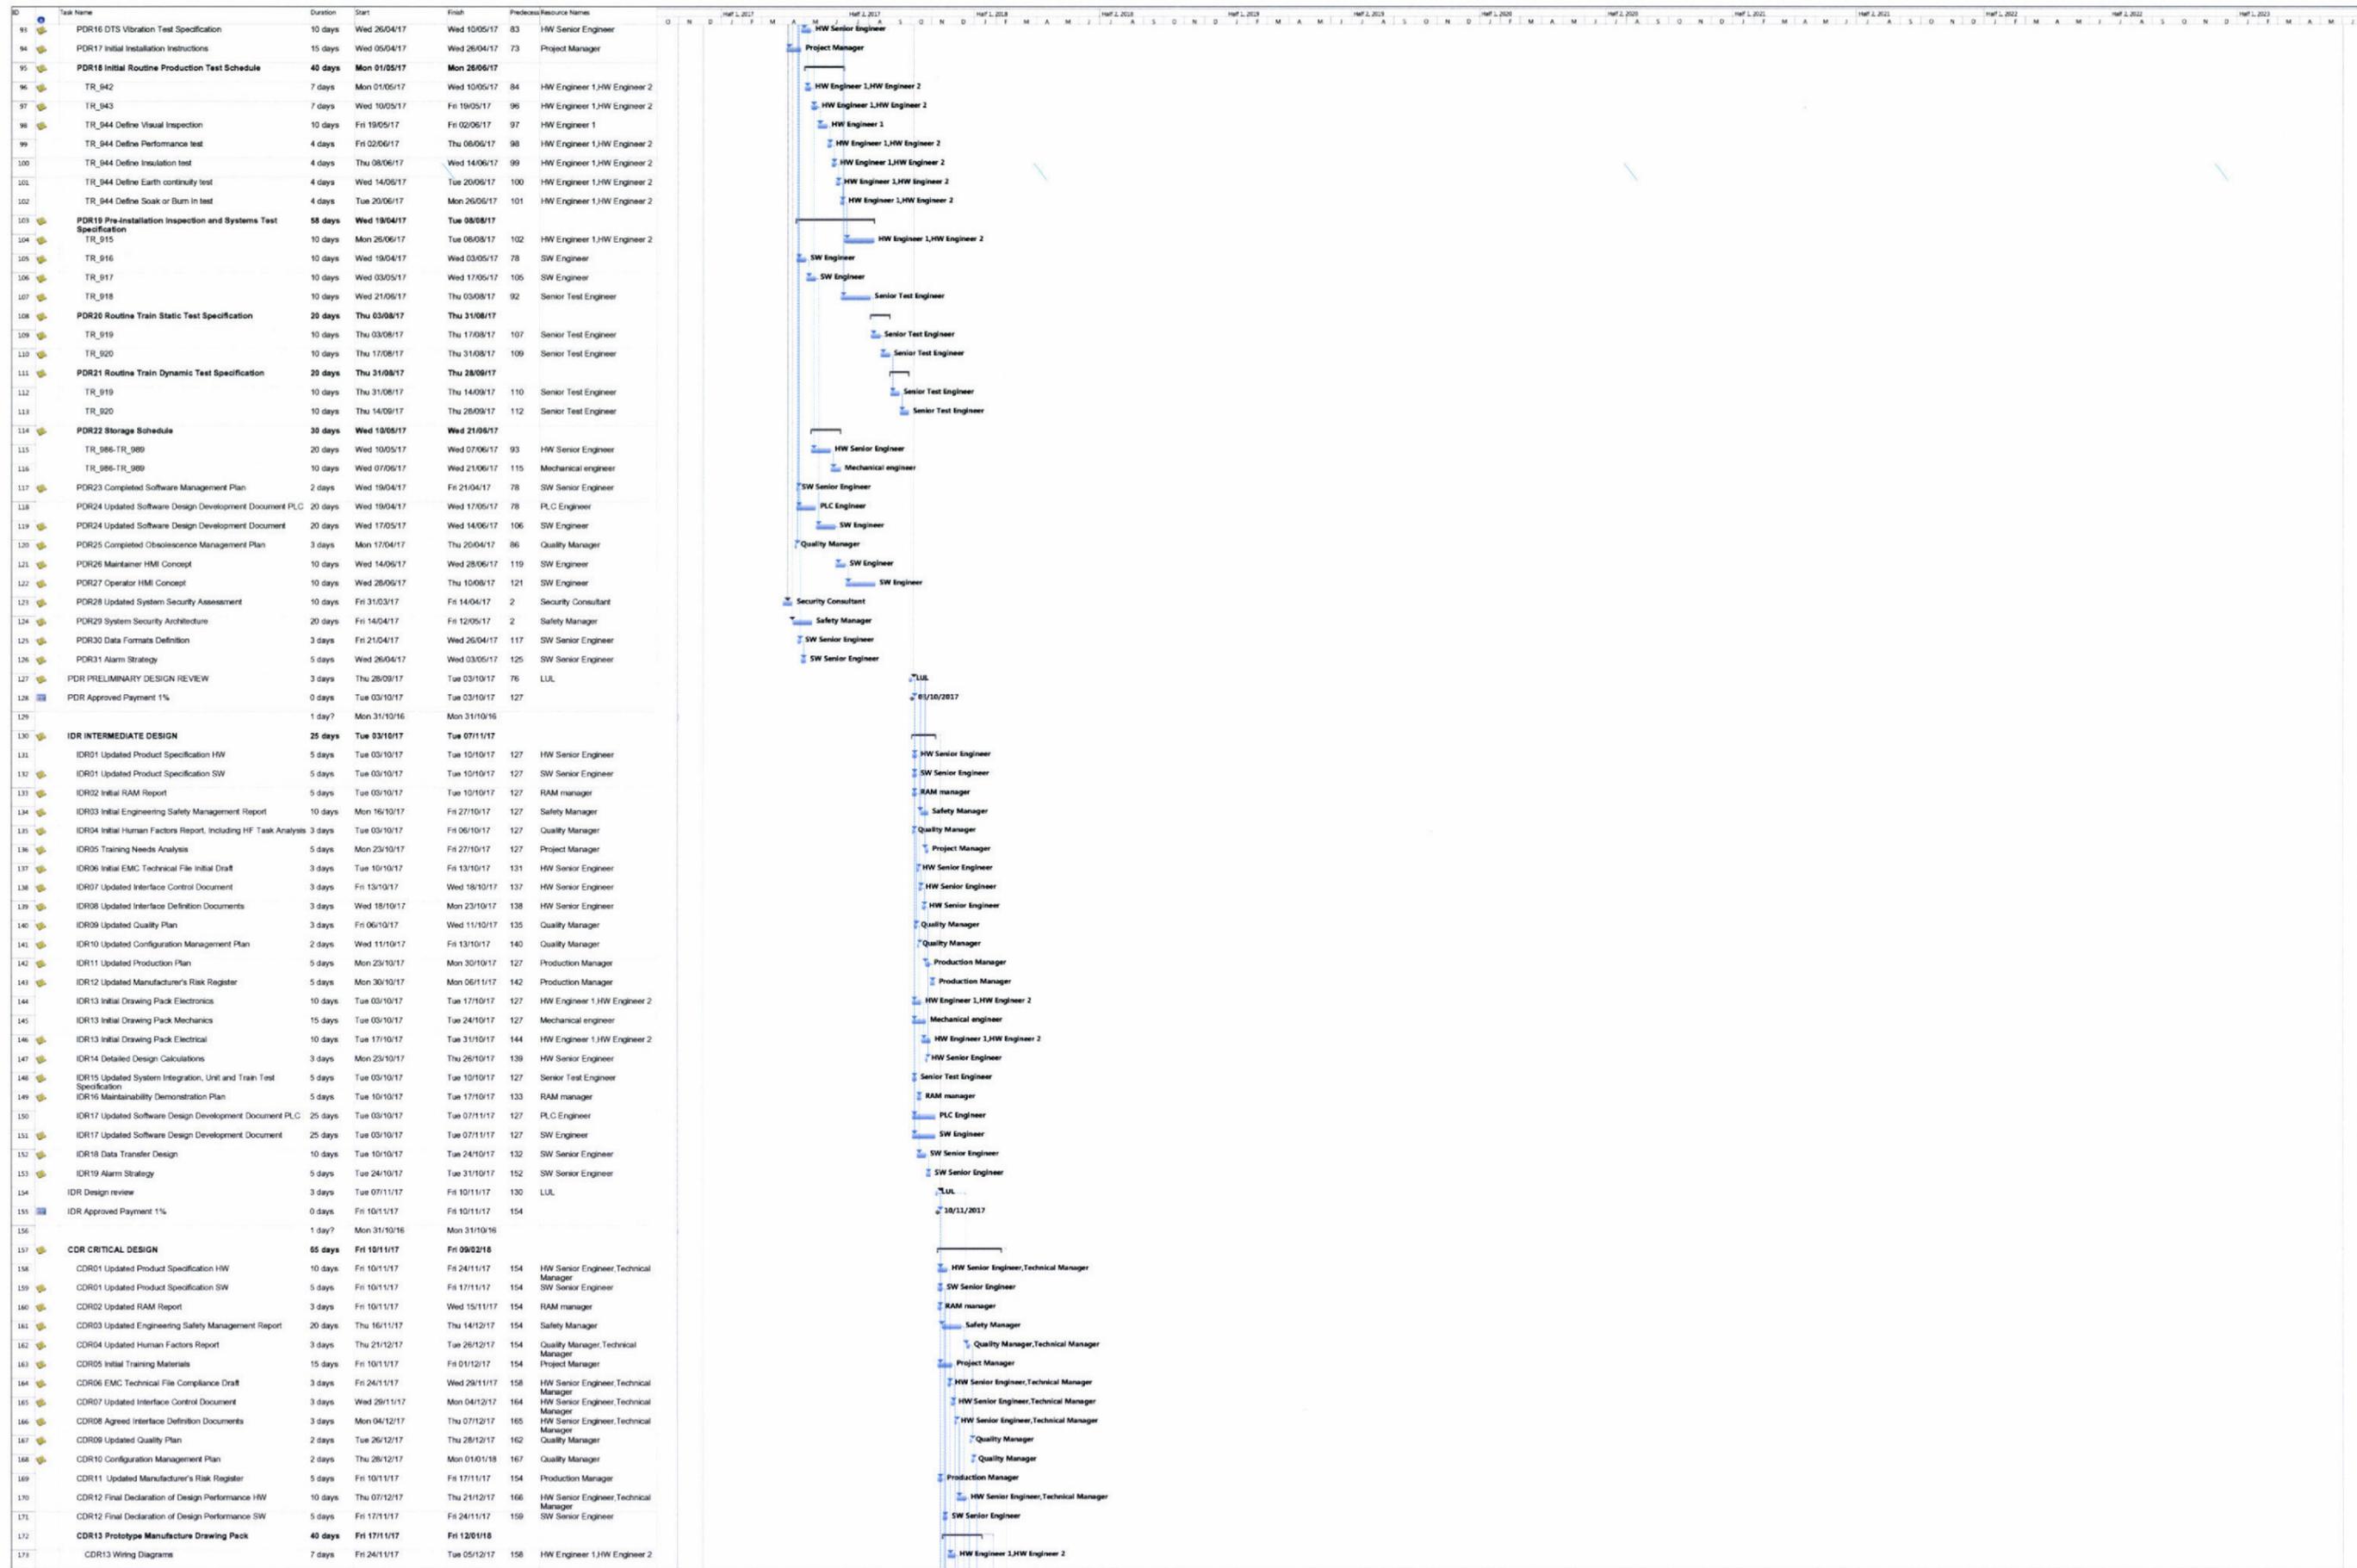

Task Name	Duration	Start	Finish	Process/Resource Name	Start	Finish	Resource
CDR13 Electrical Schematics	7 days	Tue 05/12/17	Thu 14/12/17	173 HW Engineer 1, HW Engineer 2			HW Engineer 1, HW Engineer 2
CDR13 Electronic Schematics	7 days	Thu 14/12/17	Mon 25/12/17	174 HW Engineer 1, HW Engineer 2			HW Engineer 1, HW Engineer 2
CDR13 PCB Layouts	7 days	Mon 25/12/17	Wed 03/01/18	175 HW Engineer 1, HW Engineer 2			HW Engineer 1, HW Engineer 2
CDR13 General Arrangement Drawings	7 days	Wed 03/01/18	Fri 12/01/18	176 HW Engineer 1, HW Engineer 2			HW Engineer 1, HW Engineer 2
CDR13 Assembly Drawings	10 days	Fri 17/11/17	Fri 01/12/17	169 Mechanical engineer			Mechanical engineer
CDR13 Mechanical Engineering/Enclosure Drawings	10 days	Fri 01/12/17	Fri 15/12/17	178 Production Manager			Production Manager
CDR14 Design Calculations	10 days	Fri 01/12/17	Fri 15/12/17	163 Project Manager			Project Manager
CDR15 Final Schedule of Non-Metallic Components	3 days	Mon 01/01/18	Thu 04/01/18	168 Quality Manager			Quality Manager
CDR16 Final System Integration, Unit and Train Test Specification	10 days	Fri 10/11/17	Fri 24/11/17	154 Senior Test Engineer			Senior Test Engineer
CDR17 Component List	5 days	Fri 15/12/17	Fri 22/12/17	179 Production Manager			Production Manager
CDR18 Weight Schedule	3 days	Fri 22/12/17	Wed 27/12/17	183 Production Manager			Production Manager
CDR19 Reliability Management Plan	3 days	Wed 15/11/17	Mon 20/11/17	160 RAM manager			RAM manager
CDR20 Draft Maintenance Documents (Including Installation Instructions)	10 days	Fri 15/12/17	Fri 29/12/17	180 Project Manager			Project Manager
CDR21 Physical and Functional Configuration Specification	5 days	Thu 21/12/17	Thu 28/12/17	170 HW Senior Engineer			HW Senior Engineer
CDR22 Updated Routine Production Test Schedule	3 days	Wed 27/12/17	Mon 01/01/18	184 Production Manager			Production Manager
CDR23 Updated Pre-Installation Inspection and Systems Test Specification	5 days	Thu 28/12/17	Thu 04/01/18	167 HW Senior Engineer			HW Senior Engineer
CDR24 Updated Routine Train Static Test Specification	10 days	Fri 24/11/17	Fri 08/12/17	182 Senior Test Engineer			Senior Test Engineer
CDR25 Updated Routine Train Dynamic Test Specification	10 days	Fri 08/12/17	Fri 22/12/17	190 Senior Test Engineer			Senior Test Engineer
CDR26 Updated Storage Schedule	10 days	Thu 04/01/18	Thu 18/01/18	189 HW Senior Engineer			HW Senior Engineer
CDR27 Completed Software Design Development Document PLC	20 days	Fri 10/11/17	Fri 08/12/17	154 PLC Engineer			PLC Engineer
CDR27 Completed Software Design Development Document SW	20 days	Fri 17/11/17	Fri 15/12/17	159 SW Engineer			SW Engineer
CDR28 HMI Testing Specification	10 days	Fri 22/12/17	Fri 05/01/18	191 Senior Test Engineer			Senior Test Engineer
CDR29 System Security Assessment	5 days	Fri 10/11/17	Fri 17/11/17	154 Security Consultant			Security Consultant
CDR30 System Security Architecture	10 days	Thu 14/12/17	Thu 28/12/17	161 Safety Manager			Safety Manager
CDR31 Data Formats Document	5 days	Fri 15/12/17	Fri 22/12/17	194 SW Engineer			SW Engineer
CDR32 Data Transfer Design	5 days	Fri 22/12/17	Fri 29/12/17	198 SW Engineer			SW Engineer
CDR33 Alarm List	10 days	Fri 08/12/17	Fri 22/12/17	193 PLC Engineer			PLC Engineer
CDR34 Type Test of Sub Components	5 days	Thu 18/01/18	Thu 25/01/18	192 HW Senior Engineer			HW Senior Engineer
CDR35 Type Test System Specification	5 days	Thu 25/01/18	Thu 01/02/18	201 HW Senior Engineer			HW Senior Engineer
CDR36 Final System Integration, Unit and Train Test Specification for 'New Systems and Devices'	5 days	Fri 05/01/18	Fri 12/01/18	195 Senior Test Engineer			Senior Test Engineer
CDR37 Pre-Installation Inspection and Systems Test Specification for 'New Systems and Devices'	5 days	Fri 12/01/18	Fri 19/01/18	203 Senior Test Engineer			Senior Test Engineer
CDR38 Routine Train Dynamic Test Specification for 'New Systems and Devices'	5 days	Fri 19/01/18	Fri 26/01/18	204 Senior Test Engineer			Senior Test Engineer
CDR39 Final Pre-Installation Inspection and Systems Test Specification for 'New Systems and Devices'	5 days	Fri 26/01/18	Fri 02/02/18	205 Senior Test Engineer			Senior Test Engineer
CDR40 Penetration Testing Specification for 'New Systems and Devices'	5 days	Fri 02/02/18	Fri 09/02/18	206 Senior Test Engineer			Senior Test Engineer
CDR Design Review	3 days	Fri 09/02/18	Wed 14/02/18	157 LUL			LUL
CDR Approved Payment 1%	0 days	Wed 14/02/18	Wed 14/02/18	208			14/02/2018
STR SYSTEM TEST READINESS	30 days	Wed 14/02/18	Wed 28/02/18				
STR Readiness Review	3 days	Wed 28/03/18	Mon 02/04/18	211 LUL			LUL
STR Approved Payment 2.5%	0 days	Mon 02/04/18	Mon 02/04/18	231			02/04/2018
UTRR UNIT TEST READINESS	58.75 days	Mon 02/04/18	Thu 21/06/18				
UTRR	3 days	Fri 22/06/18	Tue 26/06/18	234 LUL			LUL
UTRR Approved Payment 2.5%	0 days	Tue 26/06/18	Tue 26/06/18	263			26/06/2018
TTRR TRAIN TEST READINESS	48 days	Wed 27/06/18	Wed 03/10/18				
TTRR01 Updated EMC Technical File	3 days	Wed 27/06/18	Fri 29/06/18	263 HW Senior Engineer, Technical Manager			HW Senior Engineer, Technical Manager
TTRR02 Updated EMC Compliance Documentation	3 days	Wed 01/08/18	Fri 03/08/18	267 HW Senior Engineer, Technical Manager			HW Senior Engineer, Technical Manager
TTRR03 Updated Interface Control Document	5 days	Wed 27/06/18	Thu 02/08/18	263 SW Senior Engineer			SW Senior Engineer
TTRR04 Updated Agreed Interface Definition Documents	5 days	Wed 27/06/18	Thu 02/08/18	263 Project Manager			Project Manager
TTRR05 Updated Quality Plan	3 days	Wed 27/06/18	Fri 29/06/18	263 Quality Manager			Quality Manager
TTRR06 Updated Manufacturer's Risk Register	5 days	Wed 27/06/18	Thu 02/08/18	263 Production Manager			Production Manager
TTRR07 Pre-Production Drawing Pack	5 days	Wed 27/06/18	Thu 02/08/18				
TTRR08 Unit Test Report	2 days	Wed 27/06/18	Thu 28/06/18	263 Senior Test Engineer			Senior Test Engineer
TTRR09 Completed Train Test Specification	5 days	Fri 29/06/18	Mon 06/08/18	276 Senior Test Engineer			Senior Test Engineer
TTRR10 Updated Maintainability Demonstration Report	5 days	Wed 27/06/18	Thu 02/08/18	263 RAM manager			RAM manager
TTRR11 Train Fit CRS	10 days	Fri 03/08/18	Thu 16/08/18	270 Project Manager			Project Manager
TTRR12 Updated Installation & Maintenance documents	5 days	Fri 17/08/18	Thu 23/08/18	279 Project Manager			Project Manager
TTRR13 Train Physical Configuration Audit Report	3 days	Mon 06/08/18	Wed 08/08/18	268 Technical Manager			Technical Manager
TTRR14 Train Functional Configuration Audit Report	3 days	Thu 09/08/18	Mon 13/08/18	281 Technical Manager			Technical Manager
TTRR15 Final Routine Production Test	10 days	Tue 07/08/18	Mon 20/08/18	277 Senior Test Engineer, SW Engineer			Senior Test Engineer, SW Engineer, HW Engineer 1
TTRR16 Final Pre-Installation Inspection and Systems Test Specification	5 days	Tue 14/08/18	Mon 20/08/18	282 HW Senior Engineer			HW Senior Engineer
TTRR17 Final Routine Train Static test Specification	5 days	Tue 21/08/18	Mon 27/08/18	284 HW Senior Engineer			HW Senior Engineer
TTRR18 Final Routine Train Dynamic test Specification	5 days	Tue 28/08/18	Mon 03/09/18	285 HW Senior Engineer			HW Senior Engineer
TTRR19 Final Storage	5 days	Tue 04/09/18	Mon 10/09/18	286 HW Senior Engineer			HW Senior Engineer
TTRR20 Simulator Integration Testing Report	5 days	Tue 21/08/18	Mon 27/08/18	283 HW Engineer 1, SW Engineer			HW Engineer 1, SW Engineer
TTRR21 HMI Testing Report	1 day	Tue 28/08/18	Tue 28/08/18	288 Senior Test Engineer			Senior Test Engineer
TTRR22 Updated System Security Assessment	5 days	Wed 27/06/18	Thu 02/08/18	263 Security Consultant			Security Consultant
TTRR23 Penetration Testing Final Configuration	3 days	Wed 28/08/18	Fri 31/08/18	289 Senior Test Engineer			Senior Test Engineer
TTRR24 Final Routine Production Test Schedule	3 days	Fri 24/08/18	Tue 28/08/18	280 Project Manager			Project Manager
TTRR25 Unit test report for 'New Systems and Devices'	3 days	Mon 03/09/18	Wed 05/09/18	291 Senior Test Engineer			Senior Test Engineer
TTRR26 Final Pre-Installation Inspection and Systems Test Specification for 'New Systems and Devices'	5 days	Thu 06/09/18	Wed 12/09/18	293 Senior Test Engineer, Technical Manager			Senior Test Engineer, Technical Manager
TTRR27 Routine Train Dynamic Test results for 'New Systems and Devices'	5 days	Thu 13/09/18	Wed 19/09/18	294 Senior Test Engineer, Technical Manager			Senior Test Engineer, Technical Manager
TTRR28 Final Pre-Installation Inspection and Systems Test Specification for 'New Systems and Devices'	5 days	Thu 20/09/18	Wed 26/09/18	295 Senior Test Engineer			Senior Test Engineer
TTRR29 Penetration Testing Final Configuration for 'New Systems and Devices'	5 days	Thu 27/09/18	Wed 03/10/18	296 Senior Test Engineer			Senior Test Engineer
TTRR30 Final Routine Train Dynamic Production Test Schedule for 'New Systems and Devices'	3 days	Wed 29/08/18	Fri 31/08/18	292 Project Manager			Project Manager
TTRR	3 days	Thu 04/10/18	Mon 08/10/18	266 LUL			LUL
TTR Approved Payment 3%	0 days	Mon 08/10/18	Mon 08/10/18	299			08/10/2018
TTR	1 day	Mon 31/10/16	Mon 31/10/16				



ID	Task Name	Duration	Start	Finish	Predecessor/Resource Names	HF 1, 2017	HF 2, 2017	HF 1, 2018	HF 2, 2018	HF 1, 2019	HF 2, 2019	HF 1, 2020	HF 2, 2020	HF 1, 2021	HF 2, 2021	HF 1, 2022	HF 2, 2022
538	Train 34 Acceptance for Service	0 days	Sun 15/08/20	Sun 16/08/20													
539	Train 35 Delivery to storage	0 days	Fri 22/05/20	Fri 22/05/20													
541	Train 35 Delivery to Installer	0 days	Fri 29/05/20	Fri 29/05/20													
542	Train 35 Pre Installation Inspection System Test Completion	0 days	Fri 05/06/20	Fri 05/06/20													
543	Train 35 Acceptance for Service	0 days	Wed 26/08/20	Wed 26/08/20													
544	Train 36 Delivery to storage	0 days	Wed 03/06/20	Wed 03/06/20													
545	Train 36 Delivery to Installer	0 days	Wed 10/06/20	Wed 10/06/20													
547	Train 36 Pre Installation Inspection System Test Completion	0 days	Wed 17/06/20	Wed 17/06/20													
548	Train 36 Acceptance for Service	0 days	Mon 07/09/20	Mon 07/09/20													
550	Train 37 Delivery to storage	0 days	Mon 15/06/20	Mon 15/06/20													
551	Train 37 Delivery to Installer	0 days	Mon 22/06/20	Mon 22/06/20													
552	Train 37 Pre Installation Inspection System Test Completion	0 days	Mon 29/06/20	Mon 29/06/20													
553	Train 37 Acceptance for Service	0 days	Thu 17/09/20	Thu 17/09/20													
554	Train 38 Delivery to storage	0 days	Thu 25/06/20	Thu 25/06/20													
556	Train 38 Delivery to Installer	0 days	Thu 02/07/20	Thu 02/07/20													
557	Train 38 Pre Installation Inspection System Test Completion	0 days	Thu 09/07/20	Thu 09/07/20													
558	Train 38 Acceptance for Service	0 days	Wed 30/09/20	Wed 30/09/20													
560	Train 39 Delivery to storage	0 days	Tue 07/07/20	Tue 07/07/20													
561	Train 39 Delivery to Installer	0 days	Tue 14/07/20	Tue 14/07/20													
562	Train 39 Pre Installation Inspection System Test Completion	0 days	Tue 21/07/20	Tue 21/07/20													
563	Train 39 Acceptance for Service	0 days	Mon 12/10/20	Mon 12/10/20													
564	Train 40 Delivery to storage	0 days	Fri 17/07/20	Fri 17/07/20													
565	Train 40 Delivery to Installer	0 days	Fri 24/07/20	Fri 24/07/20													
567	Train 40 Pre Installation Inspection System Test Completion	0 days	Fri 31/07/20	Fri 31/07/20													
568	Train 40 Acceptance for Service	0 days	Thu 22/10/20	Thu 22/10/20													
570	Train 41 Delivery to storage	0 days	Wed 29/07/20	Wed 29/07/20													
571	Train 41 Delivery to Installer	0 days	Wed 05/08/20	Wed 05/08/20													
572	Train 41 Pre Installation Inspection System Test Completion	0 days	Wed 12/08/20	Wed 12/08/20													
573	Train 41 Acceptance for Service	0 days	Tue 03/11/20	Tue 03/11/20													
574	Train 42 Delivery to storage	0 days	Tue 11/08/20	Tue 11/08/20													
575	Train 42 Delivery to Installer	0 days	Tue 18/08/20	Tue 18/08/20													
577	Train 42 Pre Installation Inspection System Test Completion	0 days	Tue 25/08/20	Tue 25/08/20													
578	Train 42 Acceptance for Service	0 days	Sun 15/11/20	Sun 15/11/20													
579	Train 43 Delivery to storage	0 days	Fri 21/08/20	Fri 21/08/20													
581	Train 43 Delivery to Installer	0 days	Fri 28/08/20	Fri 28/08/20													
582	Train 43 Pre Installation Inspection System Test Completion	0 days	Fri 04/09/20	Fri 04/09/20													
583	Train 43 Acceptance for Service	0 days	Wed 25/11/20	Wed 25/11/20													
584	Train 44 Delivery to storage	0 days	Wed 02/09/20	Wed 02/09/20													
586	Train 44 Delivery to Installer	0 days	Wed 09/09/20	Wed 09/09/20													
587	Train 44 Pre Installation Inspection System Test Completion	0 days	Wed 16/09/20	Wed 16/09/20													
588	Train 44 Acceptance for Service	0 days	Mon 07/12/20	Mon 07/12/20													
590	Train 45 Delivery to storage	0 days	Mon 14/09/20	Mon 14/09/20													
591	Train 45 Delivery to Installer	0 days	Mon 21/09/20	Mon 21/09/20													
592	Train 45 Pre Installation Inspection System Test Completion	0 days	Mon 28/09/20	Mon 28/09/20													
593	Train 45 Acceptance for Service	0 days	Thu 17/12/20	Thu 17/12/20													
594	Train 46 Delivery to storage	0 days	Thu 24/09/20	Thu 24/09/20													
595	Train 46 Delivery to Installer	0 days	Thu 01/10/20	Thu 01/10/20													
597	Train 46 Pre Installation Inspection System Test Completion	0 days	Thu 08/10/20	Thu 08/10/20													
598	Train 46 Acceptance for Service	0 days	Tue 29/12/20	Tue 29/12/20													
599	Train 47 Delivery to storage	0 days	Tue 05/10/20	Tue 05/10/20													
601	Train 47 Delivery to Installer	0 days	Tue 13/10/20	Tue 13/10/20													
602	Train 47 Pre Installation Inspection System Test Completion	0 days	Tue 20/10/20	Tue 20/10/20													
603	Train 47 Acceptance for Service	0 days	Sun 10/01/21	Sun 10/01/21													
604	Train 48 Delivery to storage	0 days	Fri 16/10/20	Fri 16/10/20													
605	Train 48 Delivery to Installer	0 days	Fri 23/10/20	Fri 23/10/20													
607	Train 48 Pre Installation Inspection System Test Completion	0 days	Fri 30/10/20	Fri 30/10/20													
608	Train 48 Acceptance for Service	0 days	Mon 25/01/21	Mon 25/01/21													
609	Train 49 Delivery to storage	0 days	Wed 28/10/20	Wed 28/10/20													
611	Train 49 Delivery to Installer	0 days	Wed 04/11/20	Wed 04/11/20													
612	Train 49 Pre Installation Inspection System Test Completion	0 days	Wed 11/11/20	Wed 11/11/20													
613	Train 49 Acceptance for Service	0 days	Thu 04/02/21	Thu 04/02/21													
614	Train 50 Delivery to storage	0 days	Mon 08/11/20	Mon 08/11/20													
615	Train 50 Delivery to Installer	0 days	Mon 16/11/20	Mon 16/11/20													
617	Train 50 Pre Installation Inspection System Test Completion	0 days	Mon 23/11/20	Mon 23/11/20													
618	Train 50 Acceptance for Service	0 days	Tue 16/02/21	Tue 16/02/21													
619	Train 51 Delivery to storage	0 days	Thu 19/11/20	Thu 19/11/20													
621	Train 51 Delivery to Installer	0 days	Thu 26/11/20	Thu 26/11/20													
622	Train 51 Pre Installation Inspection System Test Completion	0 days	Thu 03/12/20	Thu 03/12/20													
623	Train 51 Acceptance for Service	0 days	Sun 28/02/21	Sun 28/02/21													
624	Train 52 Delivery to storage	0 days	Tue 01/12/20	Tue 01/12/20													
626	Train 52 Delivery to Installer	0 days	Tue 08/12/20	Tue 08/12/20													
627	Train 52 Pre Installation Inspection System Test Completion	0 days	Tue 15/12/20	Tue 15/12/20													
628	Train 52 Acceptance for Service	0 days	Wed 10/03/21	Wed 10/03/21													
629	Train 53 Delivery to storage	0 days	Wed 16/12/20	Wed 16/12/20													
631	Train 53 Delivery to Installer	0 days	Wed 23/12/20	Wed 23/12/20													
632	Train 53 Pre Installation Inspection System Test Completion	0 days	Wed 30/12/20	Wed 30/12/20													
633	Train 53 Acceptance for Service	0 days	Mon 22/03/21	Mon 22/03/21													
634	Train 54 Delivery to storage	0 days	Mon 28/12/20	Mon 28/12/20													
636	Train 54 Delivery to Installer	0 days	Mon 04/01/21	Mon 04/01/21													
637	Train 54 Pre Installation Inspection System Test Completion	0 days	Mon 11/01/21	Mon 11/01/21													
638	Train 54 Acceptance for Service	0 days	Thu 01/04/21	Thu 01/04/21													
639	Train 55 Delivery to storage	0 days	Thu 07/01/21	Thu 07/01/21													
641	Train 55 Delivery to Installer	0 days	Thu 14/01/21	Thu 14/01/21													
642	Train 55 Pre Installation Inspection System Test Completion	0 days	Thu 21/01/21	Thu 21/01/21													
643	Train 55 Acceptance for Service	0 days	Tue 13/04/21	Tue 13/04/21													
644	Train 56 Delivery to storage	0 days	Tue 19/01/21	Tue 19/01/21													
645	Train 56 Delivery to Installer	0 days	Tue 26/01/21	Tue 26/01/21													
647	Train 56 Pre Installation Inspection System Test Completion	0 days	Tue 02/02/21	Tue 02/02/21													
648	Train 56 Acceptance for Service	0 days	Tue 27/04/21	Tue 27/04/21													
649	Train 57 Delivery to storage	0 days	Fri 29/01/21	Fri 29/01/21													
651	Train 57 Delivery to Installer	0 days	Fri 05/02/21	Fri 05/02/21													
652	Train 57 Pre Installation Inspection System Test Completion	0 days	Fri 12/02/21	Fri 12/02/21													
653	Train 57 Acceptance for Service	0 days	Sun 09/05/21	Sun 09/05/21													
654	Train 58 Delivery to storage	0 days	Wed 10/02/21	Wed 10/02/21													
655	Train 58 Delivery to Installer	0 days	Wed 17/02/21	Wed 17/02/21													
