

Kier Highways Project No: 570112
Client Reference No: 570112
A30 Whiddon Down to Crockerwell EB
MP 170.2 - 175.7 RS
Pre-Construction Information

	Yes	No
Are Works to be carried out under the Commission / Contract Health and Safety Plan?		✓
Is the Scheme notifiable under the CDM Regulations 2015?		✓
1. Last longer than 30 working days and have more than 20 workers simultaneously at any point in the project;		✓
2. Exceed 500 person days		✓

Project type as categorised by GG104 (if applicable to contract / delete in not required)	A
<p>* If applicable GG104 will determine the Kier Highways minimum Scheme Principal Designer (Scheme PD) level. Refer to SHEMS-FOR-HIG-S-055 for GG104 type categorisation and minimum Scheme PD level. Type A projects the Design Team Lead, Type B projects the Senior Manager, Type C projects the Service Director.</p>	

This document has been produced in accordance with the recommendations and requirements of the Construction (Design and Management) Regulations 2015.

Prepared by: (Designer)	
Reviewed by: (Design Team Lead)	
Accepted by: (Scheme PD)	



Authorised By: [REDACTED]	Page 1 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



Site Specific Hazards Identified in Design		
<i>ONLY include significant and unusual hazards that a competent contractor would need to know, could not reasonably foresee, or are likely to be difficult to manage effectively.</i>		
Activity	Residual Hazard	Comments
Cores	Potential Presence of coal tar.	Contractor to ensure that all workers wear appropriate PPE at all times during construction works and any tar arisings will be disposed off to licensed tips and in line with the Company policy and the requirements for materials containing tar.

FOR INFORMATION ONLY



Authorised By: [REDACTED]	Page 2 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



1. Project Description

Scope of Works

Survey Scope of Works – Cores

To undertake 50 no. of Cores to determine existing Construction Layers, including PAK marker testing to confirm the likelihood of the presence of Tar Bound Materials (TBM).


For locations, please refer to the following VCS Plans:

- A30 Whiddon Down to Crockernwell EB- Defect Treatment Plan
- A30 Whiddon Down to Crockernwell EB MP 170.2 - 175.7 RS - Core Schedule.

PLEASE NOTE, THIS DOCUMENT COVERS THE SURVEY WORKS ONLY

Location

This site is located on the A30 Whiddon Down to Crockernwell EB MP 170.2 - 175.7

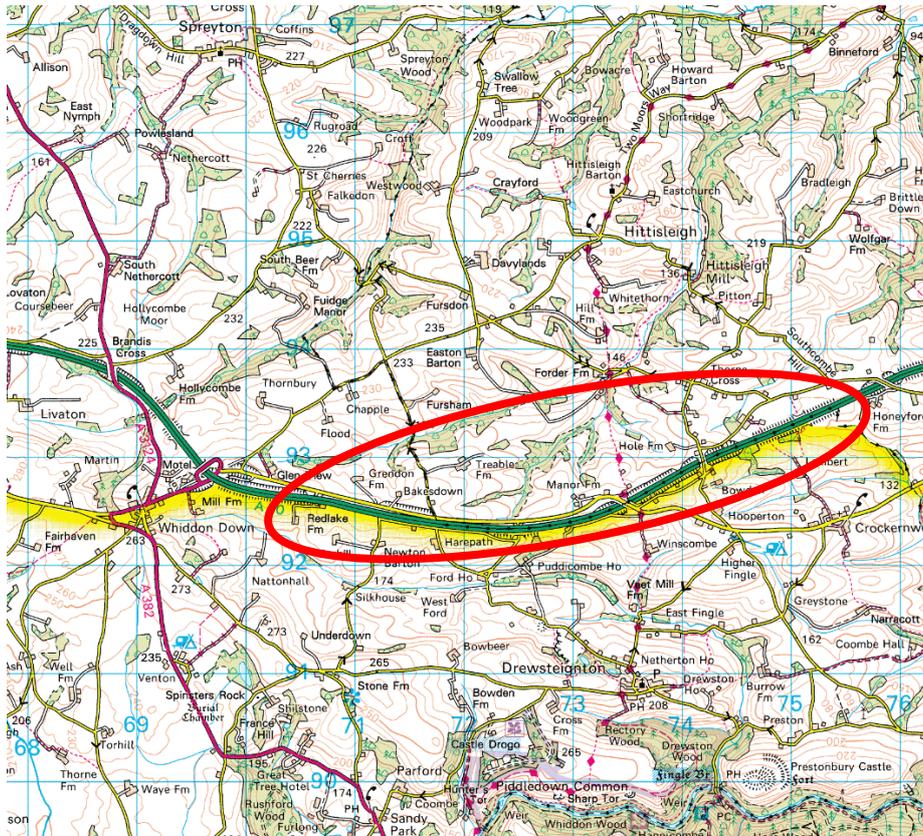

Site Address	This site is located on the A30 Whiddon Down to Crockernwell EB MP 170.2 - 175.7.			
OSGR	From	E 270126 N 92675	To	E 275416 N 93485
Core Locations	Refer to drawings: <ul style="list-style-type: none"> • A30 Whiddon Down to Crockernwell EB - Defect Treatment Plan • A30 Whiddon Down to Crockernwell EB MP 170.2 - 175.7 RS - Core Schedule 			
Traffic Management	Cores within A30 mainline. TM to be A30 EB Lane 1 closure and Lane 2 closure.			
Traffic Flows	A30 Eastbound AADT: 16,036			
Anticipated Working Hours, subject to Traffic Counts	Night time shifts (20:00-04:00)			



Authorised By: [Redacted]	Page 3 of 11	SEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



3. Scheme Specific Requirements			
	Yes	No	Comments
Does an H&S file exist?		X	No existing H&S File has been made available by Highways England.
Site Welfare	X		Welfare van on site for duration of works.
Security / Segregation	X		Existing highway boundary is adequate to protect the site.
Are there any other projects taking place in the vicinity?		X	Unknown at this stage. HE PM to provide details.
Are there any restrictions on vehicle movements?	X		All site vehicles (incl. delivery vehicles) must abide by the TM requirements and regulations 1. Enter and exit site from the dedicated points; 2. Comply with the designated site safety speed limits; All vehicles within Traffic Management shall comply with the conspicuity requirements of Chapter 8.
Are there any restrictions on deliveries, waste collection, or storage?	X		No deliveries to take place unless Traffic Management is in place. No waste shall be stored on site. Waste Carriers Licence required
Are there any parking restrictions?	X		All vehicles and plant within the works area shall be parked in a safe area clear of access and egress points. All vehicles and plant shall be removed from the carriageway prior to removal of traffic management. No Private vehicles are allowed on site
Height Restrictions		X	No over bridges located within the survey extents.
Overhead Cables	X		Locations of O/H located on VCS plans.
Structures		X	No structures located within the survey extents.
Will fire precautions be required?	X		Suitable fire precautions shall be in place and in accordance with the Contractors hot works permit.
Are emergency procedures and means of escape required?	X		The Contractor shall ensure that emergency procedure plans are in place and all staff have been inducted. One lane will remain serviceable throughout the works duration for emergency services at all times. Nearest A&E hospital: Royal Devon and Exeter Hospital, Barrack Rd, Exeter, Devon EX2 5DW Tel: 01392 411611
Are there any areas in or around the site classified as no-go areas?	X		No site personnel shall enter the safety zones or tapers within the extents of the traffic management unless trained and competent for installation / removal / maintenance of TM. Provision of minimum 20m Pedestrian worker Exclusion zone, behind and in front of Operating Road Sweeper to be in place. Sub-Contractor's Method Statements and Risk Statements shall contain suitable risk control to protect pedestrian workers and plant operators.

3. Scheme Specific Requirements			
	Yes	No	Comments
Are there any noise restrictions?	X		The Contractor shall comply with the requirements of BS 5228 Parts 1, 2 & 4 (Noise in Relation to Construction). The Contractor shall ensure that the best practicable means of minimising noise are employed throughout the proposed works ensuring the quietest methods of working are used.
Are temporary works required?		X	
Are there any vibration restrictions?	X		The Contractor shall ensure that the peak particle velocity and frequency generated from any operation during the associated works does not present risk of damage to any structure.
Are there any poor or hazardous ground conditions		X	Unknown at this stage, cores to confirm.
Are there any unstable structures?		X	
Are there any areas classed (existing or designed) classed as confined spaces?		X	
Are there any smoking restrictions?	X		No smoking is allowed on site. Designated smoking areas to be confirmed during site inductions.
Any environmental constraints identified?		X	Unknown at this stage, cores to confirm.

Materials and Substances with Health and / or Safety Hazards

Asbestos – Highways

Lucion Environmental Ltd carried out an Asbestos Refurbishment Survey in 2016 titled 'A30 Devonshire House to Honiton'. The inspection shows that there is asbestos material present within five samples associated with catch pit / fibre pipe material. The proposed survey works will not interfere with any asbestos containing materials.

If Asbestos Containing Materials are found during construction, all works shall stop immediately, and the area is to be isolated from the workforce. The Contractor must inform the Principal Contractor, who will then implement the necessary emergency response procedures in line with the Company policy.

Under no circumstances will the Contractor attempt to remove any Asbestos Containing Materials without prior consent from the overseeing organisation.

Lead

Scope of Works are unlikely to encounter lead.

Tar based pavement / surfacing

Historic core log information confirms that TBM material is unlikely to be present within this section of carriageway

Covid-19 pandemic

The Contractor is to ensure they are protecting their workforce and minimising the risk of spread of infection. They must comply with the latest Government advice on working safely during coronavirus covid-19 which is currently available at <https://www.gov.uk/guidance/working-safely-during-coronavirus->



Authorised By: [REDACTED]	Page 6 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



Materials and Substances with Health and / or Safety Hazards

[covid-19/construction-and-other-outdoor-work](https://www.cic.org.uk/covid-19/construction-and-other-outdoor-work). Further guidance is given in the Construction Leadership Council's "Construction Sector – Site Operating Procedures". The latest version may be found at <http://cic.org.uk/important-documents.php>

The health and safety requirements of any construction activity must not be compromised. If an activity cannot be undertaken in line with social distancing being implemented, or by exception, safely, without risk and mitigating measures then it shall not take place.

Leptospirosis / Weil's disease / Psittacosis

Contact with highway drainage during resurfacing works potential risk of Weil's disease. The Contractor is to ensure sufficient welfare facilities are in place at all times. All appropriate PPE must be worn at all times. Any instances of illness / sickness on site should be reported to the Site Manager/Principal Contractor Representative immediately and the persons affected should seek medical advice.

FOR INFORMATION ONLY



Authorised By: [REDACTED]	Page 7 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



4. Existing Services (Refer to STATS plans listed in Appendix D)				
Statutory Undertaker	Not Present	Over head	Under ground	Comments
Electricity				
400/132kV [pylons]	X			
66kV	X			
33kV		X		Runs parallel with site, not affected by works
11kV		X		Positions Identified on VCS plan
240/415Volts	X			
Water (Foul and Potable)				
Public Foul	X			
Pressurised Foul	X			
Public Combined Gravity	X			
Pressurised Combined	X			
Culverted Watercourse	X			
Water Main			X	
Aqueduct	X			
Communications				
Communications			X	Present within verge and central reservation
British Telecom				
British Telecom			X	
Gigaclear PLc	X			
Vodafone	X			
SSE	X			
Virgin Media			X	Present within verges
National Grid				
National Grid	X			
Transco				
LP Mains	X			
MP Mains	X			
IP Mains	X			
LHP Mains	X			
NHP Mains	X			
Government Pipelines				
CLH Pipelines Ltd	X			
Defence Infrastructure Organisation Fuel Pipeline	X			
Fisher German Pipelines				
Fisher German Pipelines	X			
Energis				
Energis				
Motorway Communication				
Motorway Comms	X			
Street Lighting				
Street lighting	X			
Highway Drainage				
Various apparatus			X	

NOTE – THE ABOVE STATS INFORMATION IS BASED ON EXISTING RECORDS. STATS RECORDS EXPIRE EVERY 3 MONTHS. PRIOR TO WORKS, LIAISON WITH THE RELEVANT UTILITY COMPANIES IS AGAIN NECESSARY TO ENSURE CURRENT STATS INFORMATION IS PROVIDED.



Authorised By: [REDACTED]	Page 8 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



5. Health and Safety File Requirements

All information will be produced in an electronic format. The format of the electronic data issued is to be as follows: All documents and product data sheets are to be in PDF format, drawings are to be in PDF and AutoCAD DWG format.

The Principal Contractor shall collate all appropriate information as it becomes available, and this shall subsequently be collated in the File. The Principal Contractor is to implement an early procedure that advises contractors and materials suppliers of the detailed requirements for this record information. The health and safety file will be created and/or updated in accordance with the requirements of the IAN105/08.


FOR INFORMATION ONLY



Authorised By: [REDACTED]	Page 9 of 11	SHEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



Appendix A – Location Plan

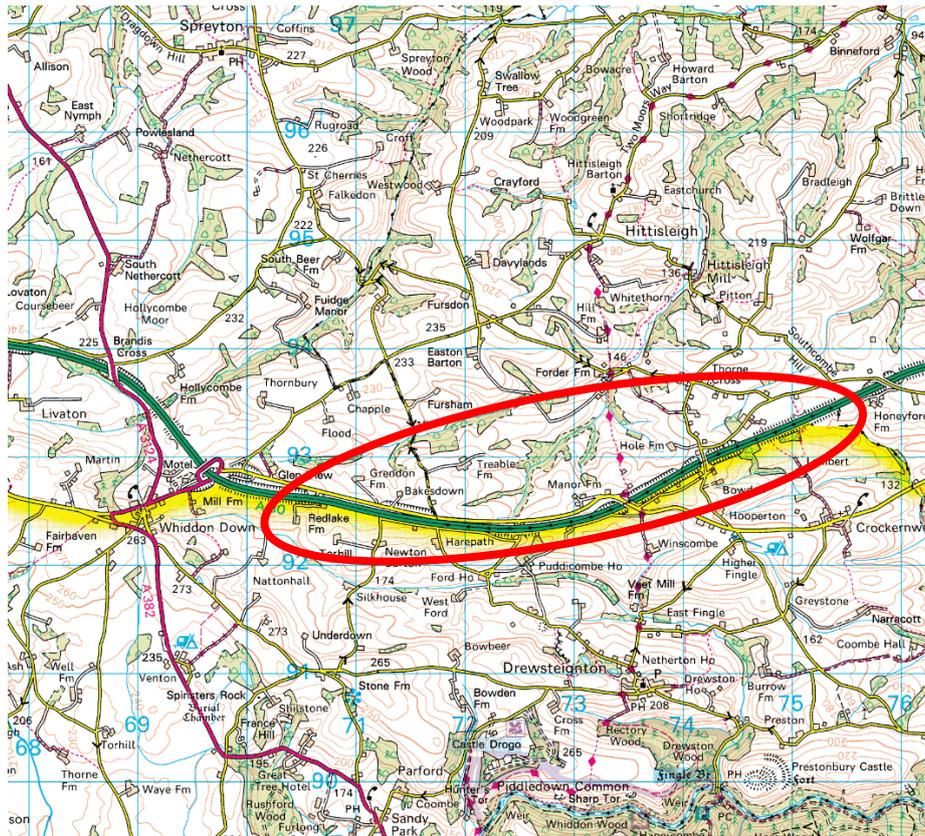

Appendix B – Construction Drawings

Reference	Rev	Title
A30 Whiddon Down to Crockernwell EB- Defect Treatment Plan	-	-
A30 Whiddon Down to Crockernwell EB MP 170.2 - 175.7 RS - Core Schedule.	-	-

Appendix C – Existing Records and As-Built Drawings

Reference	Rev	Title	Company
Refer to Document / Drawings Transmittal Register.			

Appendix D – Statutory Undertaker Drawings

Reference	Rev	Title	Company
Refer to Document / Drawings Transmittal Register.			



Authorised By: [Redacted]	Page 10 of 11	SEMS-FOR-HIG-051
Author: Highways CDM Team	Date: October 2019	Version: 1.0
As part of our system review, this document is valid until April 2021		



Appendix F – List of Structures

HE Structure Key	Name	Structure Type	Comments
ID 12700	Torhill cottage	Underpass	Section Ch.1100A30/447+600m
ID 12698	Puddicombe Lane	Underpass	Section Ch.1100A30/447+2500m
ID 12697	Hask Lane	overbridge	Section Ch.1100A30/450+555m
ID 12696	Hoopertone Lane	overbridge	Section Ch.1100A30/450+1390m
ID 12695	Meadow farm	underpass	Section Ch..1100A30/450+2335m

Appendix G – Asbestos Action Plans

Report No.	Report Title	Plan Owner	Date
122738	A30 Devonshire House to Honiton	Lucion Environmental Ltd	2016

Appendix H – Overhead Cables

Overhead Cables Information
<p>Overhead cables are located within the survey scope of works.</p> <p>All overhead power lines have been identified on the scheme drawings, however information regarding safe working heights in accordance with GS6 has not been indicated. Prior to the commencement of works on site, overhead power line heights to be confirmed and recorded by way of signature and date by a trained and competent person. Survey works to be undertaken using suitable traffic management arrangements or utilisation of scheme TM where appropriate.</p>
