


M621 Junction 1 To 7 Improvements - Stage 5 CI 32.1 Week 120 LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

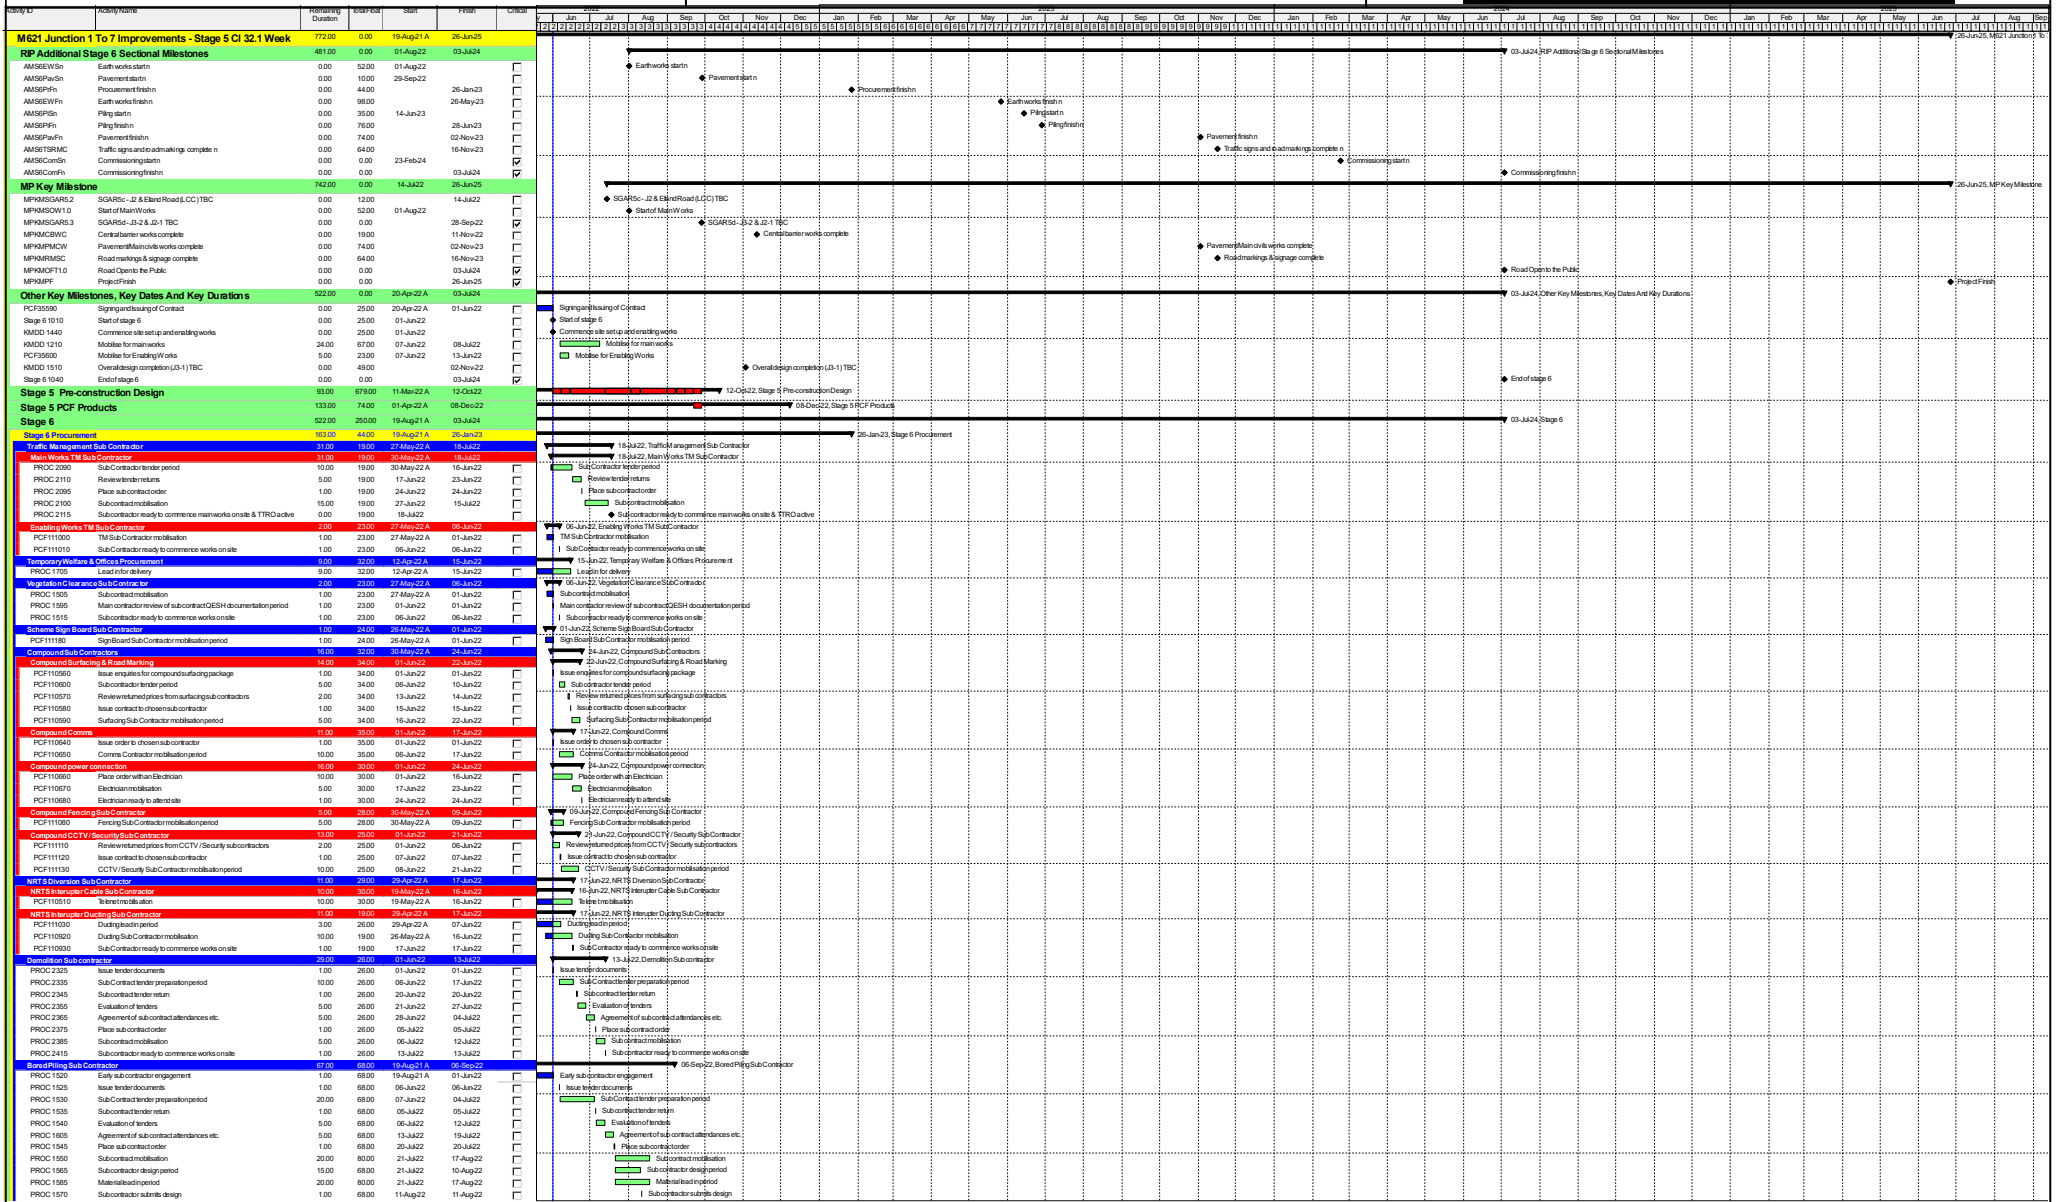


Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CI 32.1 Week 120 LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

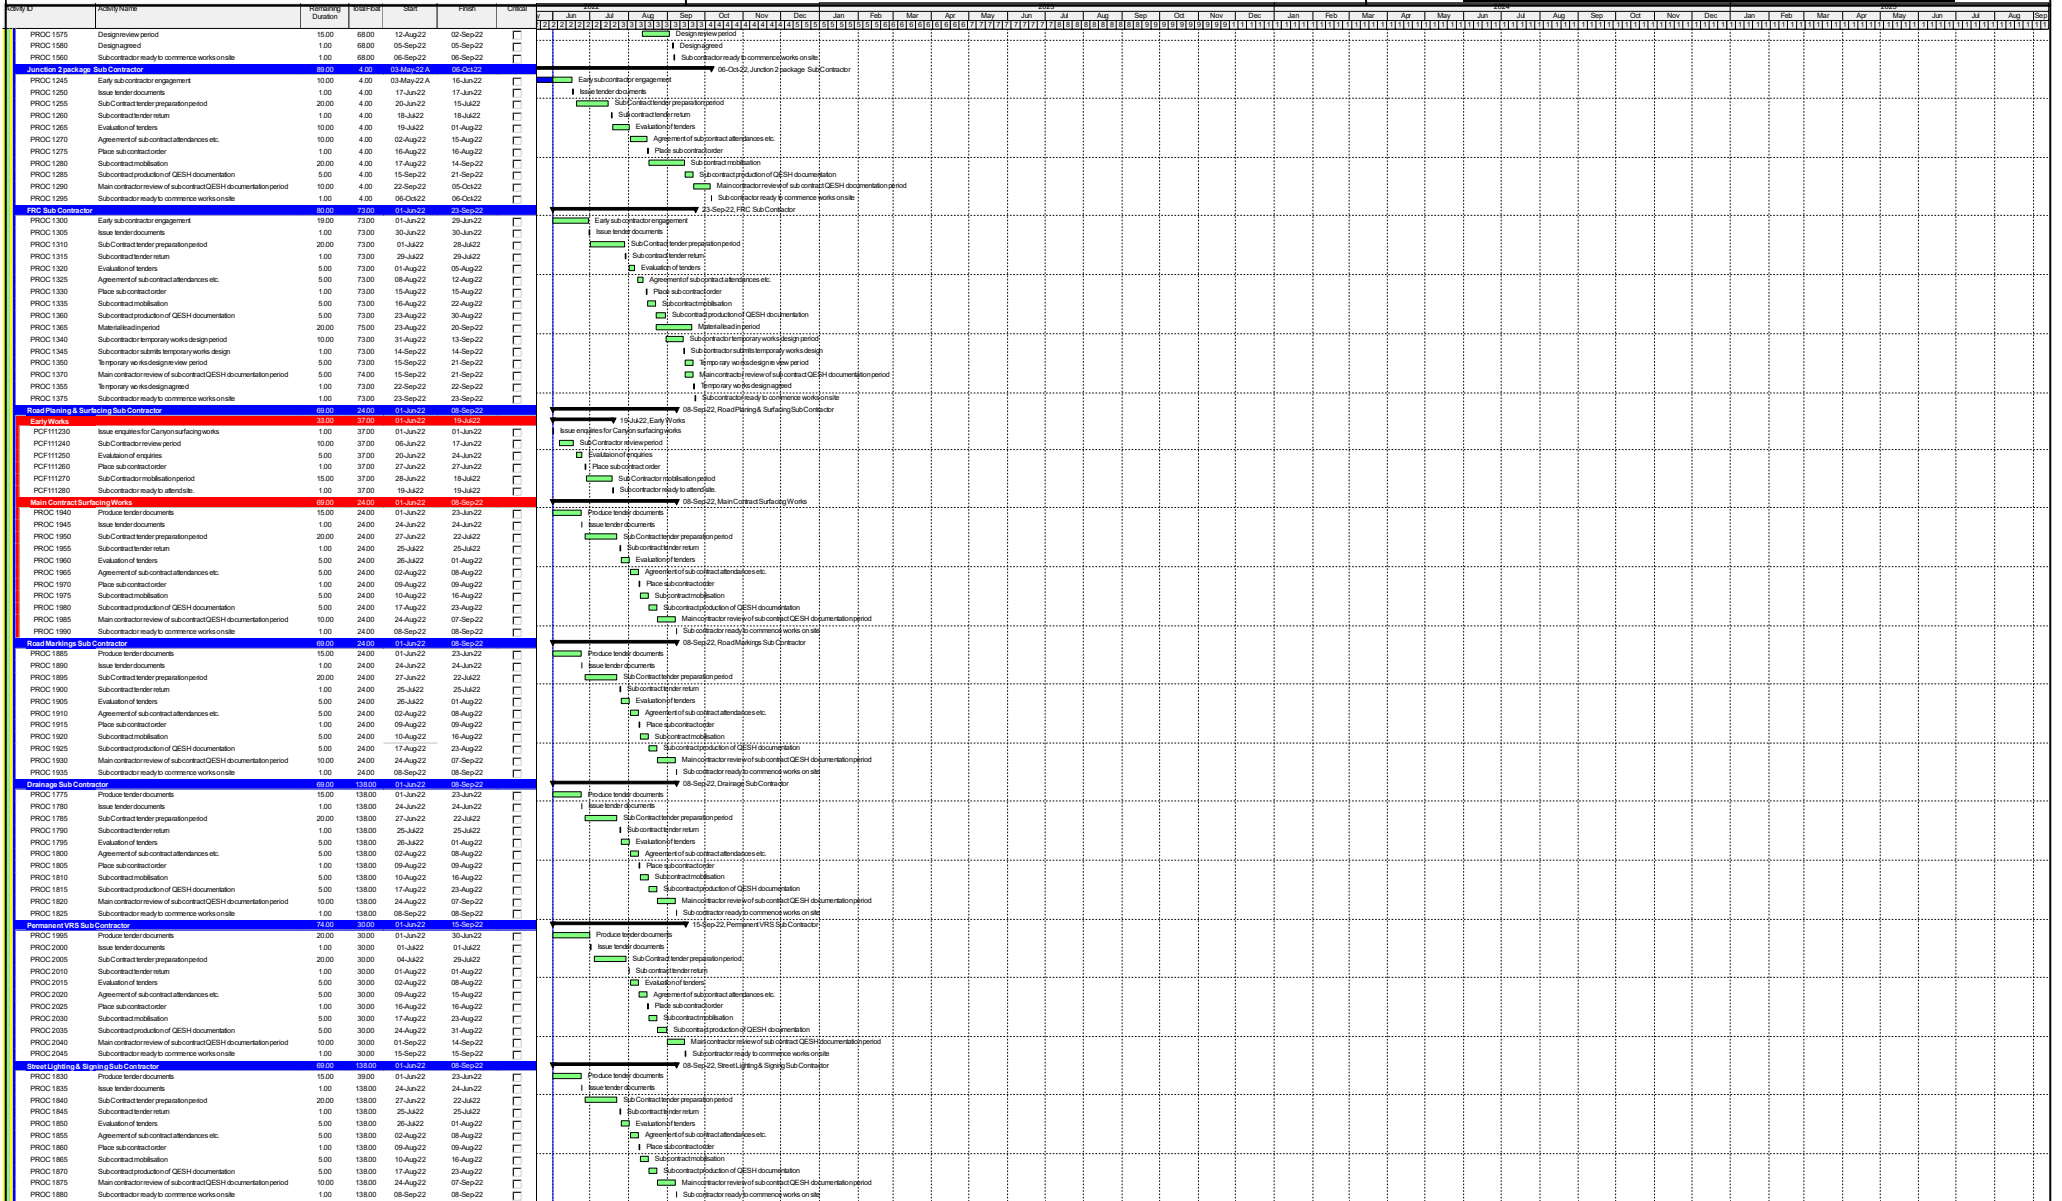


Actual Work Critical Remaining Work
Remaining Work ◆ Milestone

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CL32.1 Week 120
LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

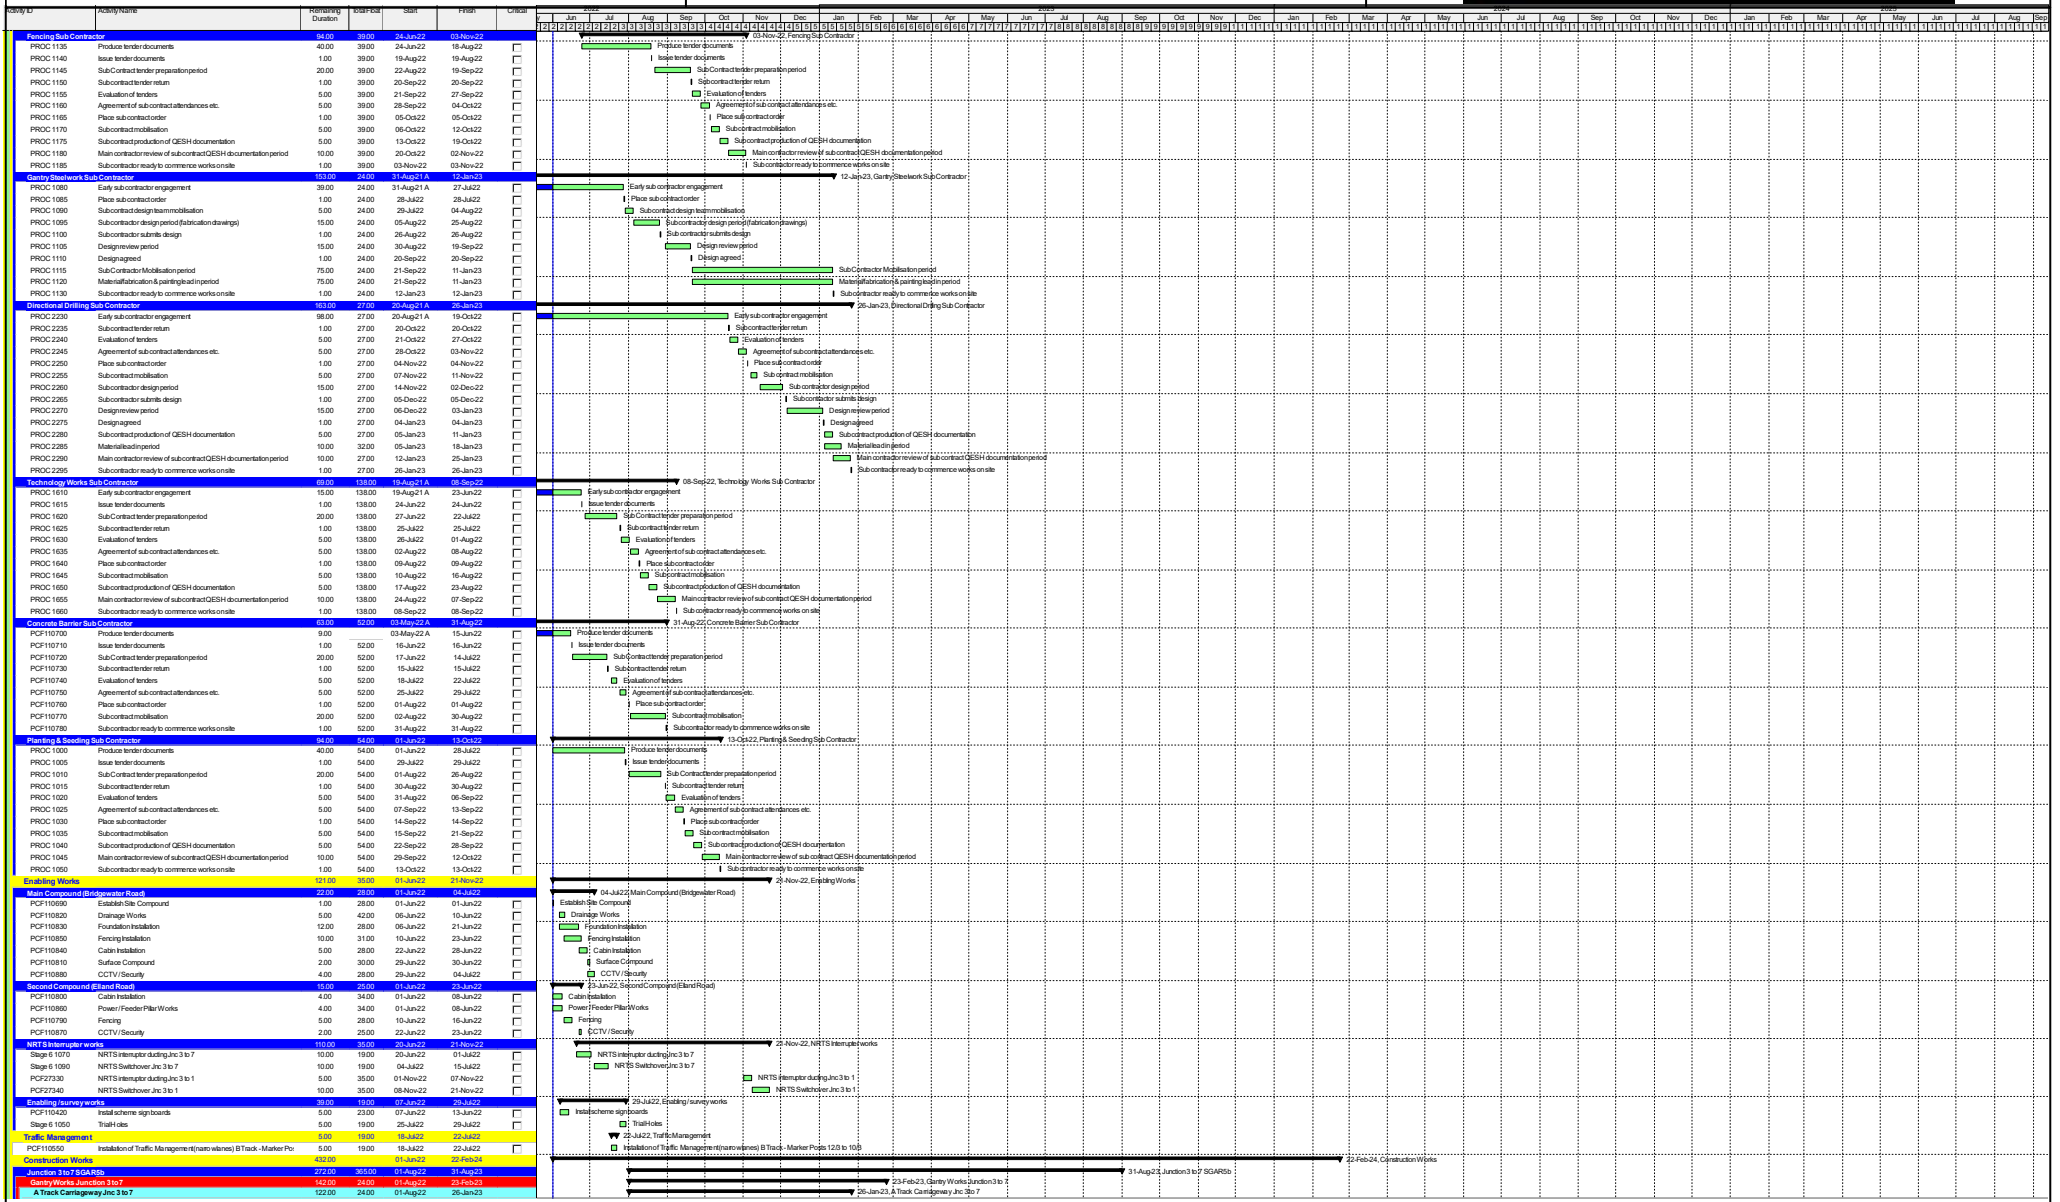


Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CI 32.1 Week 120 LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

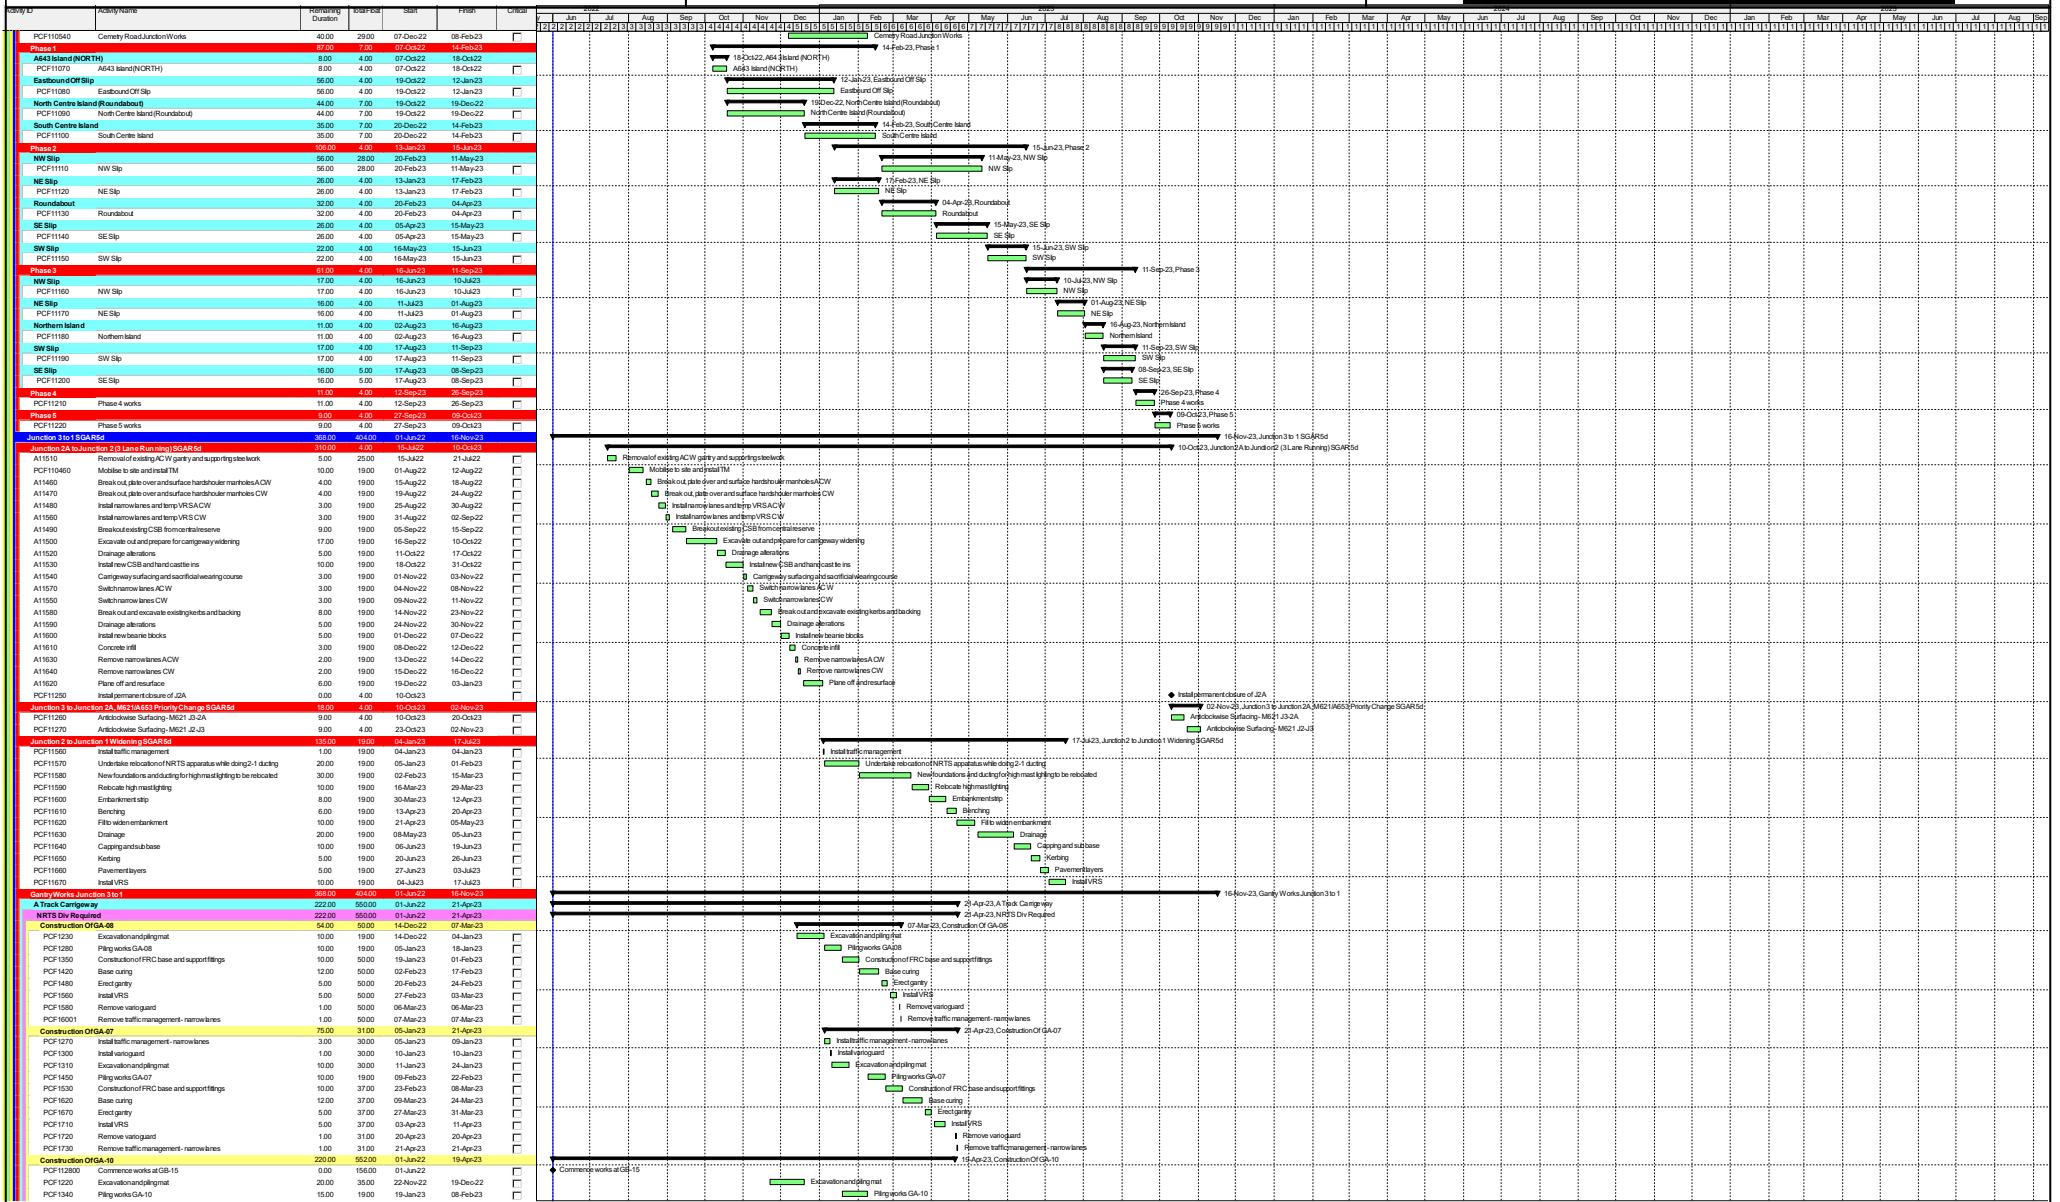


Actual Work Critical Remaining Work
Remaining Work ♦ Milestone

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CL32.1 Week 120
LIVE


M621 Stage 5 CL32.1 Week 120 Live Draft Programme

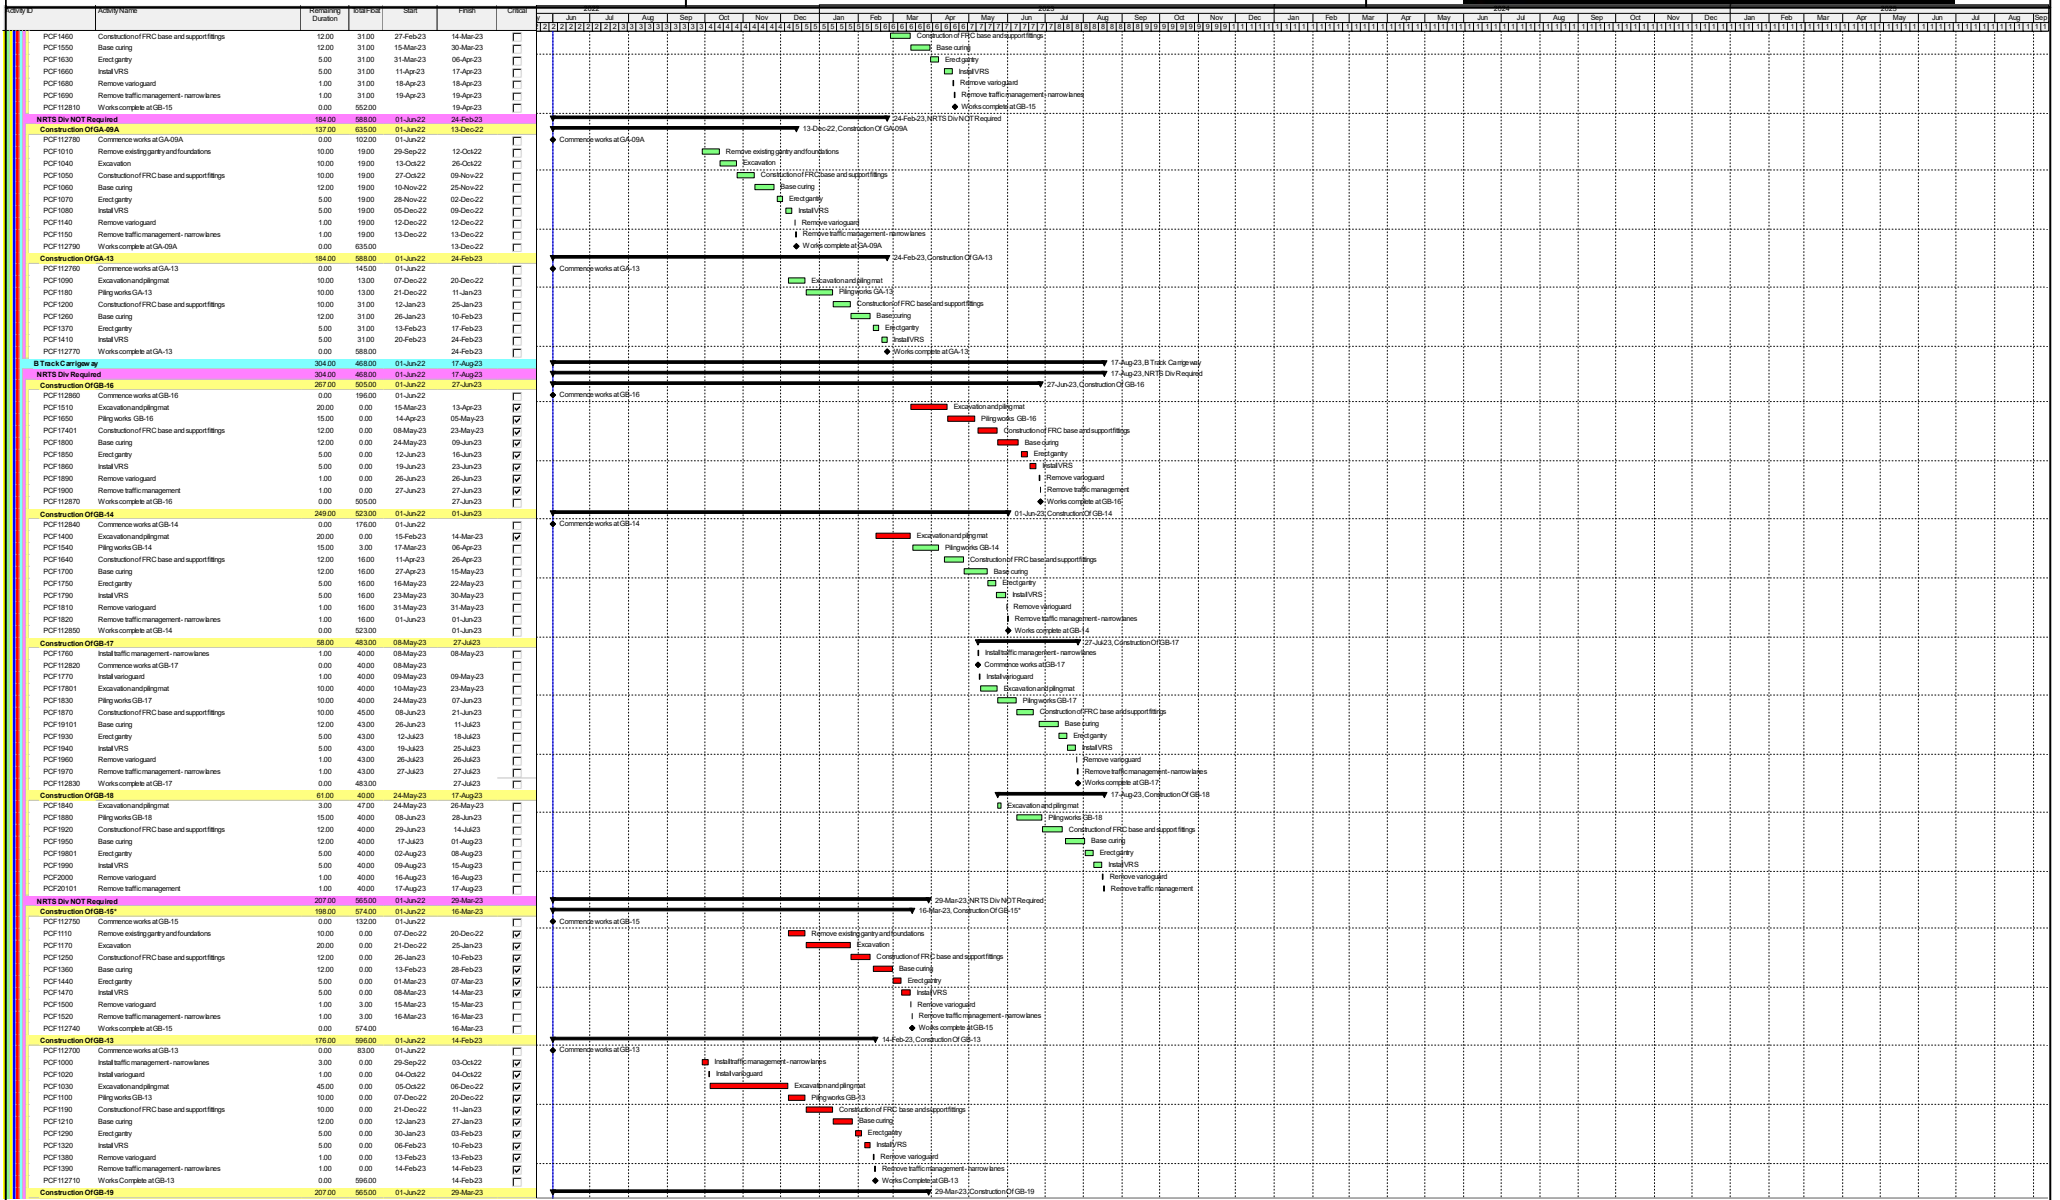

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CI 32.1 Week 120
LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

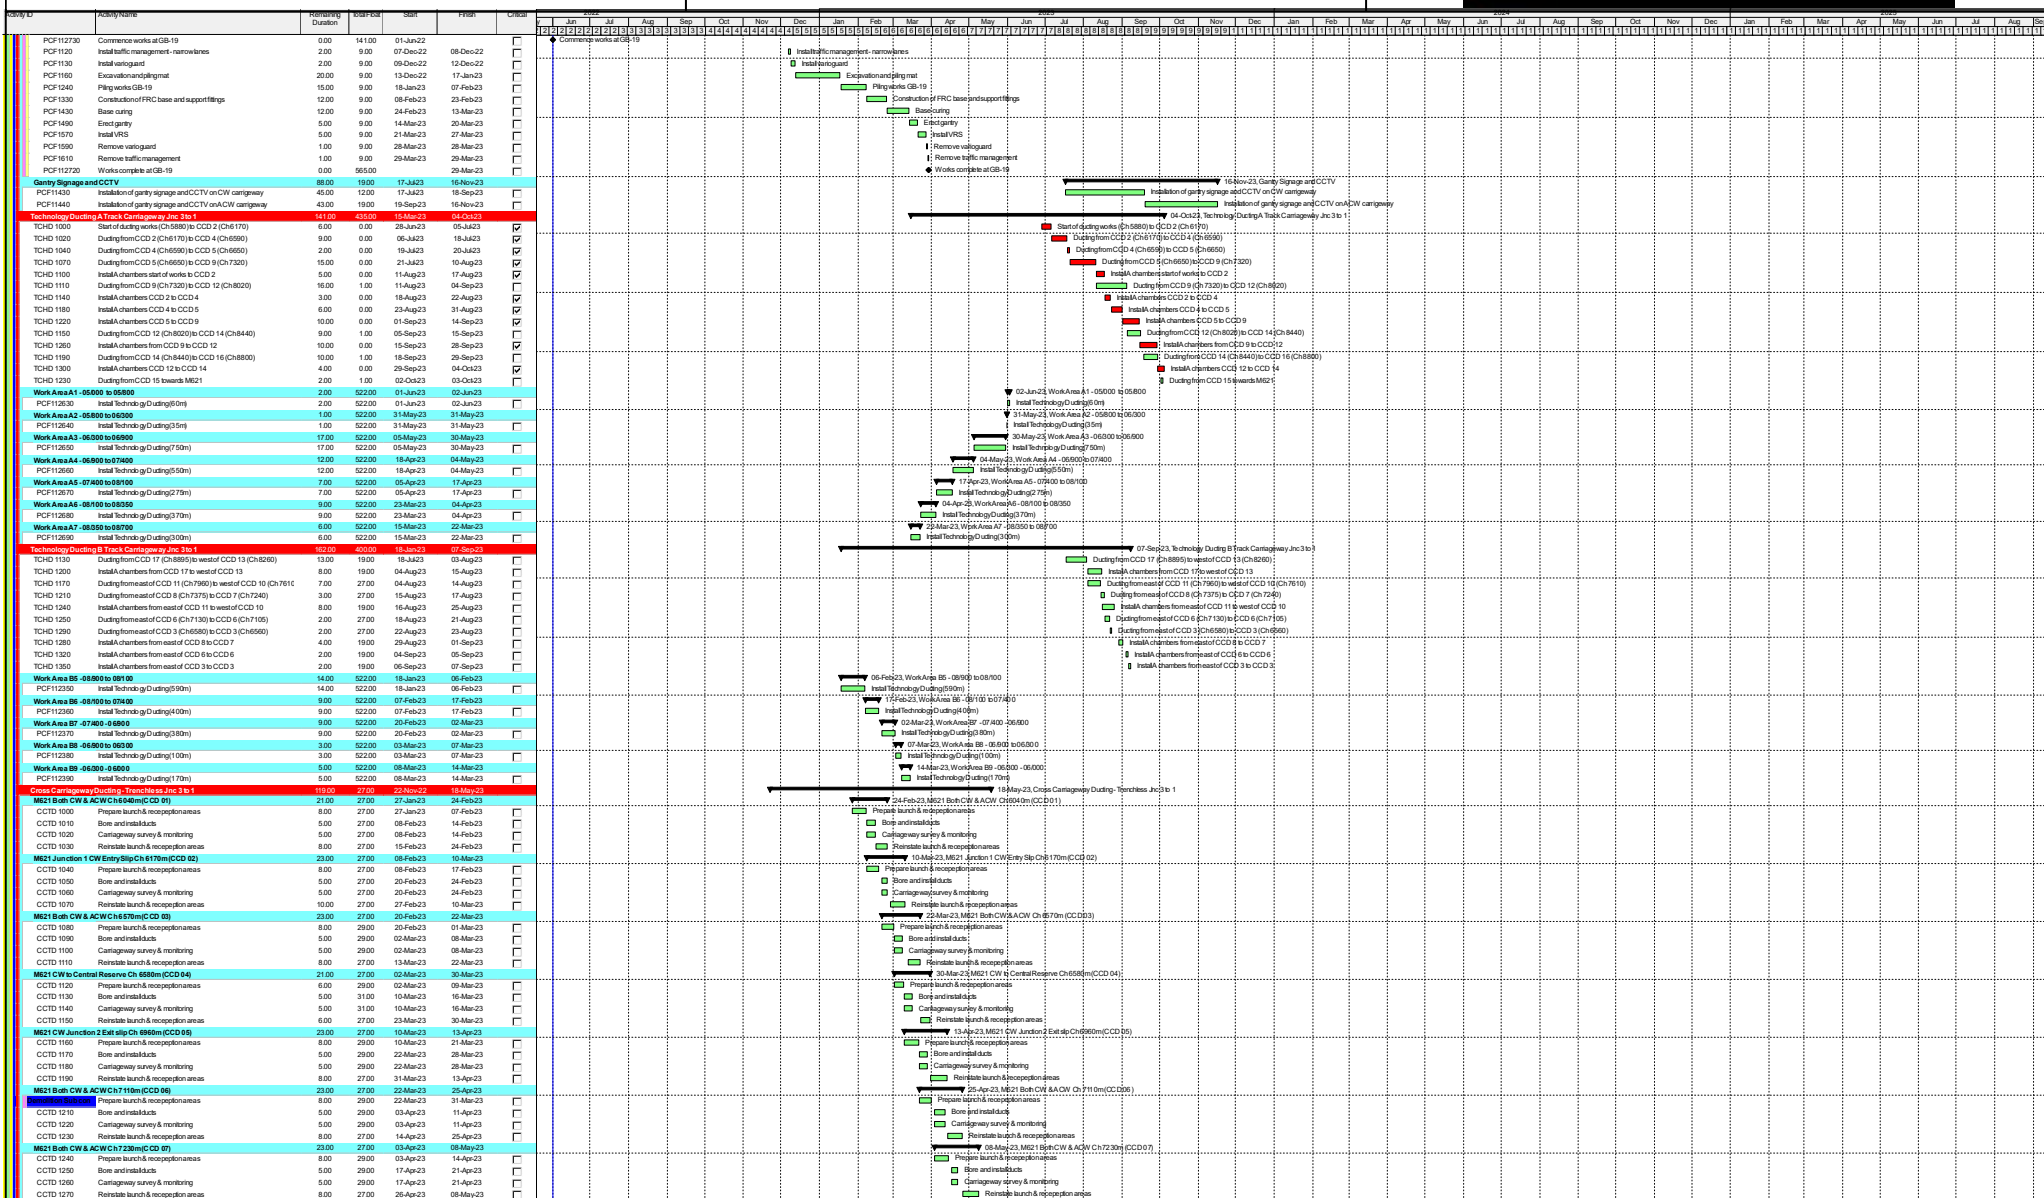


 Actual Work  Critical Remaining Work
 Remaining Work  Milestone

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Junction 1 To 7 Improvements - Stage 5 CI 32.1 Week 120 LIVE

M621 Stage 5 CL32.1 Week 120 Live Draft Programme

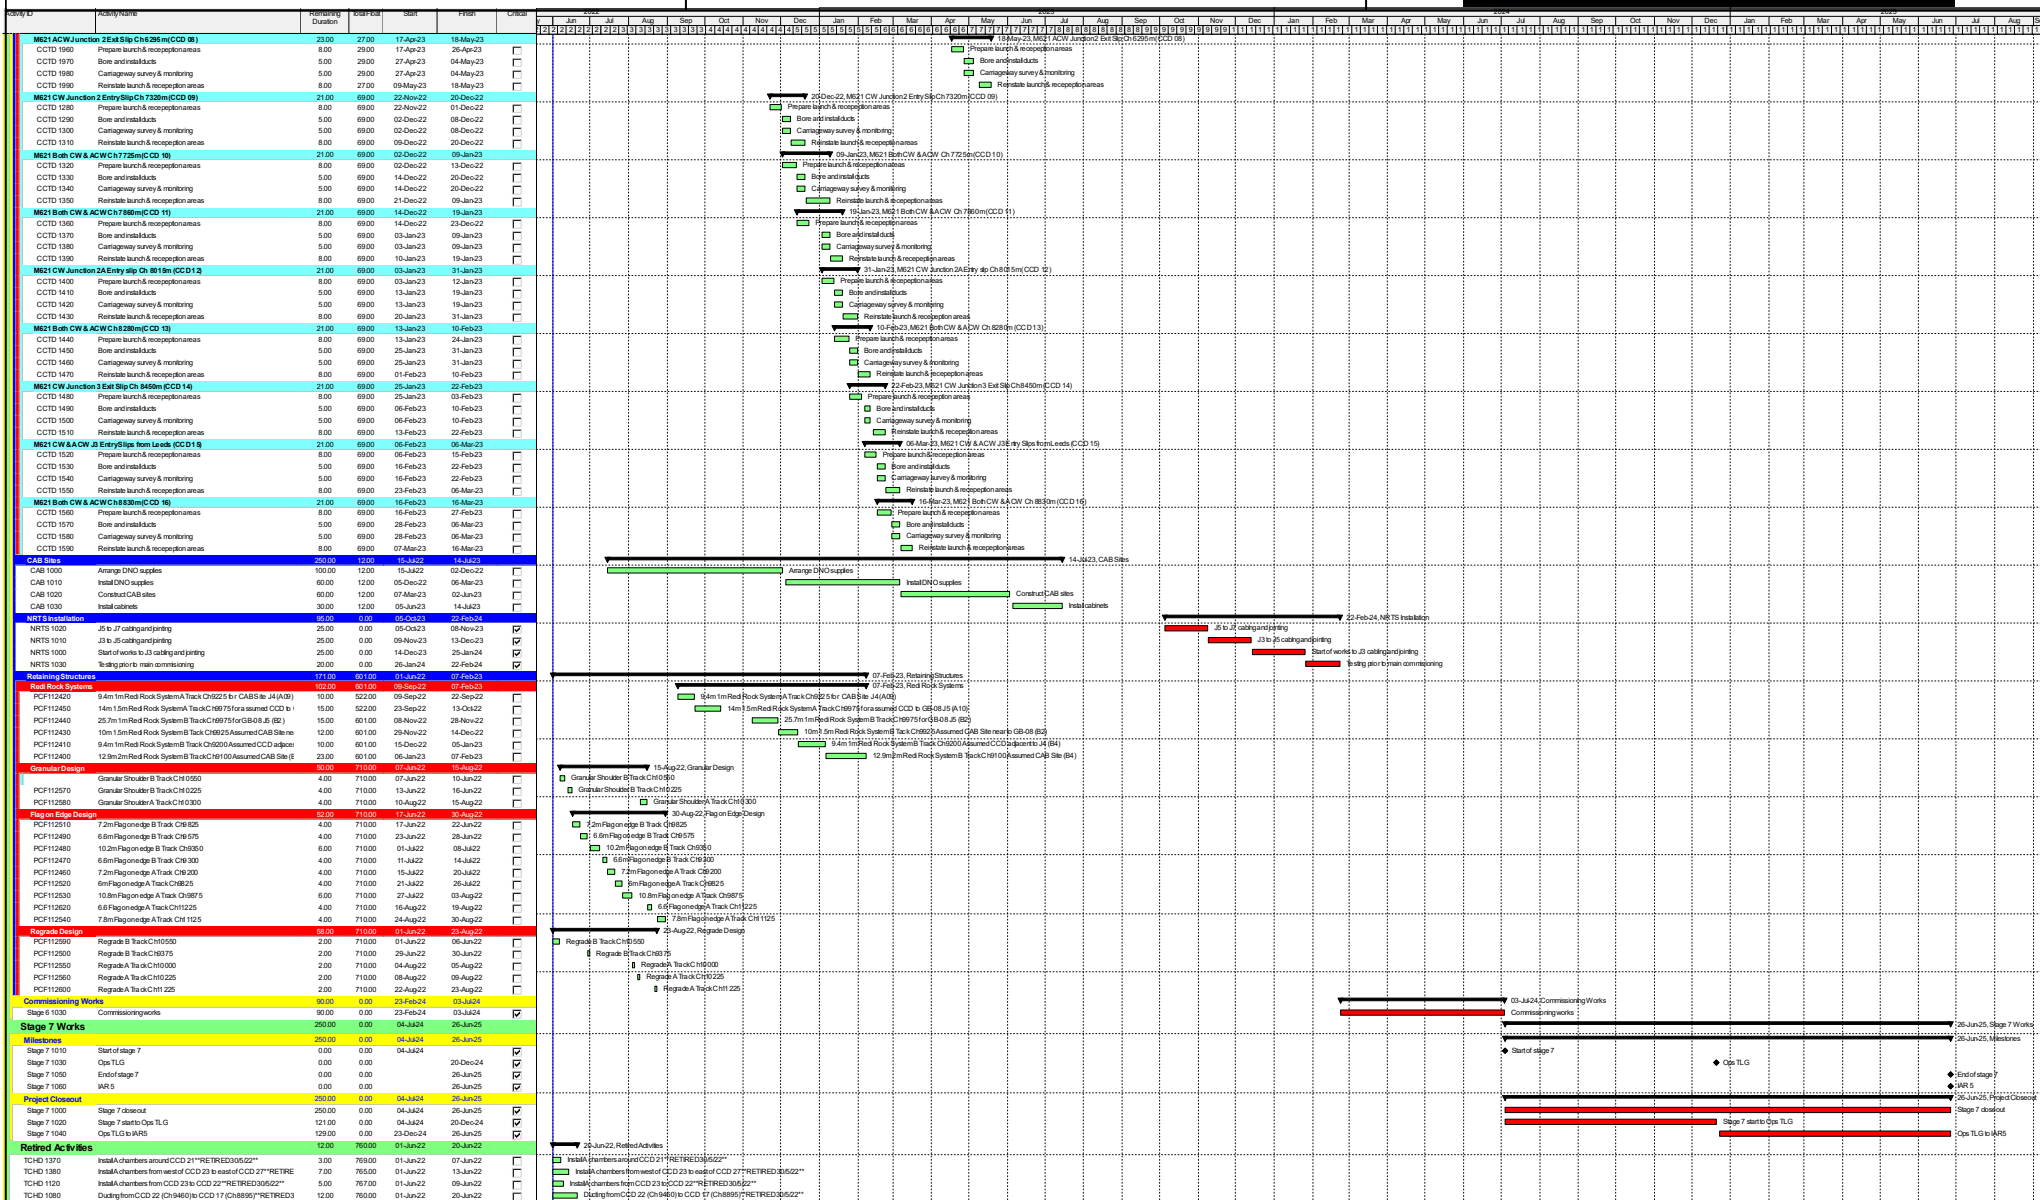

■ Actual Work
 ■ Critical Remaining Work
 ■ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
28-Jan-22	CL32.1 Week 100	PD	JC
25-Feb-22	CL32.1 Week 104	PD	JC

M621 Stage 5 CL32.1 Week 120 Live Draft Programme



Activity ID	Activity Name	Planning Duration	Total Cost	Start	Finish	Critical	2024																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
							Jan												Feb												Mar												Apr												May																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
TCHD 1980	Install chambers from CCD 22 to CCD 17 "RETRED 306522"	12.00	76500	01-Jan-22	20-Jan-22	☐	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2

Actual Work Critical Remaining Work Remaining Work ◆ Milestone	Page 9 of 9	<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>28-Jan-22</td><td>CL32.1 Week 100</td><td>PD</td><td>JC</td></tr><tr><td>25-Feb-22</td><td>CL32.1 Week 104</td><td>PD</td><td>JC</td></tr></table>	Date	Revision	Checked	Approved	28-Jan-22	CL32.1 Week 100	PD	JC	25-Feb-22	CL32.1 Week 104	PD	JC
Date	Revision	Checked	Approved											
28-Jan-22	CL32.1 Week 100	PD	JC											
25-Feb-22	CL32.1 Week 104	PD	JC											
