



CDDFRS
Peterlee Fire Station

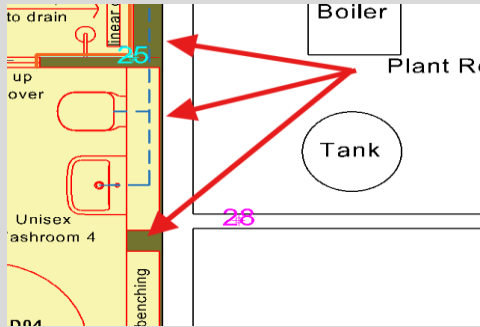
Tender Queries & Addendum Tracker

Tender Date: 26/06/24
Query Deadline: 17/07/24
Tender Return: **25/07/24**

Revision Date: **03/07/24**

The final version of this document will form a part of the contract documentation
The responses take precedence over any information contained within the initial Tender pack

Any reference to the identity of individual contractors within the query text will be hidden

No.	Date	Query	Response/ Addendum
1	26/06/24	<p>Please can you confirm if the areas pointed to below require wall linings:</p> 	Yes, wall linings are required to these areas
2	26/06/24	<p>Can you confirm Altro Aquarius 'Walrus' Vinyl flooring is to be used throughout for all new floor areas including the showers as well as a requirement for coved skirting to all areas throughout</p>	Yes, to all areas hatched yellow on the plan
3	27/06/24	<p>It appears the drawings ask for the same vinyl on the shower room walls as is specified on the floors assuming this is a mistake please can you confirm if an internal wall cladding is to be used instead</p>	The internal wall lining to the showers has been updated to Polyclad Pro PU 'Grey Steel', please find attached updated Proposed Plan rev4.
4	02/07/24	<p>The shower area wall finishing spec is 'Altro Aquarius Walrus' Vinyl; Is this correct or would you like us to price for a wet room wall cladding system, like a Altro Whiterock?</p>	Refer to Query 3 response above.
5	02/07/24	<p>Could you please issue a R&D survey for the building?</p>	With regard asbestos please refer to Section 3.10 of the Pre-Construction H&S Info. Also attached the confirmation letter from DCC.
6	02/07/24	<p>When we looked at DB1 there was no schedule in the board. Could you please issue us with the latest test certificate, so we can determine if there is any spare ways in the board?</p>	Please find attached relevant certificate.
7	02/07/24	<p>Are the floor gulleys in the locker room to remain?</p>	Yes.

8 02/07/24 *Are utility connection required to the temporary Fire Service cabins?*

Yes, temporary power, water, and drainage connections should be provided by the Contractor.

9 02/07/24 *What is the required Fire Rating for the new doors?*

The 5 new internal doors do not form part of the fire compartmentation. Note that the existing doors (eg. D06, D12) are on a fire compartmentation line.
