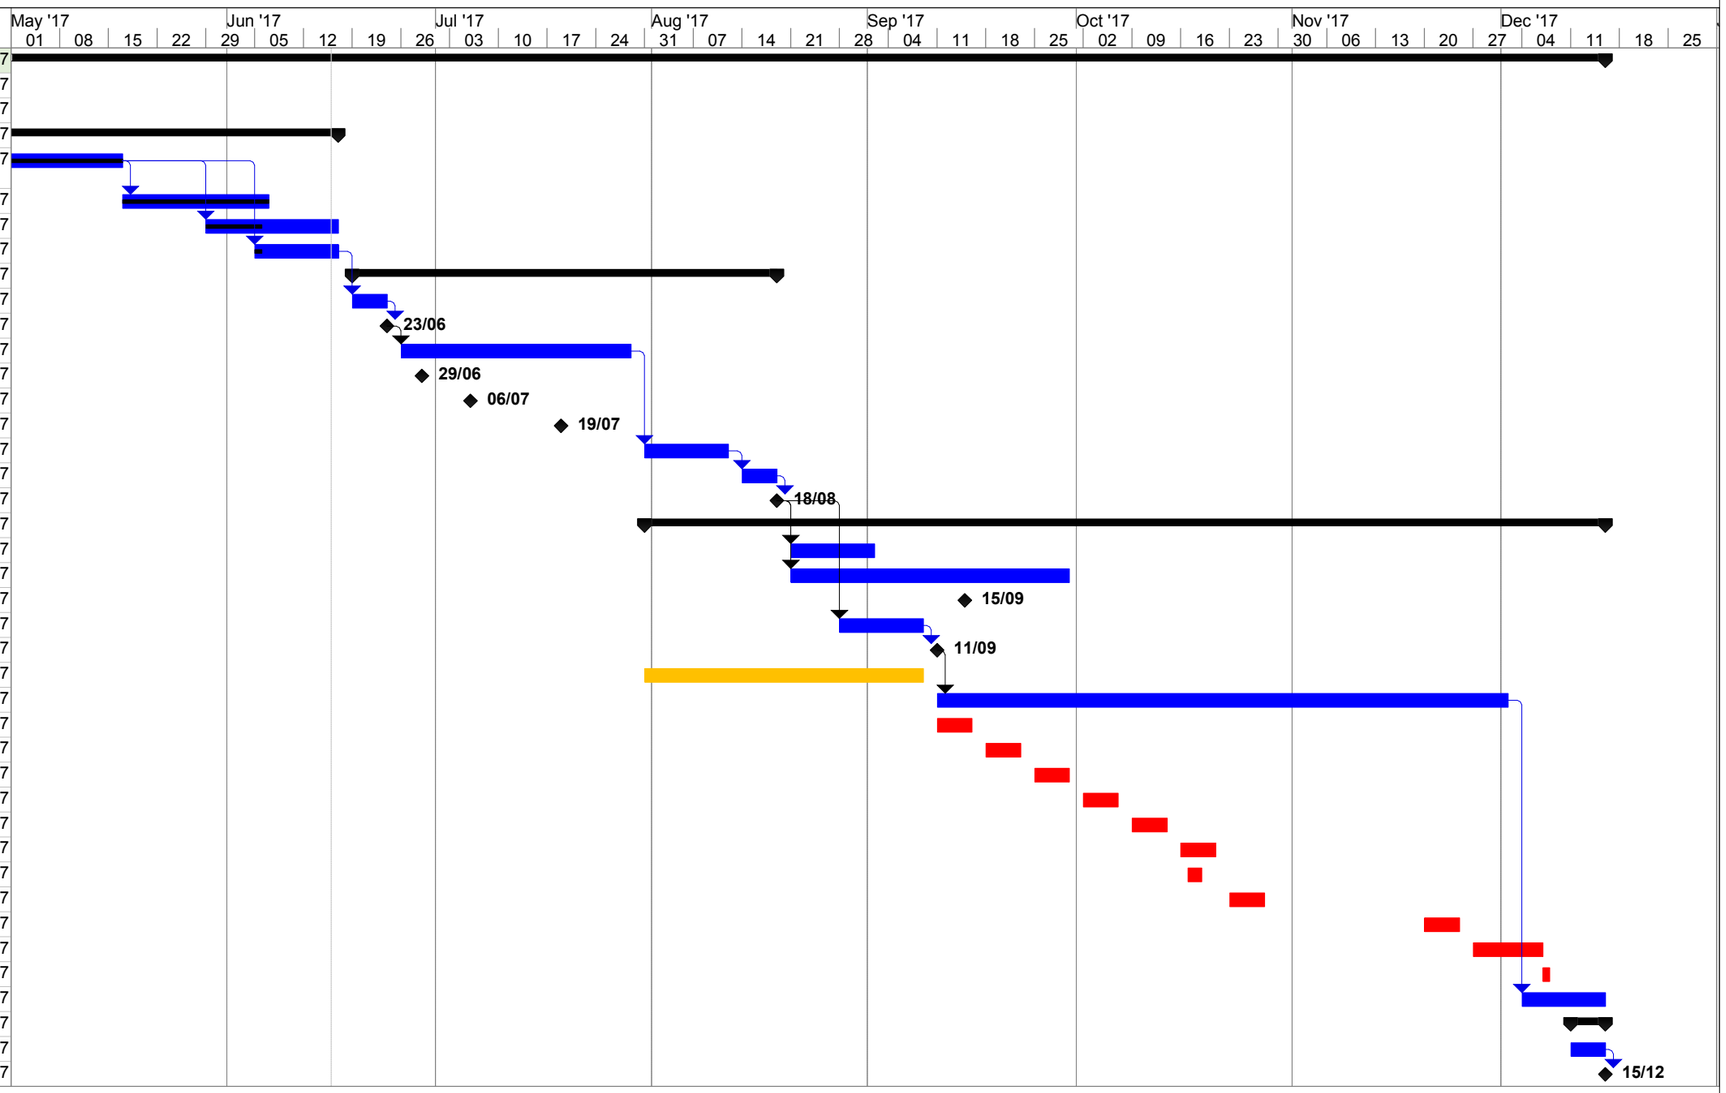ID	Task Name	Duration	Start
1	**Electrical Works**	237 days?	Tue 17/01/17
2	**RIBA Stage 2**	14 days	Tue 17/01/17
6	**RIBA Stage 3**	49 days?	Mon 06/02/17
18	**RIBA Stage 4**	44 days?	Tue 18/04/17
19	Specification for Sump Pumps, LV DB, Control Panels, Emergency Lighting	21 days?	Tue 18/04/17
20	Completion of PCI	3 wks	Wed 17/05/17
21	Preparation of final Pre-tender estimate	3 wks	Mon 29/05/17
22	Preparation of Tender Package	2 wks	Mon 05/06/17
23	**Tender**	45 days	Mon 19/06/17
24	Client Instruction to Proceed following review	1 wk	Mon 19/06/17
25	Issue Tender Documents	0 days	Fri 23/06/17
26	Tender Period	5 wks	Mon 26/06/17
27	Site visit Slot 1 (10am)	0 days	Thu 29/06/17
28	Site visit Slot 2 (10am)	0 days	Thu 06/07/17
29	Final date for tender clarifications	0 days	Wed 19/07/17
30	Tender Analysis	2 wks	Mon 31/07/17
31	Tender Report and recommendation	1 wk	Mon 14/08/17
32	Contract Award and Appointment	0 days	Fri 18/08/17
33	**RIBA Stage 5**	100 days	Mon 31/07/17
34	Preparation of Contract documents	2 wks	Mon 21/08/17
35	Procurement of Equipment	6 wks	Mon 21/08/17
36	Contractor issue contract activity schedule	0 days	Fri 15/09/17
37	Site Mobilisation	2 wks	Mon 28/08/17
38	Start on Site	0 days	Mon 11/09/17
39	IMO Shut Down Period	30 days	Mon 31/07/17
40	Construction Period	12 wks	Mon 11/09/17
41	IMO Event - no services disruption work permitted	1 wk	Mon 11/09/17
42	IMO Event - no services disruption work permitted	1 wk	Mon 18/09/17
43	IMO Event - no services disruption work permitted	1 wk	Mon 25/09/17
44	IMO Event - no services disruption work permitted	1 wk	Mon 02/10/17
45	IMO Event - no services disruption work permitted	1 wk	Mon 09/10/17
46	IMO Event - no services disruption work permitted	1 wk	Mon 16/10/17
47	IMO Event - no services disruption work permitted	2 days	Tue 17/10/17
48	IMO Event - no services disruption work permitted	1 wk	Mon 23/10/17
49	IMO Event - no services disruption work permitted	1 wk	Mon 20/11/17
50	IMO Event - no services disruption work permitted	8 days	Mon 27/11/17
51	IMO Event - no services disruption work permitted	1 day	Thu 07/12/17
52	Testing & Comissioning	2 wks	Mon 04/12/17
53	**RIBA Stage 6**	5 days	Mon 11/12/17
54	Handover	1 wk	Mon 11/12/17
55	Practical Completion	0 days	Fri 15/12/17
