TBAP Bridge Resequenced Programme
Stage 4 Tender
Main Contract
31/08/17

ID	Task Name	Duration	Start	Finish	Predecess
1					
2	**Procurement Strategy**	**82 days**	**Thu 12/01/17**	**Mon 08/05/17**	
10					
11	**TBAP Campus (Bridge Site)**	**732.5 days**	**Fri 18/11/16**	**Tue 10/09/19**	
12	**Informal Public Consultation**	**23 days**	**Fri 18/11/16**	**Tue 20/12/16**	
17	**Planning Process**	**149 days**	**Mon 23/01/17**	**Thu 17/08/17**	
24	**RIBA Stage 3 (formerly D)**	**70 days**	**Mon 16/01/17**	**Fri 21/04/17**	
29	**RIBA Stage 4 (formerly E)**	**100 days**	**Mon 24/04/17**	**Fri 08/09/17**	**28**
30	Stage 4 Design	12 wks	Mon 24/04/17	Fri 14/07/17	
31	Finalise Stage 4 Report	1 wk	Mon 17/07/17	Fri 21/07/17	30
32	RIBA Stage 4 Cost Plan issue	3 wks	Mon 24/07/17	Fri 11/08/17	31
33	Stage 4 Value Engineering Exercise	3 wks	Mon 14/08/17	Fri 01/09/17	32
34	LBHF Approval to proceed to tender issue	1 wk	Mon 04/09/17	Fri 08/09/17	33
35	**Procurement (OJEU Restricted Procedure)**	**156.5 days**	**Mon 31/07/17**	**Tue 06/03/18**	
36	Draft OJEU notice & Tender Document	4 wks	Mon 31/07/17	Fri 25/08/17	
37	Confirmation & Sign Off by Legal & Procurement	2 wks	Mon 28/08/17	Fri 08/09/17	36
38	Upload information to portal & build tender online	0 wks	Fri 08/09/17	Fri 08/09/17	37,9,31
39	Issue of OJEU Notice & Complete Tender Documents	0 wks	Wed 01/11/17	Wed 01/11/17	38
40	**Standard Selection Period**	**30.5 days**	**Wed 01/11/17**	**Wed 13/12/17**	**39**
41	Response Period (30 Calendar Days)	23 days	Wed 01/11/17	Fri 01/12/17	
42	SQ Submitted	0 days	Fri 01/12/17	Fri 01/12/17	41
43	SQ Evaluation	2 days	Mon 04/12/17	Tue 05/12/17	42
44	TAP Meeting	1 day	Fri 08/12/17	Mon 11/12/17	43FS+0.5
45	Tender Report Finalised	1 day	Mon 11/12/17	Tue 12/12/17	44
46	LBHF Agree Tender Shortlist	1 day	Tue 12/12/17	Wed 13/12/17	45
47	Feedback to Unsuccessful Parties	0 days	Wed 13/12/17	Wed 13/12/17	46
48	**Tender Period**	**88.5 days**	**Thu 02/11/17**	**Tue 06/03/18**	
49	Issue of Tender Documents	0 days	Wed 13/12/17	Wed 13/12/17	47
50	Contractor Pricing Period	6 wks	Wed 13/12/17	Wed 24/01/18	49
51	Submission of Contractors Proposals	0 days	Wed 24/01/18	Wed 24/01/18	50
52	Tender Evaluation & Report issued	5 days	Wed 24/01/18	Wed 31/01/18	51
53	LBHF TAP Meeting	1 day	Tue 30/01/18	Wed 31/01/18	52FS-1 d
54	Finalise Tender Recommendation Report	1 day	Wed 31/01/18	Thu 01/02/18	53
55	**Cabinet Process**	**75.5 days**	**Thu 02/11/17**	**Thu 15/02/18**	
56	Business Delivery Team	0 days	Thu 02/11/17	Thu 02/11/17	
57	Report issued for political cabinet	0 wks	Mon 27/11/17	Mon 27/11/17	56FS+3.5
58	Political Cabinet	0 days	Mon 04/12/17	Mon 04/12/17	57FS+1 w
59	Report issued to cabinet	0 days	Thu 01/02/18	Thu 01/02/18	58FS+4 w
60	LBHF Cabinet Approval to award contract	0 wks	Thu 15/02/18	Thu 15/02/18	59FS+2 w
61	EFA Approval to award contract	1.5 wks	Thu 01/02/18	Mon 12/02/18	54
62	LBHF Cabinet OJEU Cooling Off Period (5 calendar days)	5 days	Thu 15/02/18	Thu 22/02/18	60
63	OJEU Cooling Off Period (10 calendar days)	8 days	Thu 22/02/18	Tue 06/03/18	62
64	Contract Award	0 days	Tue 06/03/18	Tue 06/03/18	63
65	**Site Works**	**395 days**	**Tue 06/03/18**	**Tue 10/09/19**	
66	Mobilisation Period	3 wks	Tue 06/03/18	Tue 27/03/18	64
67	**Works**	**380 days**	**Tue 27/03/18**	**Tue 10/09/19**	**66**
68	Section 1a - Free School	33 wks	Tue 27/03/18	Tue 13/11/18	
69	Section 1b - Bridge South Wing	28 wks	Tue 27/03/18	Tue 09/10/18	
70	Section 2 - Greswell Centre	15.6 wks	Tue 20/11/18	Thu 07/03/19	
71	Section 3 - Bridge North Wing	22.7 wks	Thu 04/04/19	Tue 10/09/19	70FS+3 w
72					
73	**Bridge Decant 2017**	**150 days**	**Wed 01/02/17**	**Tue 29/08/17**	
87					
88	**Bridge Window Replacement 2017**	**217 days**	**Thu 12/01/17**	**Fri 10/11/17**	
108					
109	**Latimer Decant 2017**	**177 days**	**Thu 12/01/17**	**Fri 15/09/17**	

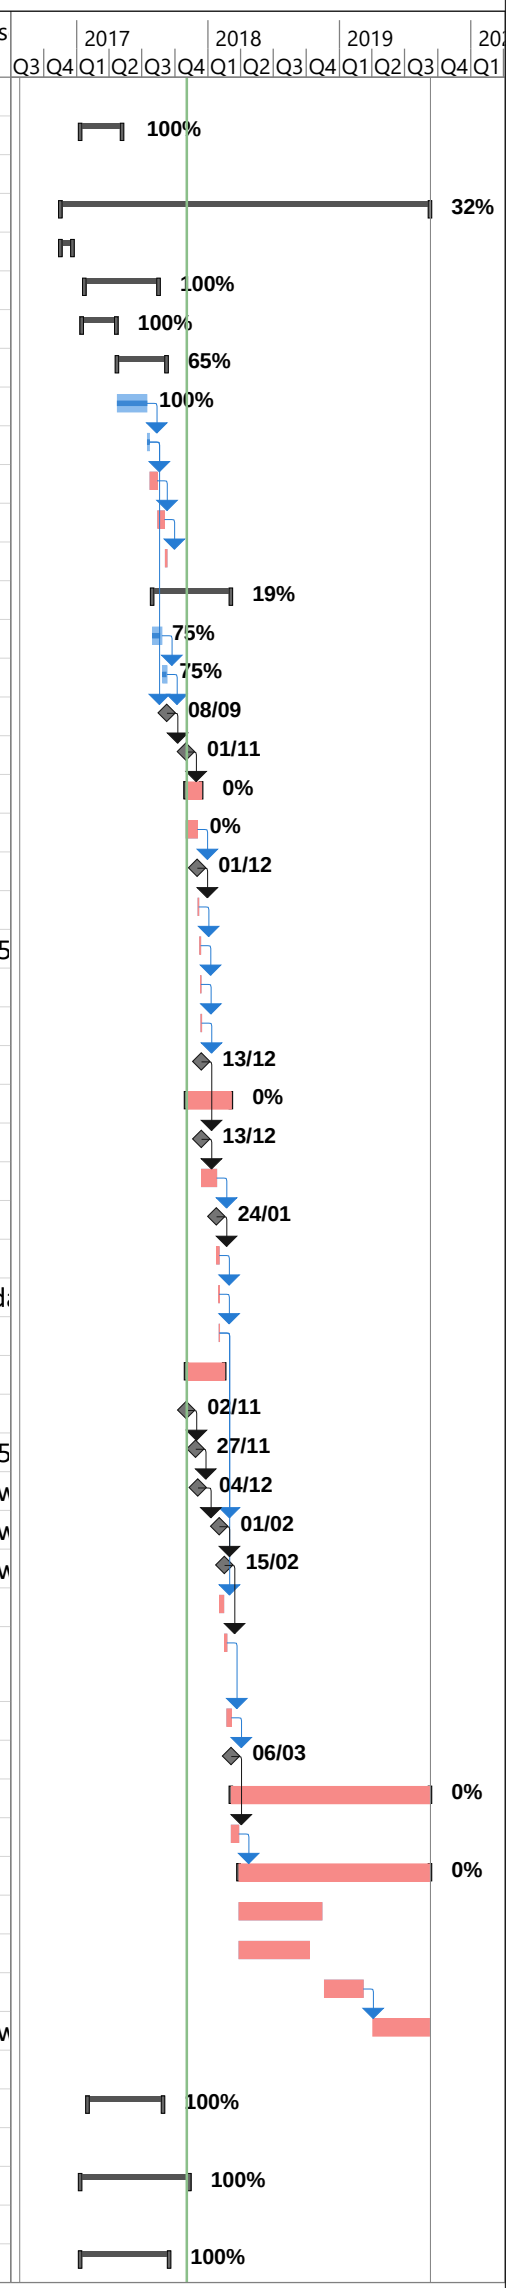

Project: TBAP - MAY Update CW 05.0
Date: Fri 03/11/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress
