Dominions House Refurbishement Project Outline Programme HEFCE
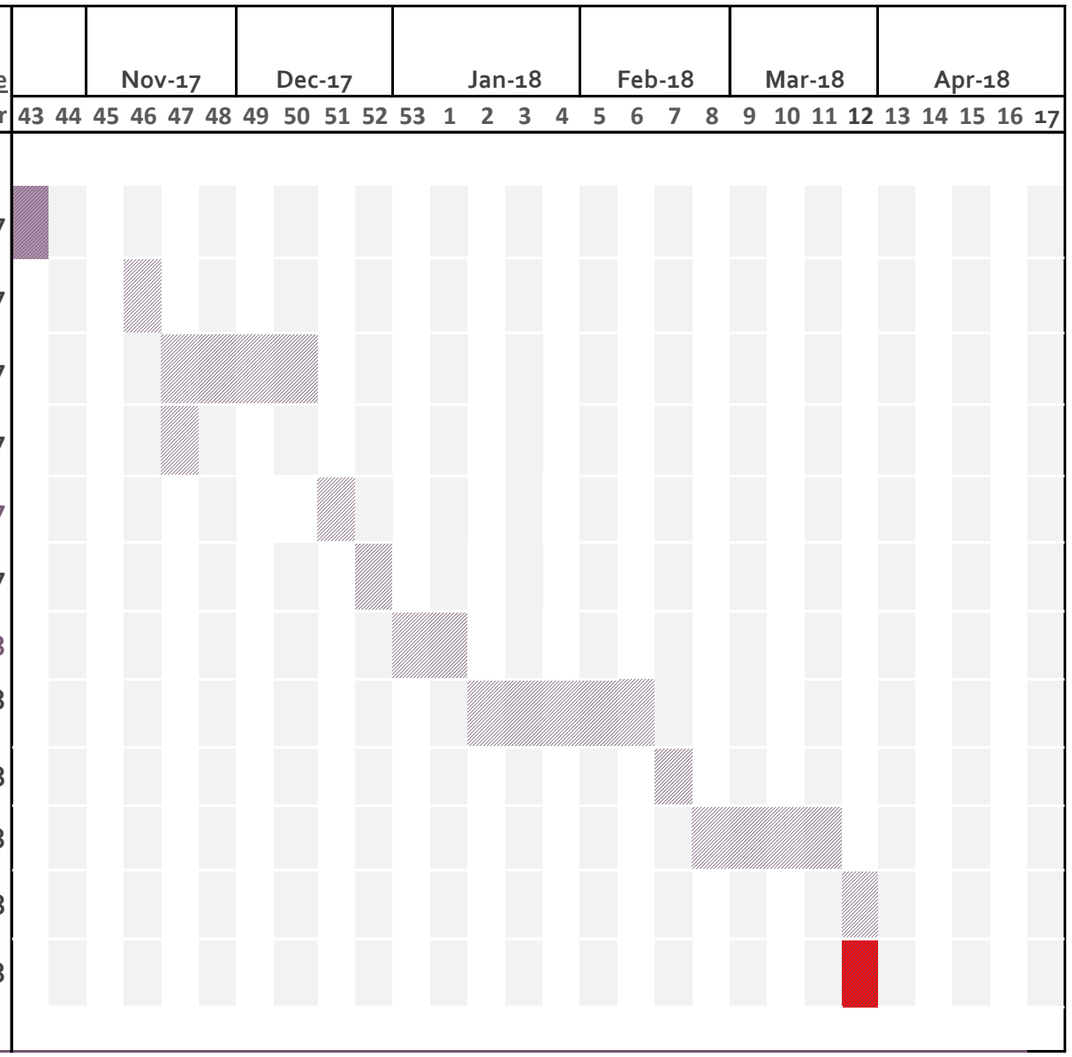
Activity	Target Date
Phase 1 - 1st Floor Occupation w/c 16/10/2017 Temp Staff HEFCE Managed	23/10/2017
ITQ Release	13/11/2017
Tender Period to Submission Date 5 weeks	13/11/17 - 08/12/17
Open Day	17/11/2017
Evauation Period 1 week	11/12/17 - 16/12/17
Contractor Appointment 1 week	wc 18/12/17
Contractor Standstill Period 2 weeks	25/12/17 - 05/01/18
Phase 2 -Re-fit Ground Floor Complete 5 weeks	08/01/18 - 09/02/18
Decant A - Staff Relocation From First floor to ground floor 1 week	wc 19/02/18
Phase 3 - Re-fit 1st Floor 4 weeks	19/02/18 - 16/03/18
Decant B - from West/Hayward into 1st floor Complete 1 week	wc 26/03/18
Completion	Frday 30/03/18
