











































ID		Task Name	Duration	Start	Finish	04 Aug '13							11 Aug '13							18 Aug '13							25 Aug '13							01 Sep '13						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
57		90 Day Milestone - Conduct Lease Review (where applicable)	0 days	Fri 18/10/13	Fri 18/10/13																																			
58		90 Day Milestone - Identify/Agree on purchase of any Transferring Assets	0 days	Wed 02/10/13	Wed 02/10/13																																			
59		90 Day Milestone - Prepare list of Assets	0 days	Tue 01/10/13	Tue 01/10/13																																			
60		60 Day Milestone - Conclude Lease review where applicable	0 days	Fri 18/10/13	Fri 18/10/13																																			
61		60 Day Milestone - Lease signed	0 days	Mon 11/11/13	Mon 11/11/13																																			
62		60 Day Milestone - Update on refurbishments and utilities	0 days	Mon 11/11/13	Mon 11/11/13																																			
63		60 Day Milestone - Draft Initial Snag List	0 days	Mon 11/11/13	Mon 11/11/13																																			
64		30 Day Milestone - Progress report regarding refurbishment and installation of utilities.	0 days	Mon 23/12/13	Mon 23/12/13																																			
65		30 Day Milestone - Refined Snag List, if any Snags exist	0 days	Mon 23/12/13	Mon 23/12/13																																			
66		15 Day Milestone - Facilities finished	0 days	Mon 13/01/14	Mon 13/01/14																																			
67		15 Day Milestone - Provide Safety Certificate as required by local law	0 days	Mon 13/01/14	Mon 13/01/14																																			
68		15 Day Milestone - Insurance in place	0 days	Mon 13/01/14	Mon 13/01/14																																			
69		15 Day Milestone - Utilities working	0 days	Mon 13/01/14	Mon 13/01/14																																			
70		15 Day Milestone - Finalise list of Assets	0 days	Mon 13/01/14	Mon 13/01/14																																			
71		15 Day Milestone - Agree categories of listed Assets	0 days	Mon 13/01/14	Mon 13/01/14																																			
72		15 Day Milestone - Finalised Snag List, if any Snags exist, with RAG Status	0 days	Mon 13/01/14	Mon 13/01/14																																			
73		Business Continuation Plan	50 days	Mon 04/11/13	Mon 13/01/14																																			
74		Post to provide local Business Continuation Plans if not already provided before and where available	5 days	Mon 04/11/13	Mon 11/11/13																																			
75		Draft Business Continuation Plan for VAC, incorporating Post Business Continuation Plans	5 days	Mon 16/12/13	Mon 23/12/13																																			
76		Finalised and signed off as appropriate	1 day	Fri 10/01/14	Mon 13/01/14																																			
77		60 Day Milestone - Post to provide local Business Continuation Plans	0 days	Mon 11/11/13	Mon 11/11/13																																			
78		30 Day Milestone - Draft Business Continuation Plan for VAC	0 days	Mon 23/12/13	Mon 23/12/13																																			
79		15 Day Milestone - Finalised and signed off as appropriate	0 days	Mon 13/01/14	Mon 13/01/14																															</				

ID		Task Name	Duration	Start	Finish	04 Aug '13							11 Aug '13							18 Aug '13							25 Aug '13							01 Sep '13						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
113		30 Day Milestone - Staff appointed and vetted	0 days	Mon 23/12/13	Mon 23/12/13																																			
114		30 Day Milestone - Update on training plans	0 days	Mon 23/12/13	Mon 23/12/13																																			
115		30 Day Milestone - Localisation of operational procedures agreed	0 days	Mon 23/12/13	Mon 23/12/13																																			
116		30 Day Milestone - Confirmation of agreed joint training with Post	0 days	Mon 23/12/13	Mon 23/12/13																																			
117		15 Day Milestone - Progress of on-going training	0 days	Wed 22/01/14	Wed 22/01/14																																			
118		Hardware	80 days	Mon 30/09/13	Fri 17/01/14																																			
119		Identify potential vendors	1 day	Mon 30/09/13	Mon 30/09/13																																			
120		Identifying local office need of hardware with specifications	2 days	Mon 30/09/13	Tue 01/10/13																																			
121		Plan to fulfil office requirements	1 day	Fri 08/11/13	Mon 11/11/13																																			
122		Appointment of vendor	1 day	Fri 08/11/13	Mon 11/11/13																																			
123		Connectivity cost finalization & vendor	15 days	Mon 21/10/13	Mon 11/11/13																																			
124		Lead time for delivery of hardware	25 days	Mon 11/11/13	Fri 13/12/13																																			
125		Installation of Hardware	5 days	Mon 16/12/13	Fri 20/12/13																																			
126		Order for Telecom connections (Connectivity and Telephone)	10 days	Mon 23/12/13	Fri 03/01/14																																			
127		Installation of telecom connectivity	3 days	Mon 06/01/14	Wed 08/01/14																																			
128		Integration of hardware and telecom equipments	3 days	Thu 09/01/14	Mon 13/01/14																																			
129		Hardware user acceptance test	4 days	Tue 14/01/14	Fri 17/01/14																																			
130		90 Day Milestone - Potential Vendors identified	0 days	Mon 30/09/13	Mon 30/09/13																																			
131		90 Day Milestone - Identify local office needs	0 days	Tue 01/10/13	Tue 01/10/13																																			
132		60 Day Milestone - Plan to fulfil office requirements	0 days	Mon 11/11/13	Mon 11/11/13																																			
133		30 Day Milestone - Update on progress against hardware plans	0 days	Fri 20/12/13	Fri 20/12/13																																			
134		15 Day Milestone - Plan completed	0 days	Fri 17/01/14	Fri 17/01/14																																			
135		Visa4UK Application Testing	13 days	Wed 25/12/13	Mon 13/01/14																																			
136		Implementation of Visa4UK Application at VAC	3 days	Tue 31/12/13	Fri 03/01/14																																			
137		User Acceptance Testing	5 days	Wed 25/12/13	Wed 01/01/14																																			
138		Dry Run and Gap fulfillment in software	3 days	Wed 08/01/14	Mon 13/01/14																																			
139		15 Day Milestone - Plan completed	0 days	Mon 13/01/14	Mon 13/01/14																																			
140		Website Development	47 days	Thu 07/11/13	Mon 13/01/14																																			
141		Domain registration for website	2 days	Thu 07/11/13	Mon 11/11/13																																			
142		Website Content Finalization - English	5 days	Mon 11/11/13	Fri 15/11/13																																			
143		Website Development	25 days	Mon 18/11/13	Fri 20/12/13																																			
144		Link Payment gateway to the website	2 days	Mon 23/12/13	Tue 24/12/13																																			
145		Website testing and hosting	2 days	Wed 25/12/13	Thu 26/12/13																																			
146		Website Dry Run	2 days	Fri 27/12/13	Mon 30/12/13																																			
147		Final sign off from UK visa for Website	5 days	Mon 06/01/14	Mon 13/01/14																																			
148		15 Day Milestone - Completion of Website and implementation	0 days	Mon 13/01/14	Mon 13/01/14																																			
149		Security	75 days	Mon 30/09/13	Mon 13/01/14																																			
150		Provide PSA1	3 days	Mon 30/09/13	Wed 02/10/13																																			
151		Identifying security vendor/consultant	10 days	Mon 30/09/13	Fri 11/10/13																																			
152		Finalization of security vendor/ consultant	5 days	Mon 30/09/13	Fri 04/10/13																																			
153		Finalization of security equipment vendor	5 days	Mon 30/09/13	Fri 04/10/13																																			
154		Provide PSA2	3 days	Mon 21/10/13	Wed 23/10/13																																			
155		Provide PSA3	3 days	Wed 06/11/13	Mon 11/11/13																																			
156		Finalization of CCTVs/Access Controls/scanners/Panic alarms/fire alarms	7 days	Thu 31/10/13	Mon 11/11/13																																			
157		Installation of Security Hardware	5 days	Mon 16/12/13	Mon 23/12/13																																			
158		Training of Security staff on the process note given by Consultant	4 days	Tue 17/12/13	Mon 23/12/13																																			
159		Provide PSA4	10 days	Mon 30/12/13	Mon 13/01/14																																			
160		Provide ISO27001 compliance details	5 days	Mon 06/01/14	Mon 13/01/14																																			
161		Provide IT Security Health-Check Report	1 day	Fri 10/01/14	Mon 13/01/14																																			
162		Provide sample Biometric CCTV footage	2 days	Thu 09/01/14	Mon 13/01/14																																			
163		90 Day Milestone - Provide PSA1 (Condensed 120 day milestone)	0 days	Wed 02/10/13	Wed 02/10/13																																			
164		75 Day Milestone - Provide PSA2 (Condensed 90 day milestone)	0 days	Wed 23/10/13	Wed 23/10/13																																			
165		60 Day Milestone - Provide PSA3	0 days	Mon 11/11/13	Mon 11/11/13																																			
166		15 Day Milestone - Provide PSA4	0 days	Mon 13/01/14	Mon 13/01/14																																			
167		15 Day Milestone - Provide ISO27001 compliance details	0 days	Mon 13/01/14	Mon 13/01/14																																			
168		15 Day Milestone - Provide IT Security Health-Check Report	0 days	Mon 13/01/14	Mon 13/01/14																																			


Project: Sample GANTT Chart Date: Tue 30/04/13	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	04 Aug '13							11 Aug '13							18 Aug '13							25 Aug '13							01 Sep '13						
					S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
169	<div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div><div></div></div>																																						

Project: Sample GANTT Chart

Date: Tue 30/04/13

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

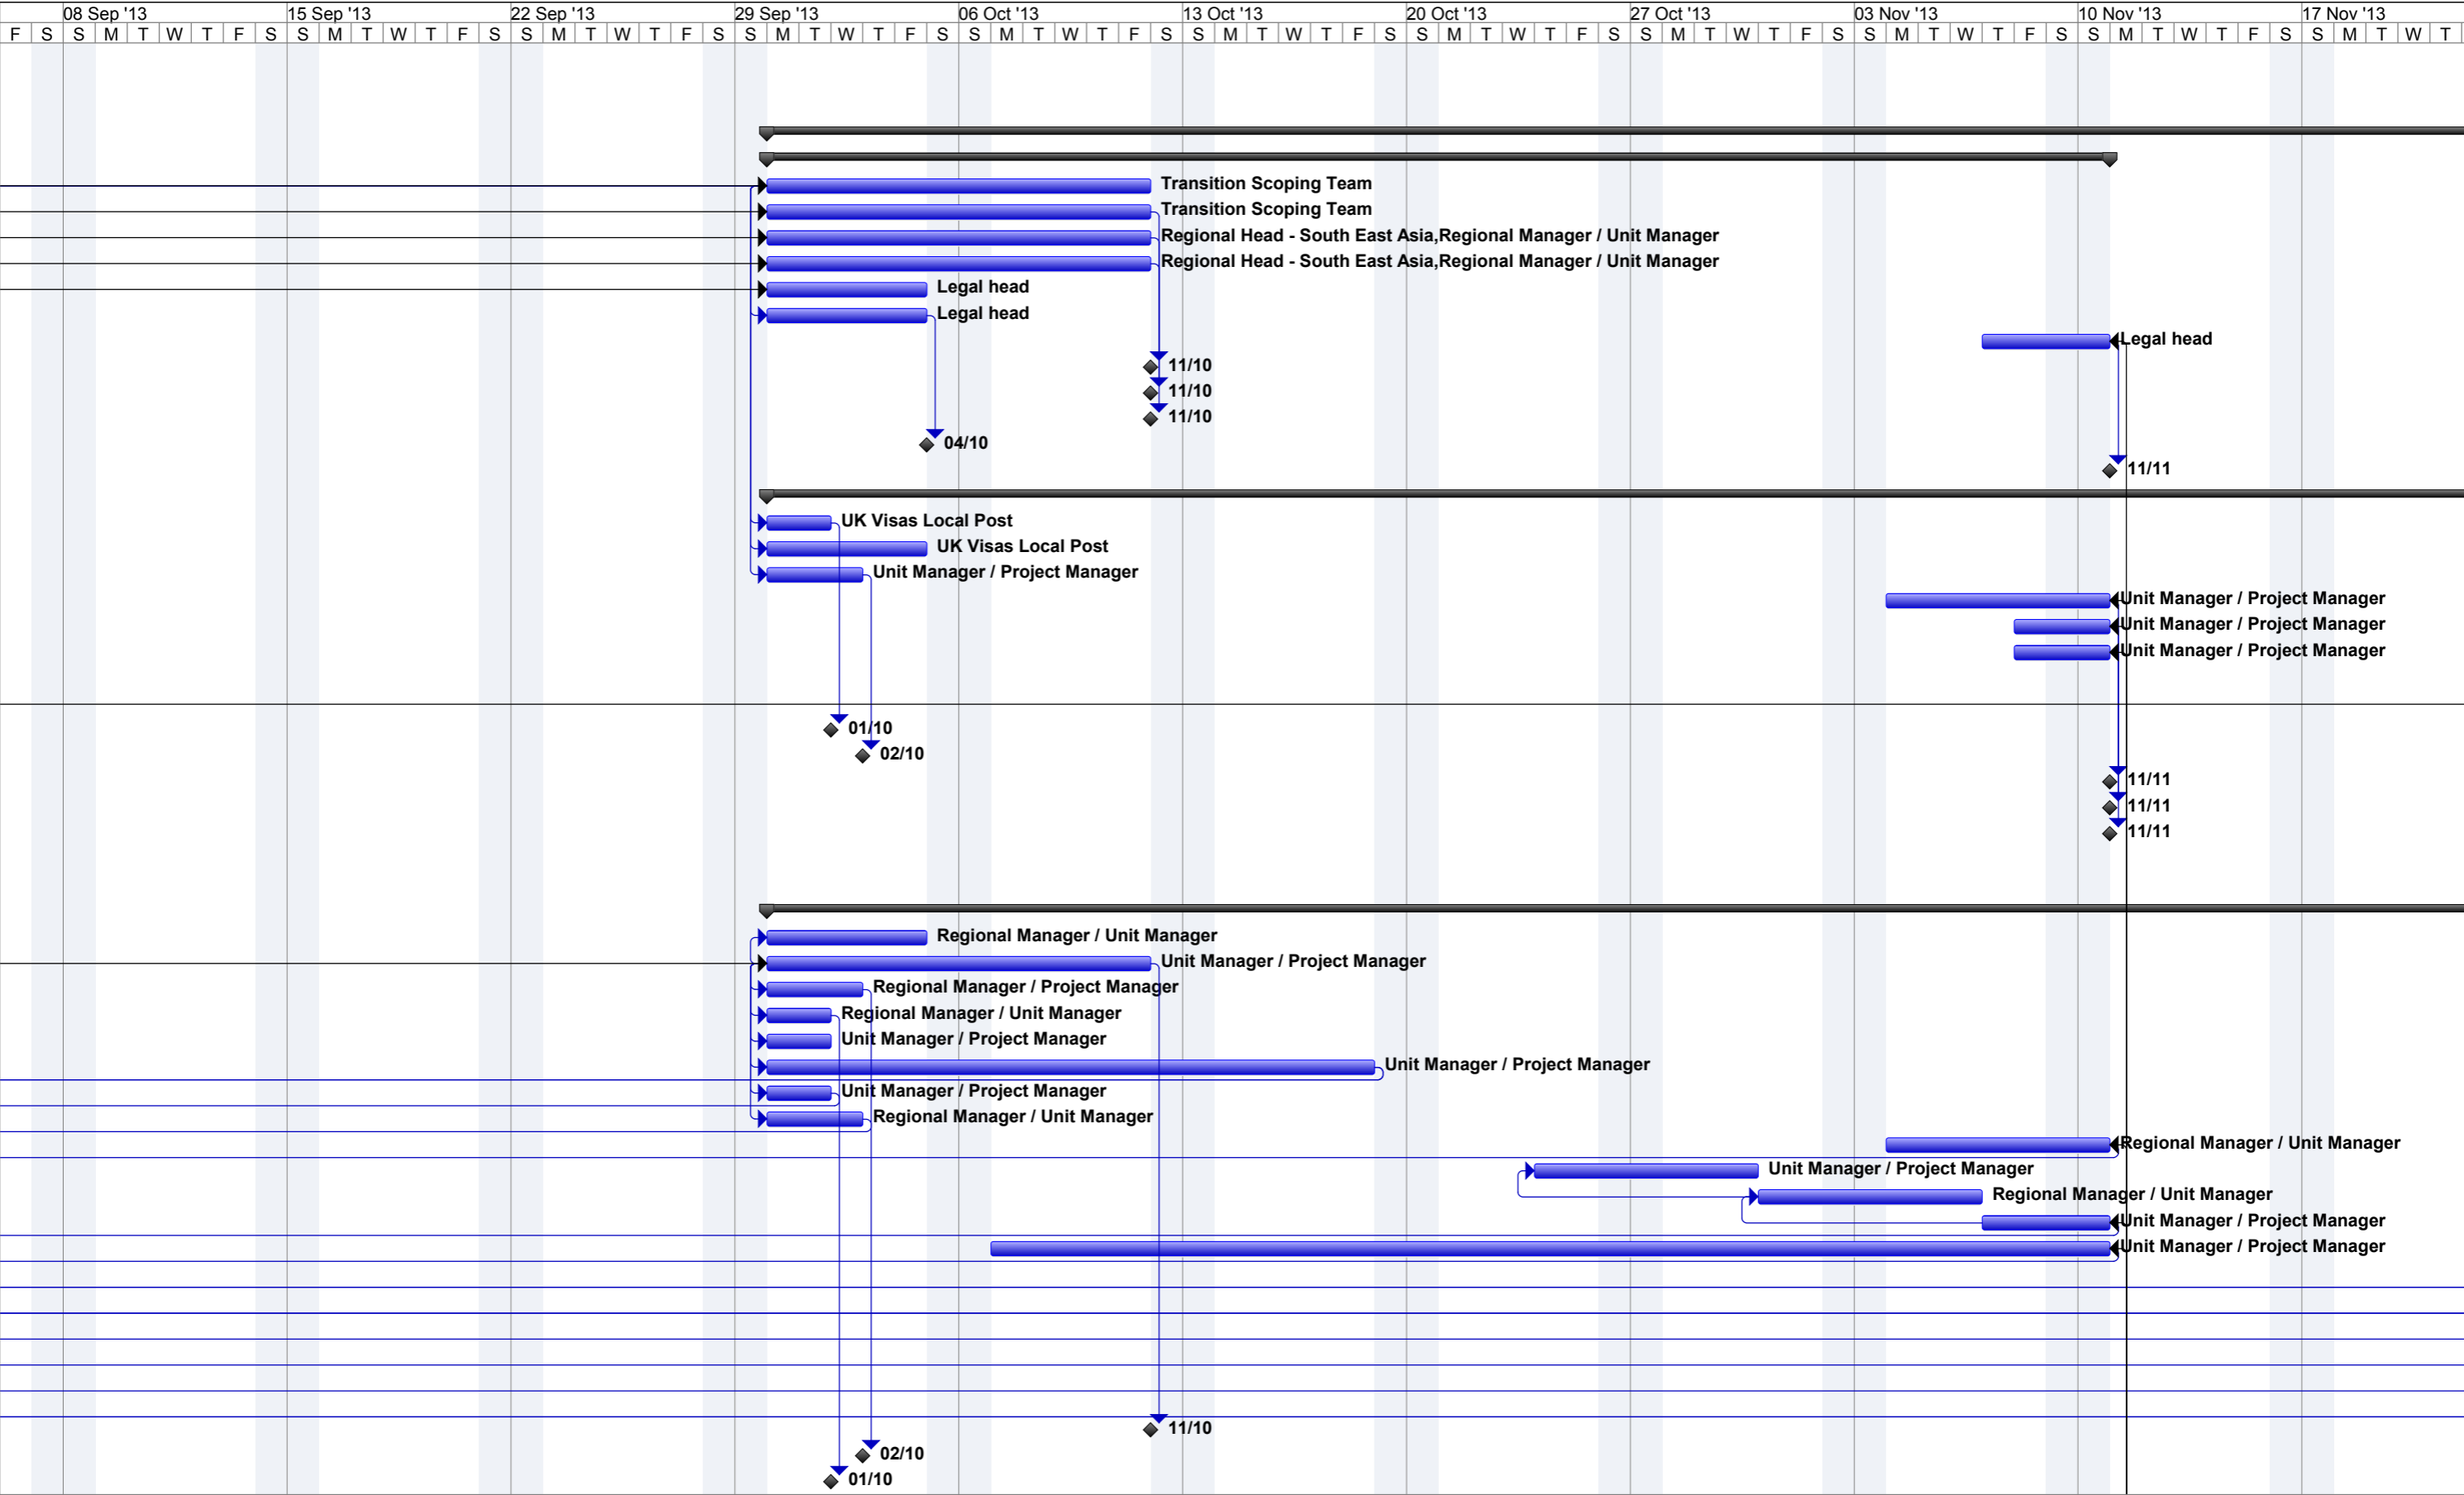

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary









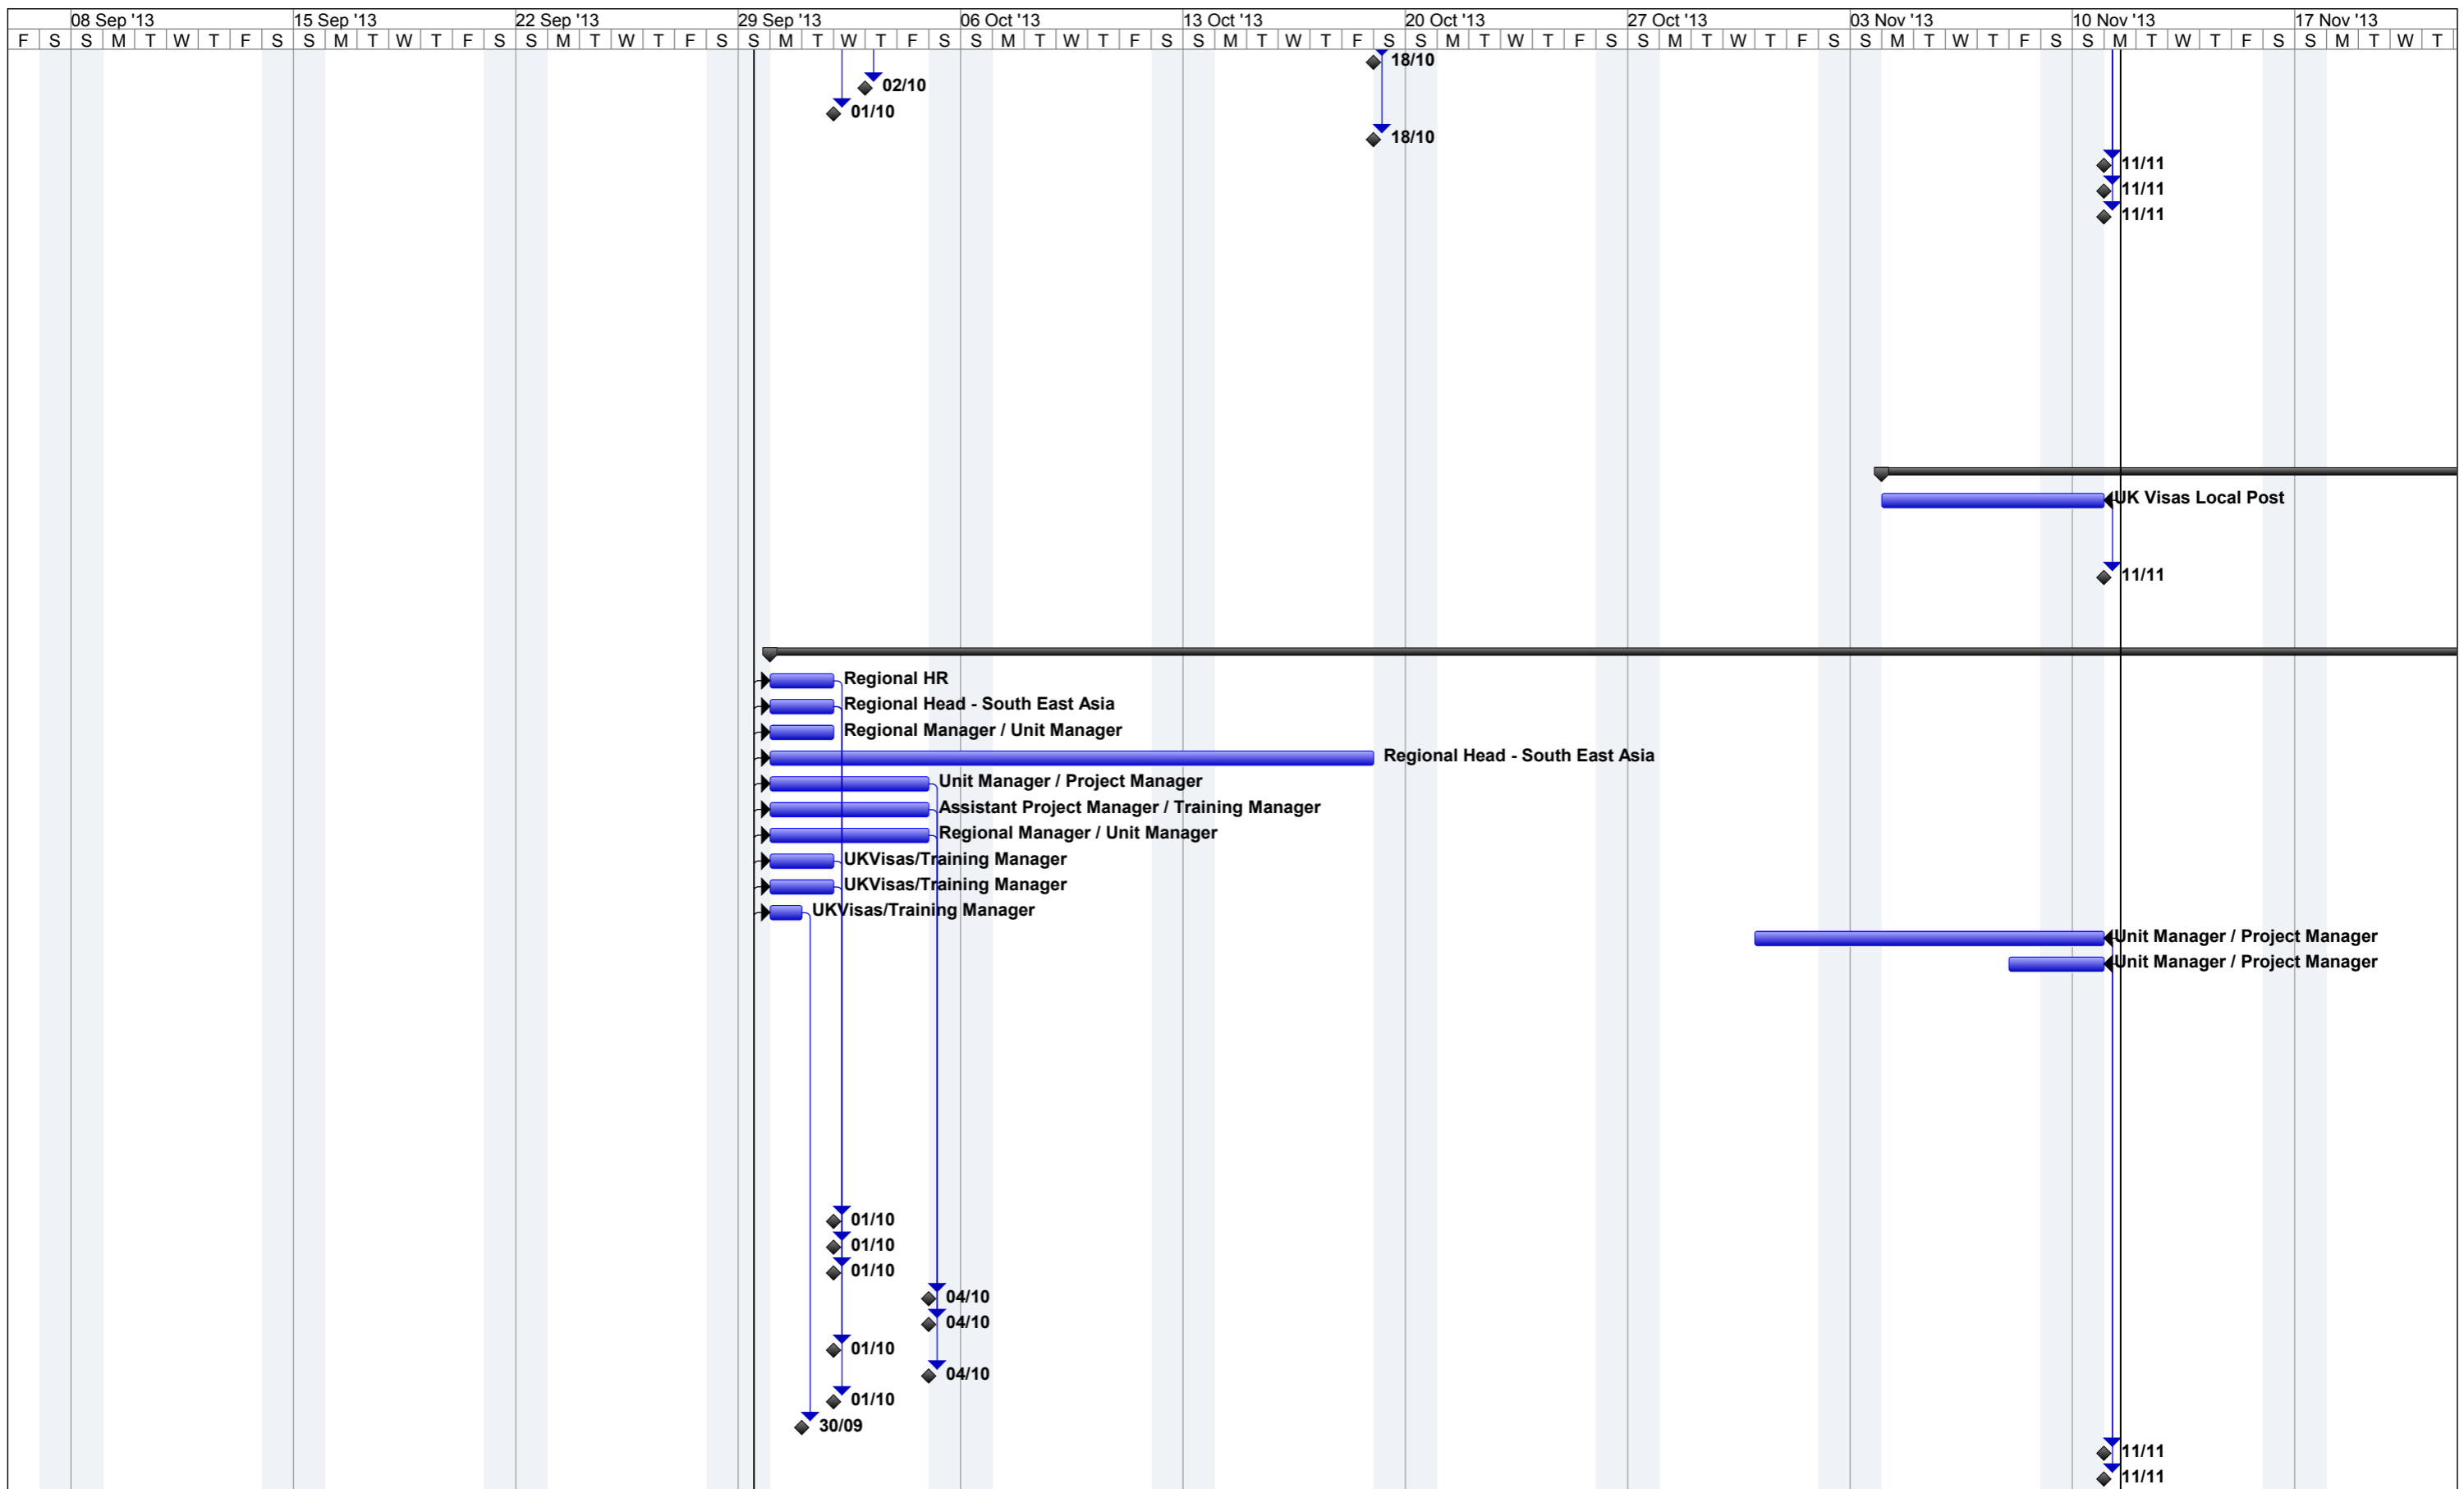









Start-only


Finish-only

Progress

Deadline



Project: Sample GANTT Chart Date: Tue 30/04/13	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

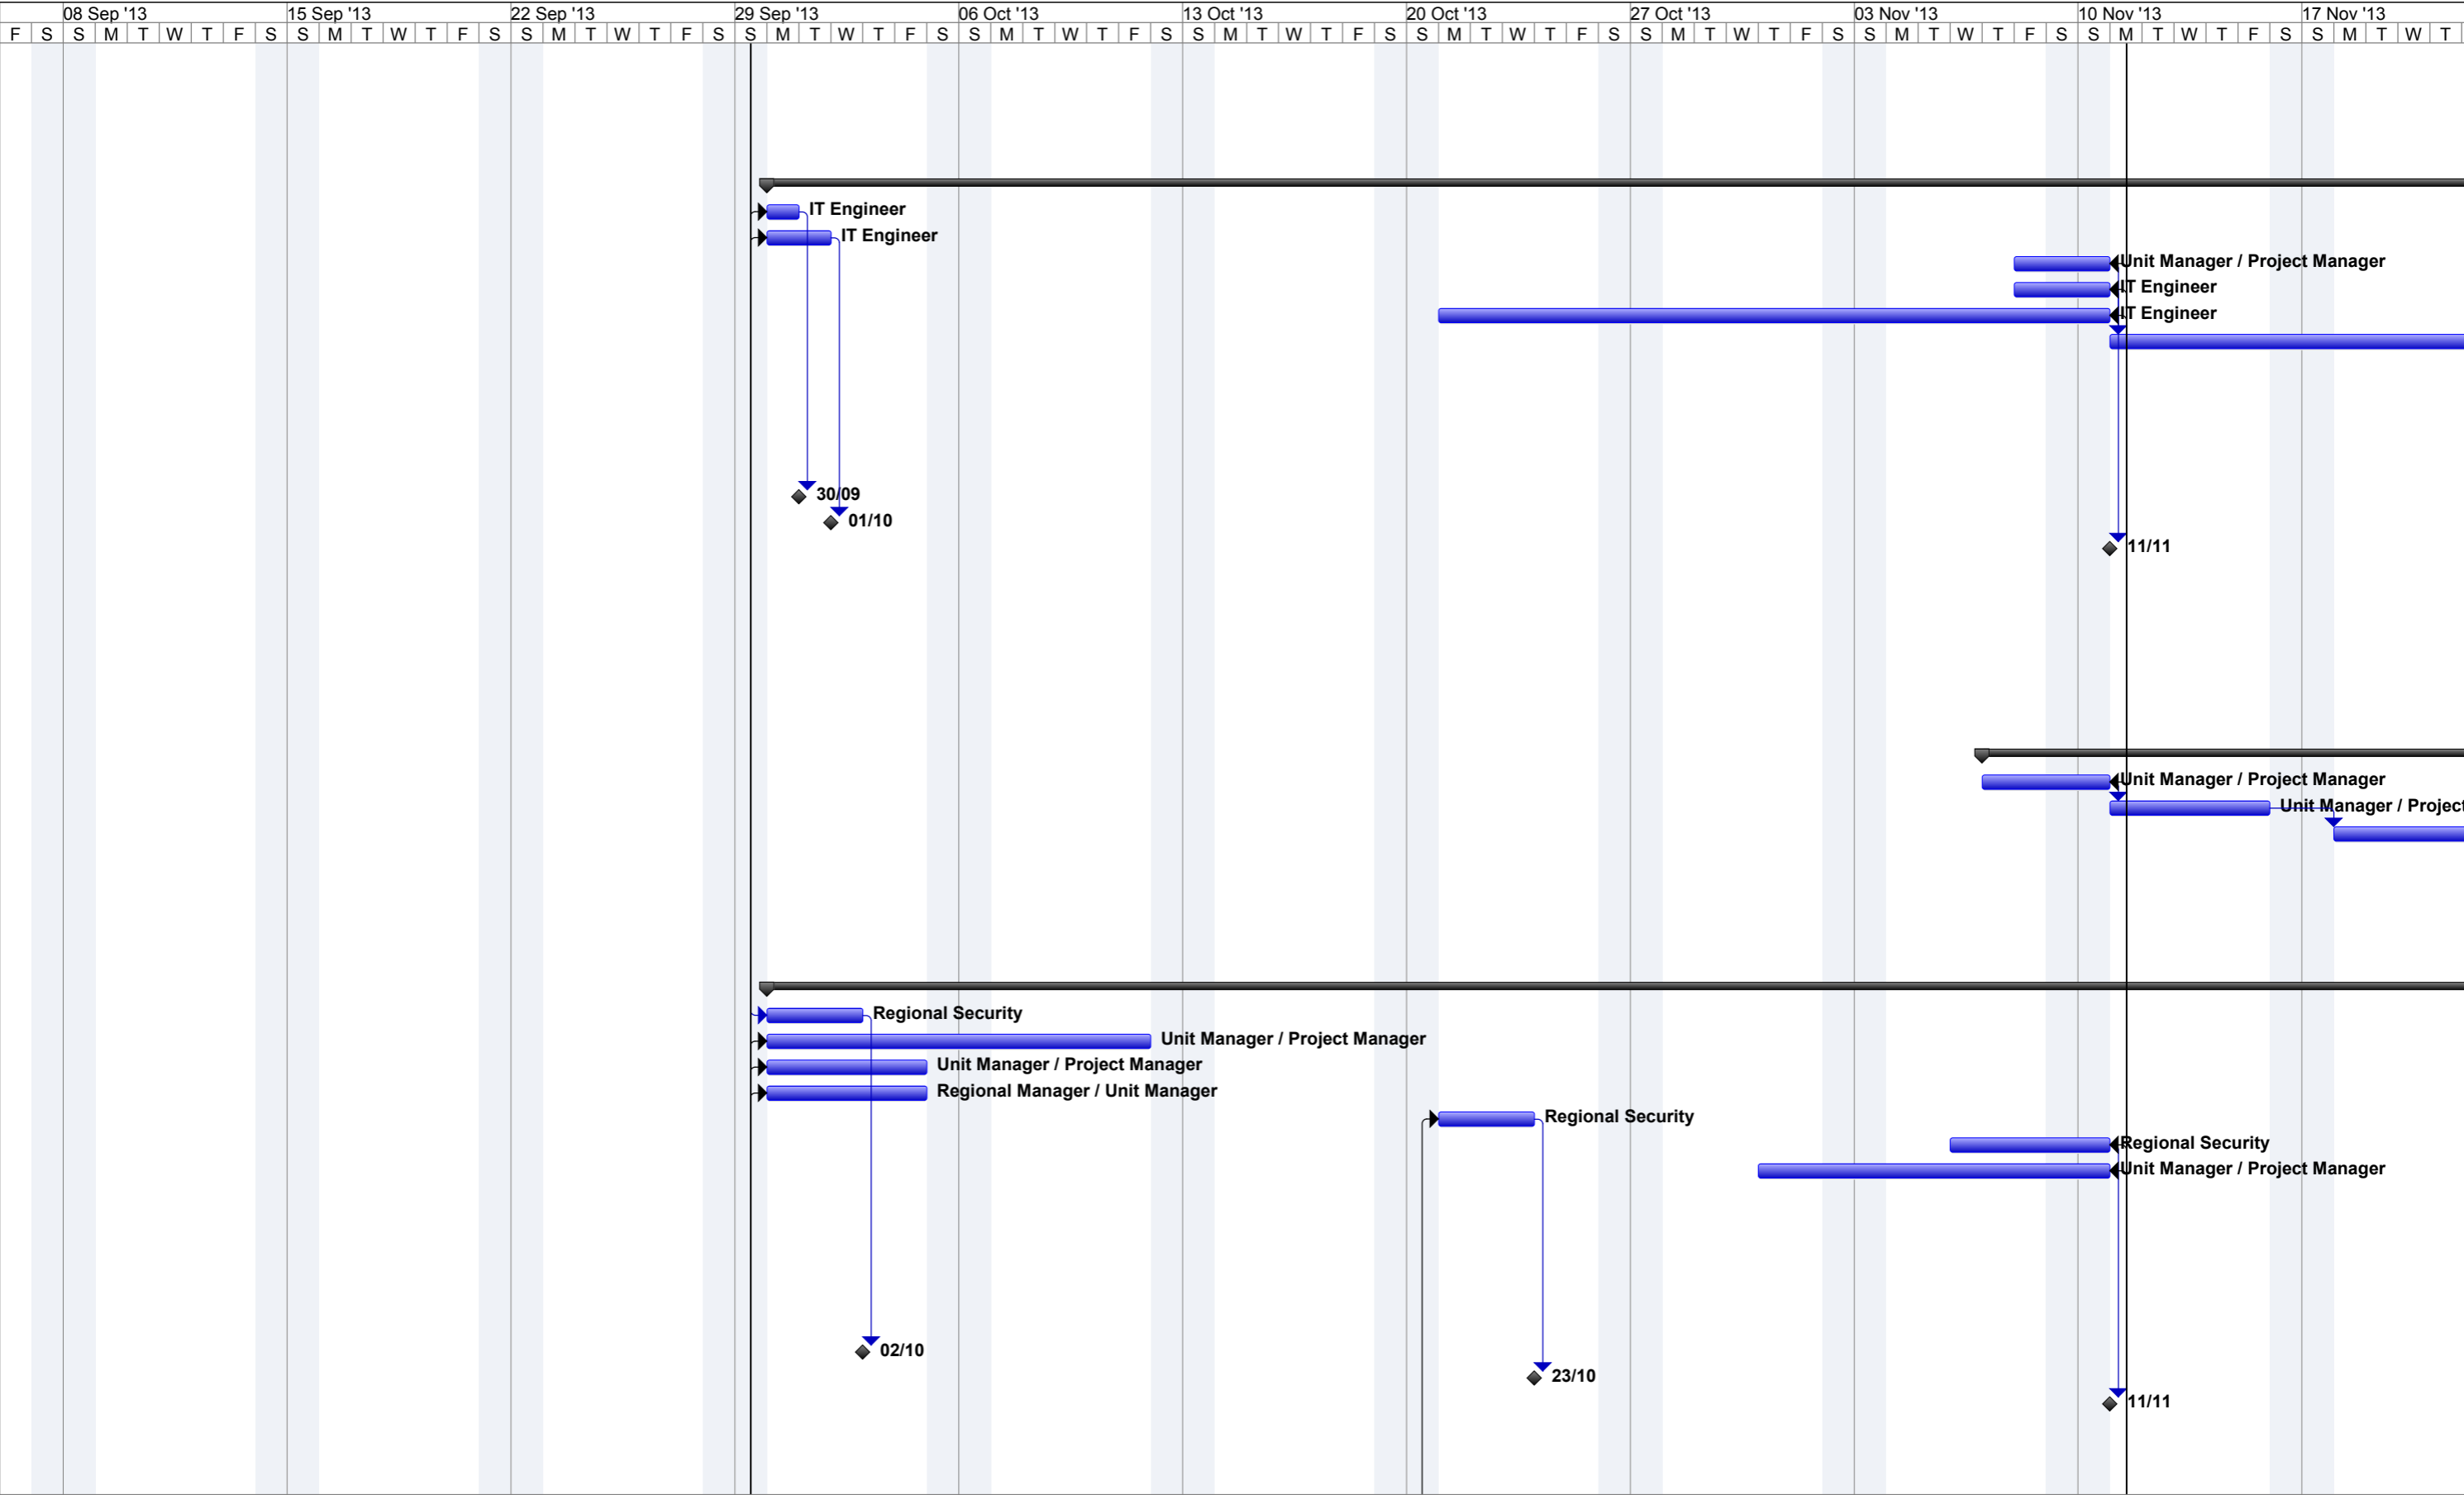

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Progress

Deadline

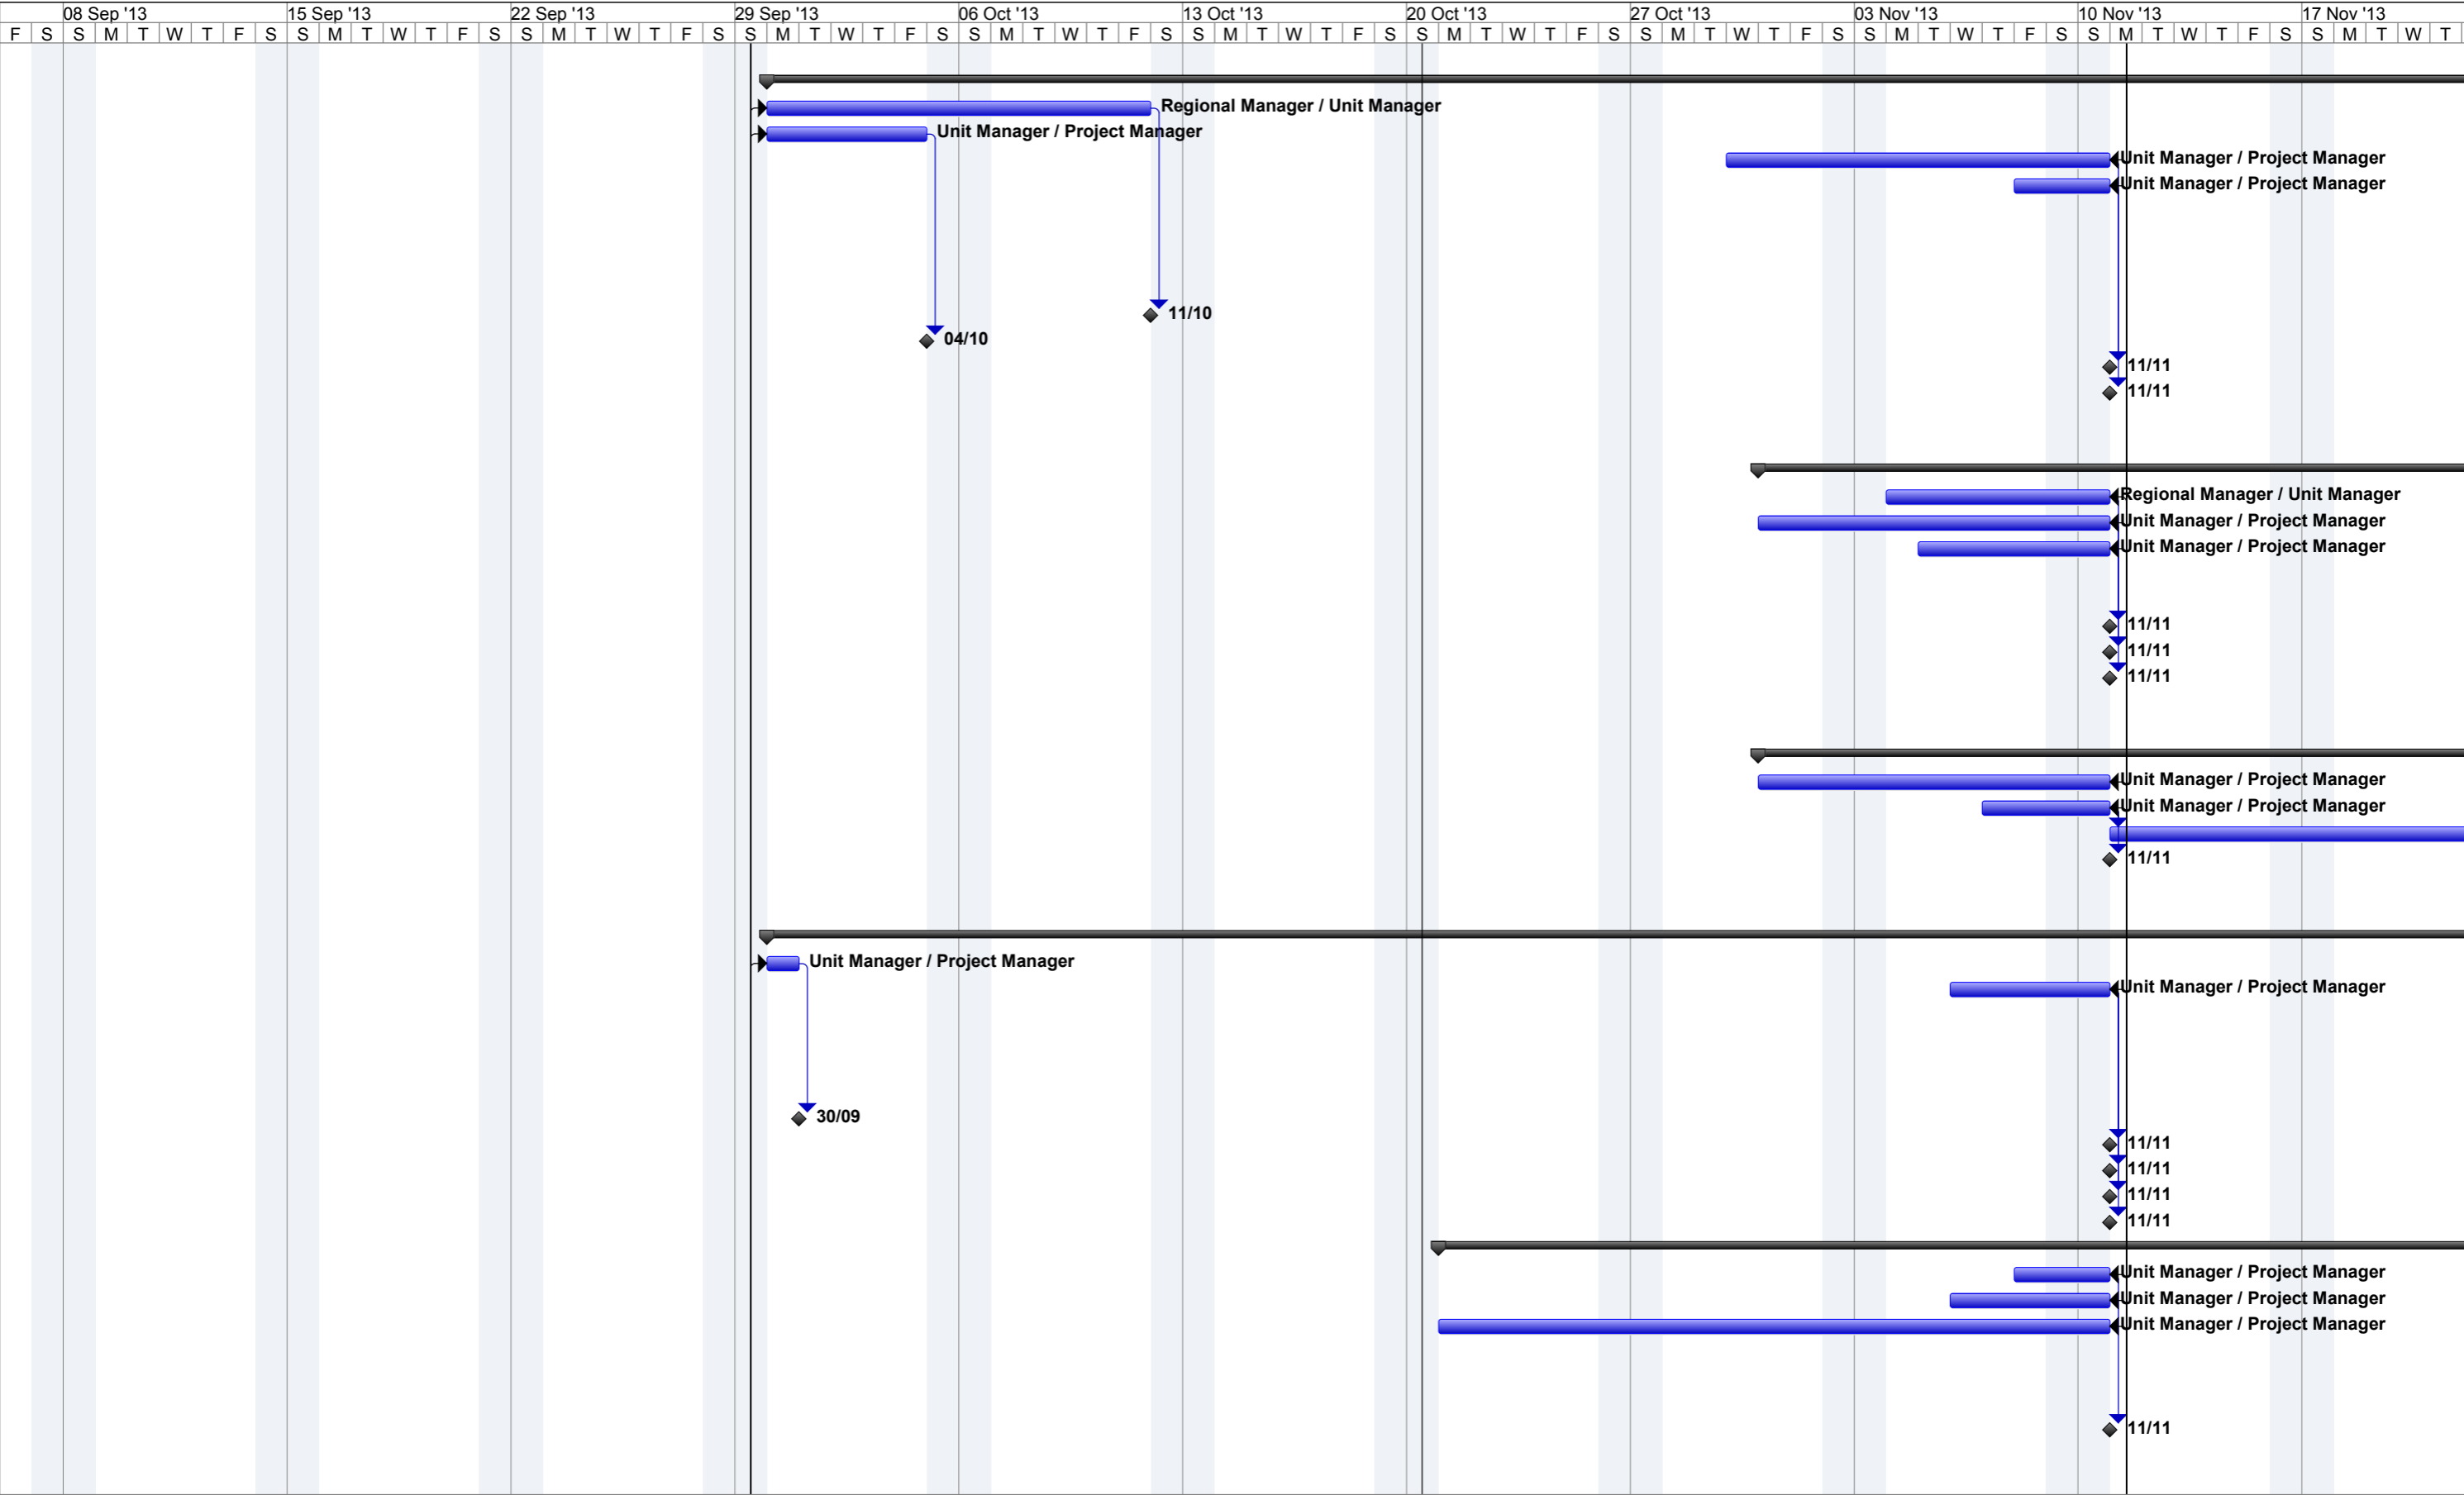

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only


Progress

Deadline

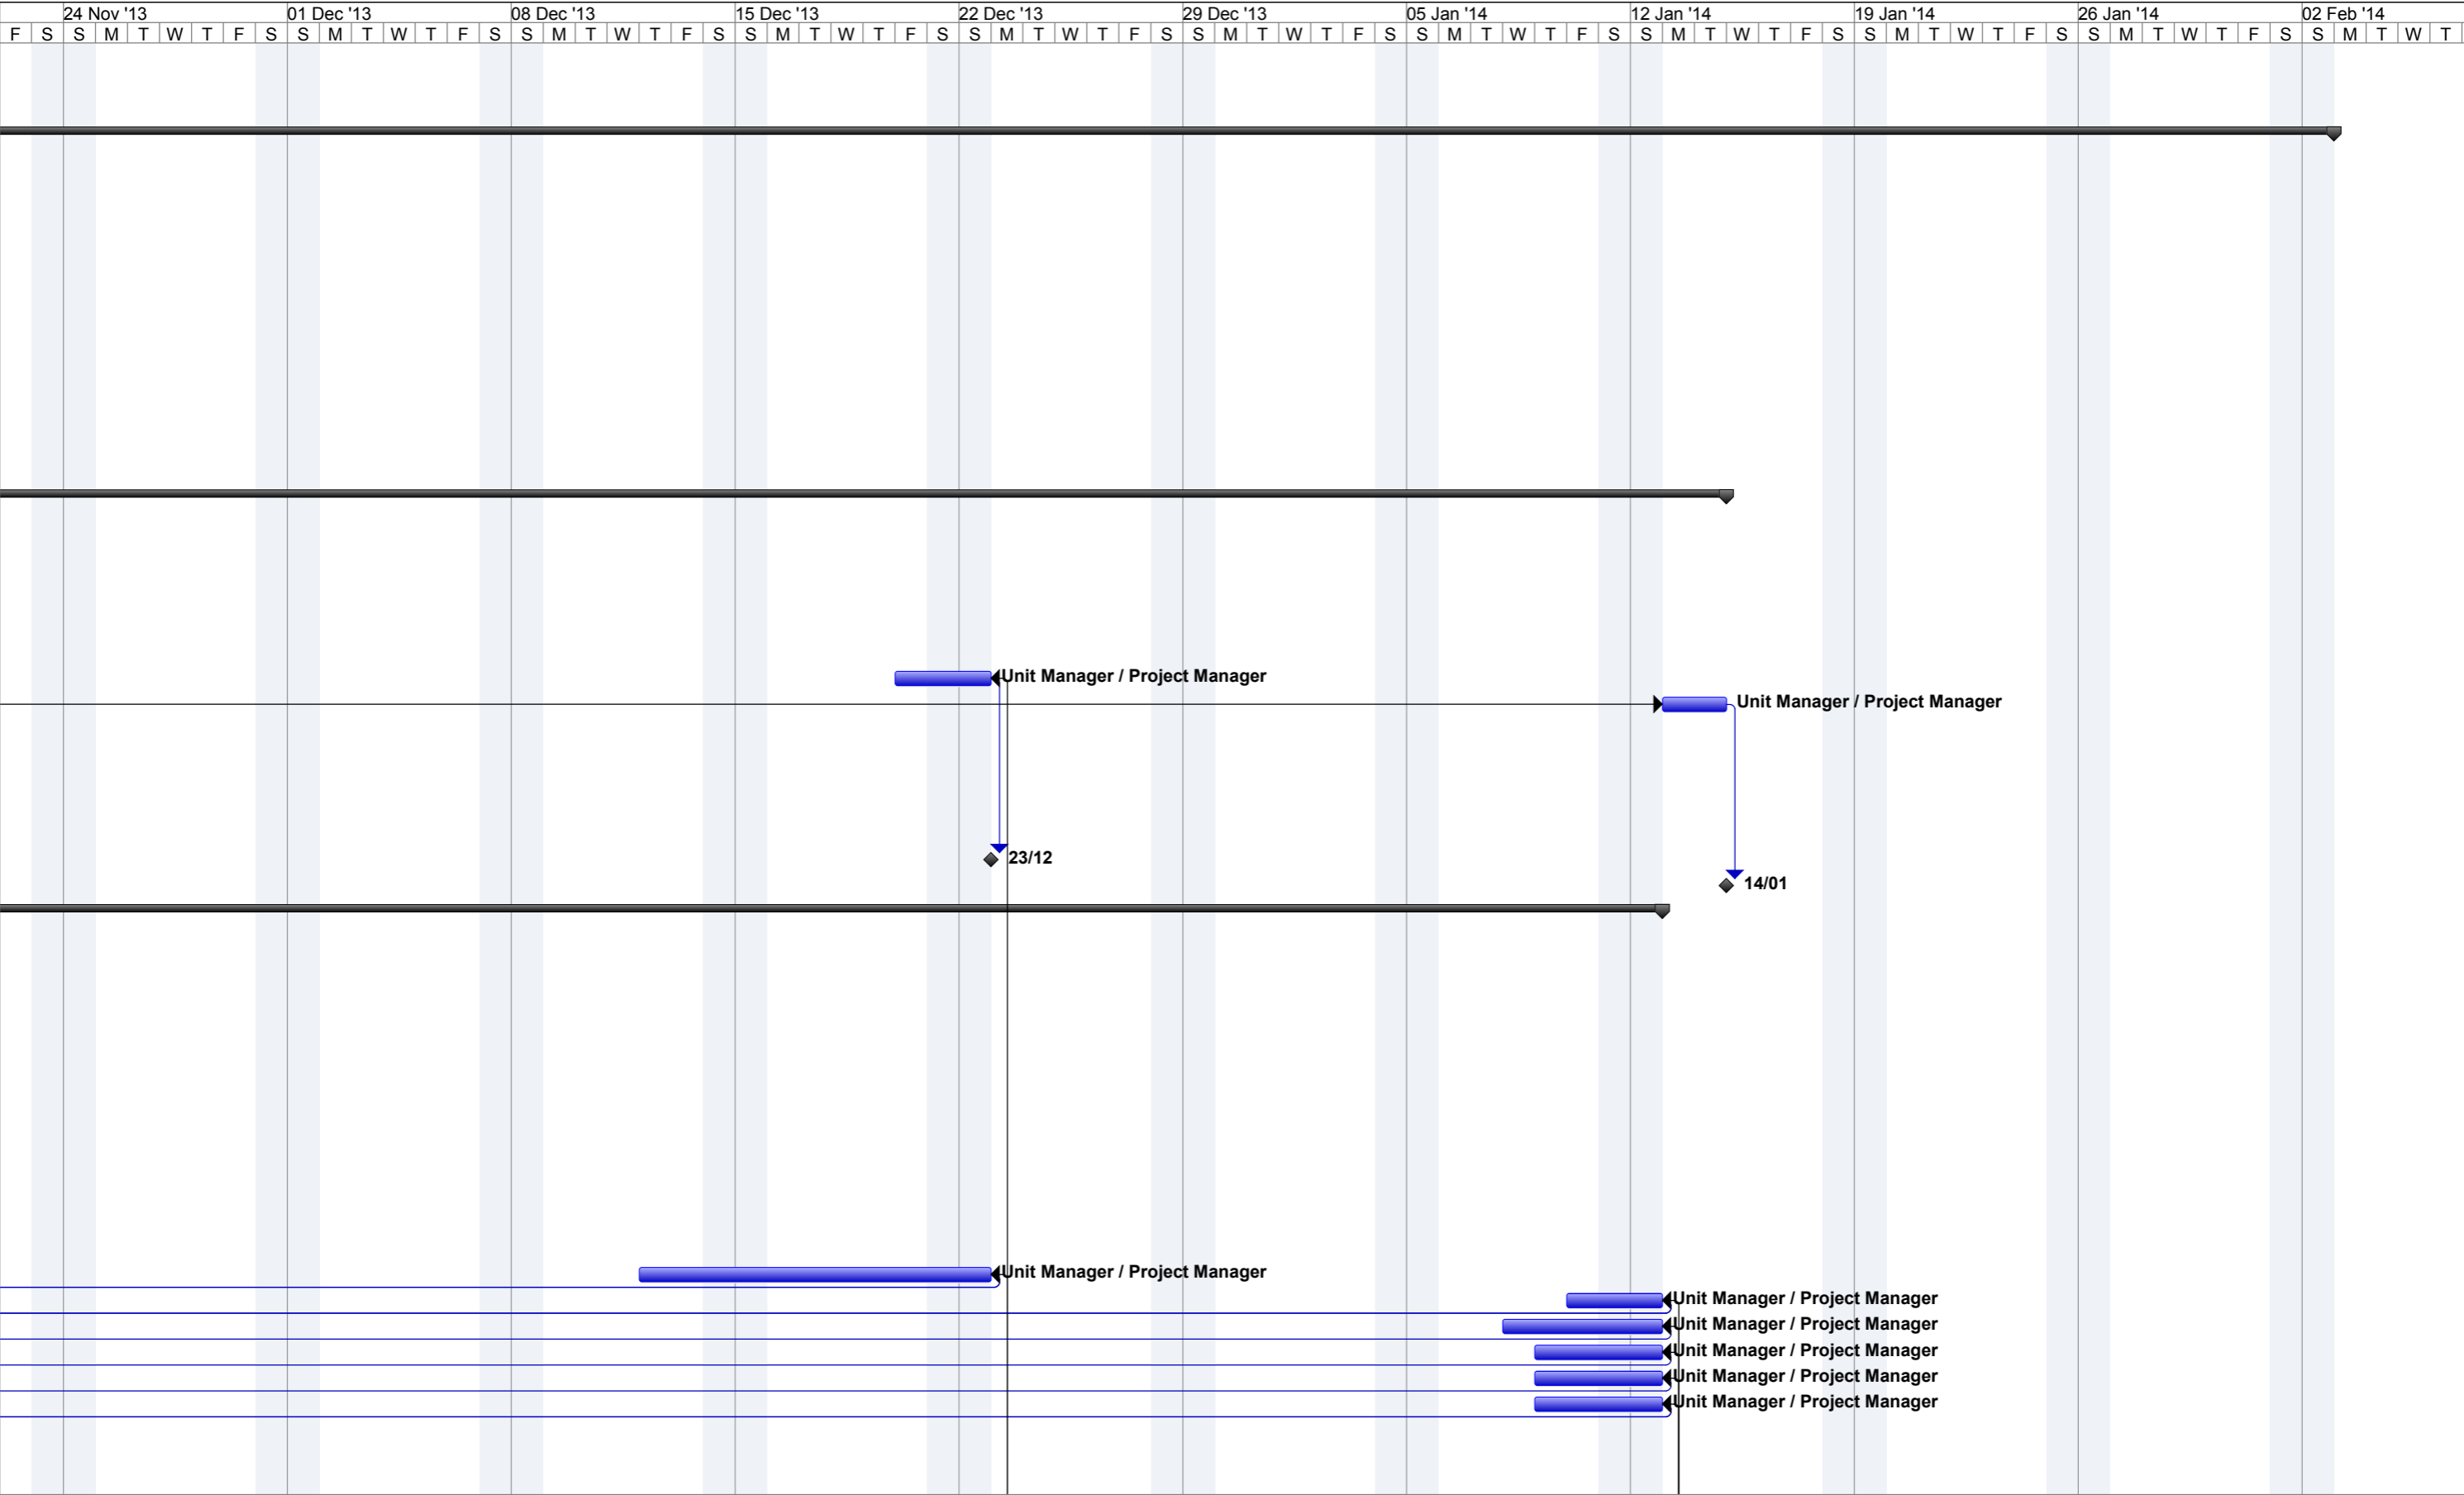

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

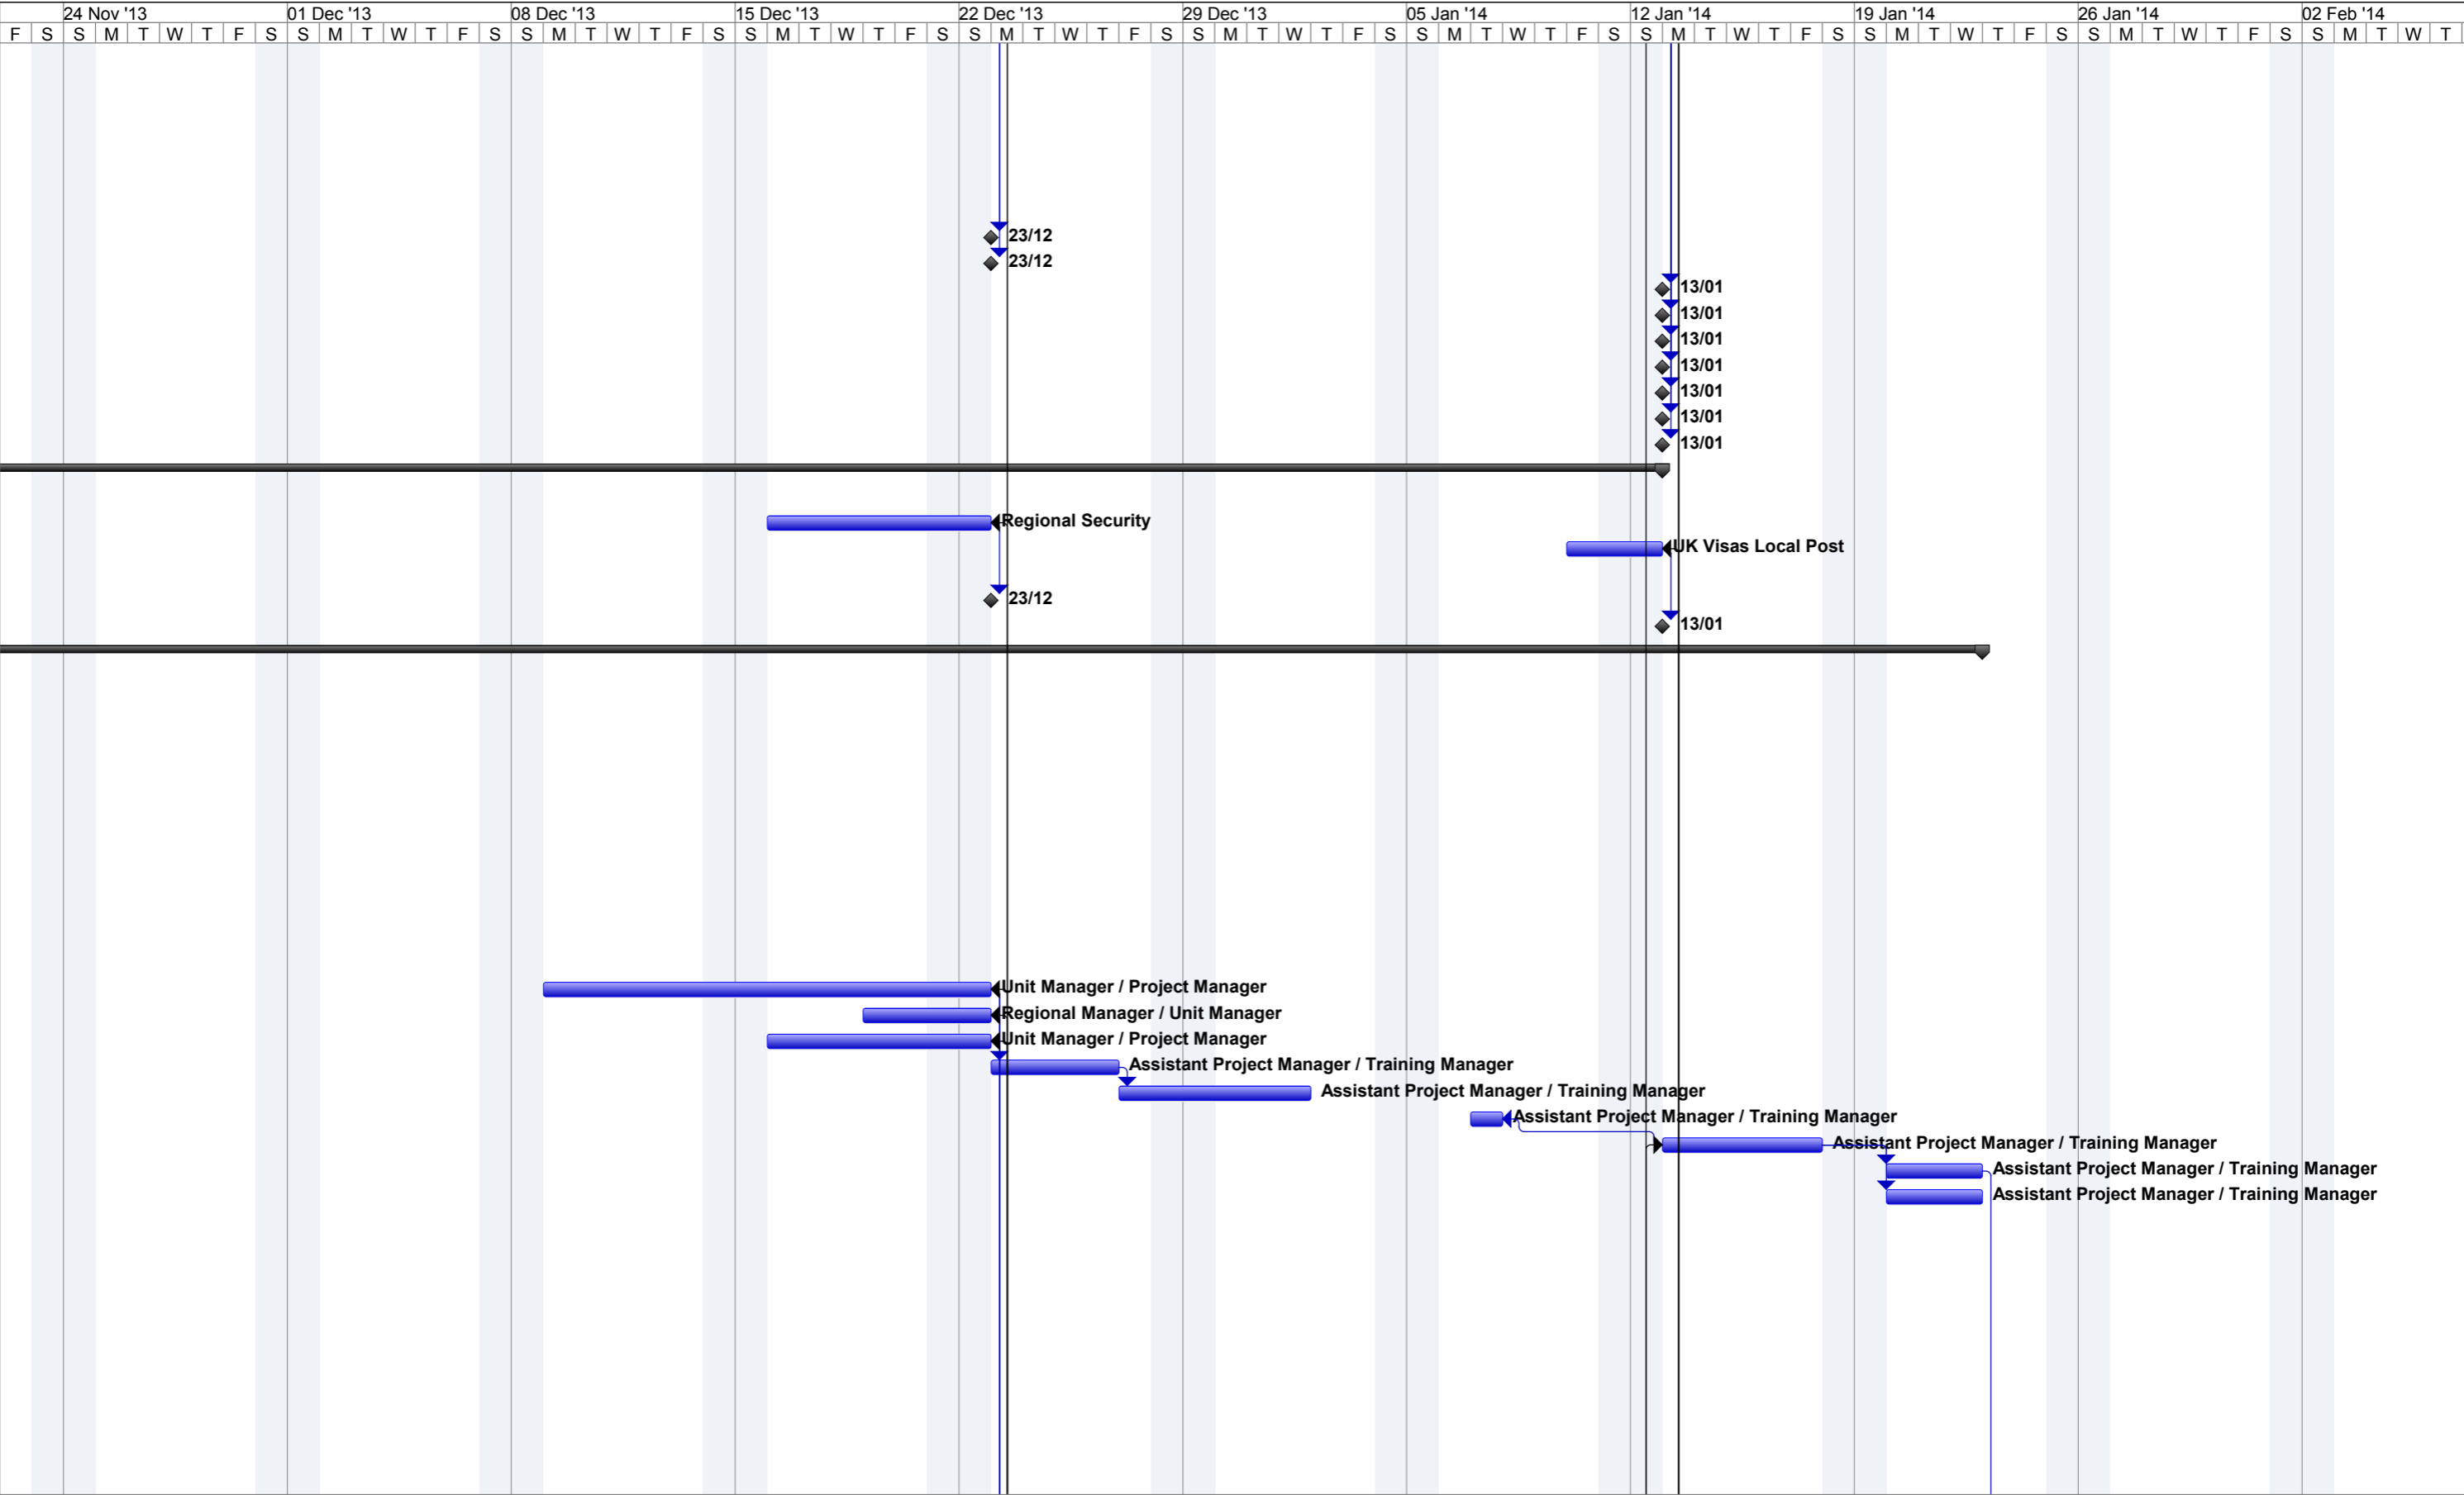

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only


Finish-only

Progress

Deadline

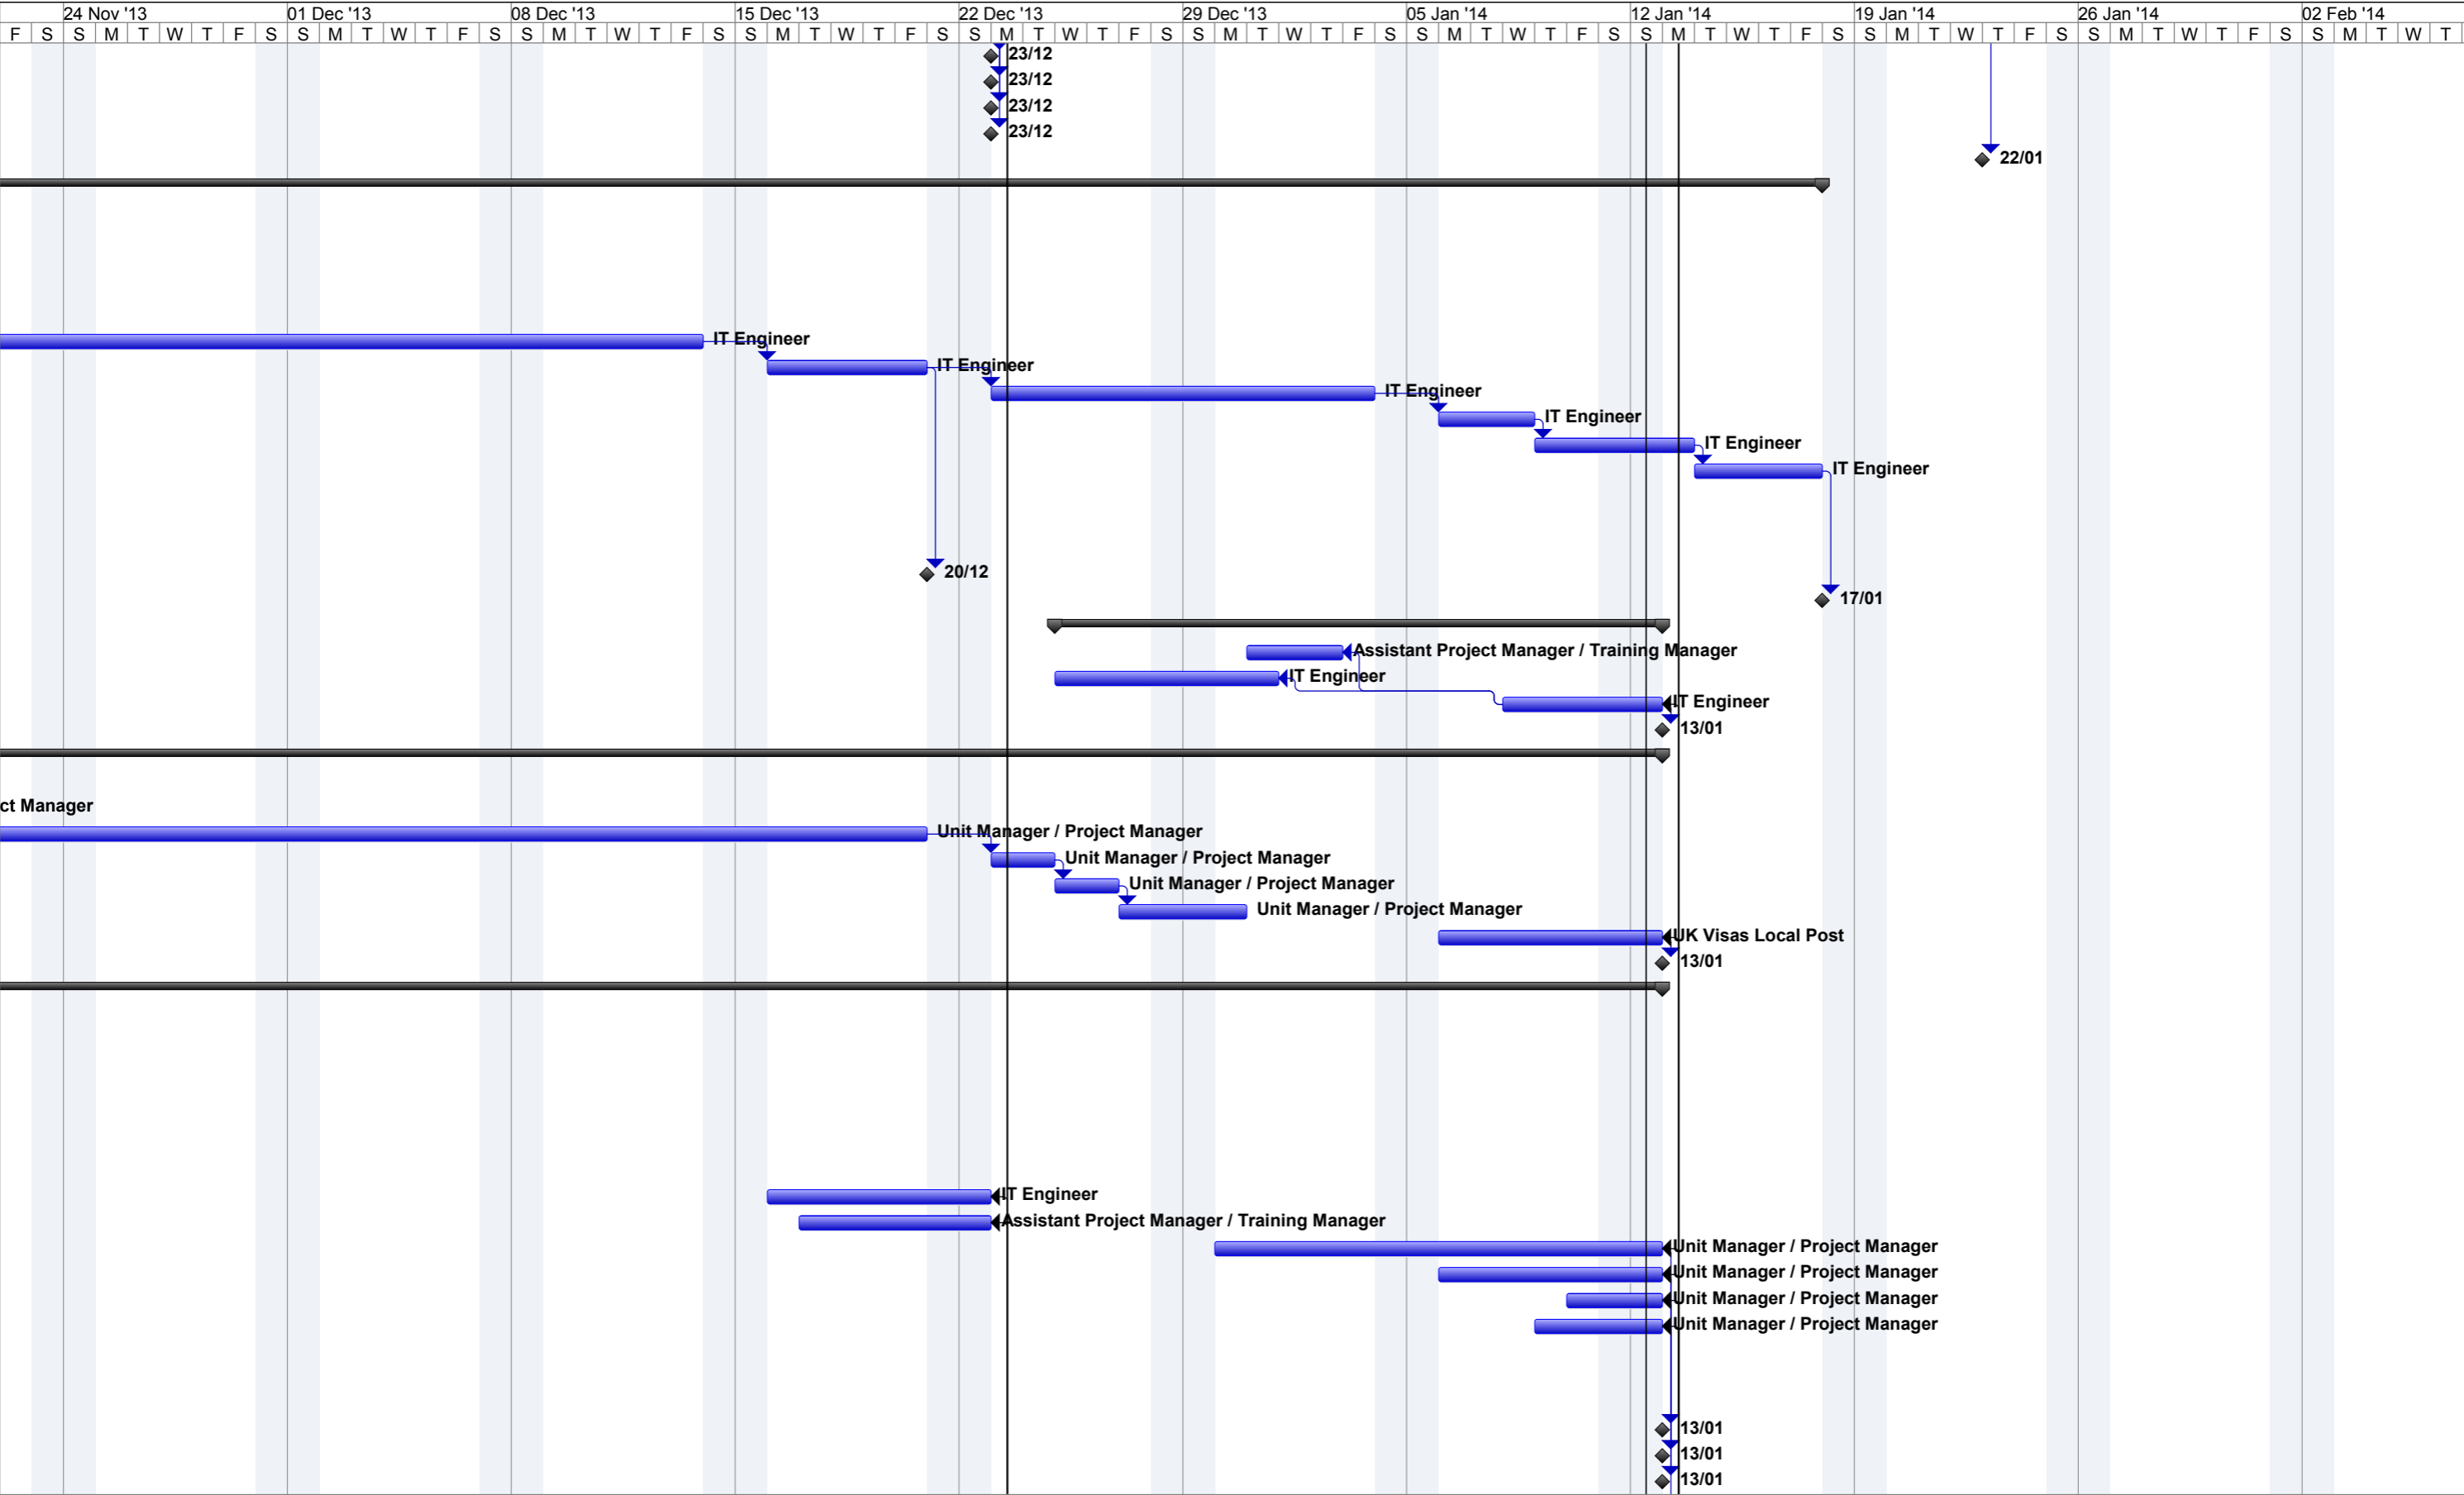

Project: Sample GANTT Chart Date: Tue 30/04/13	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

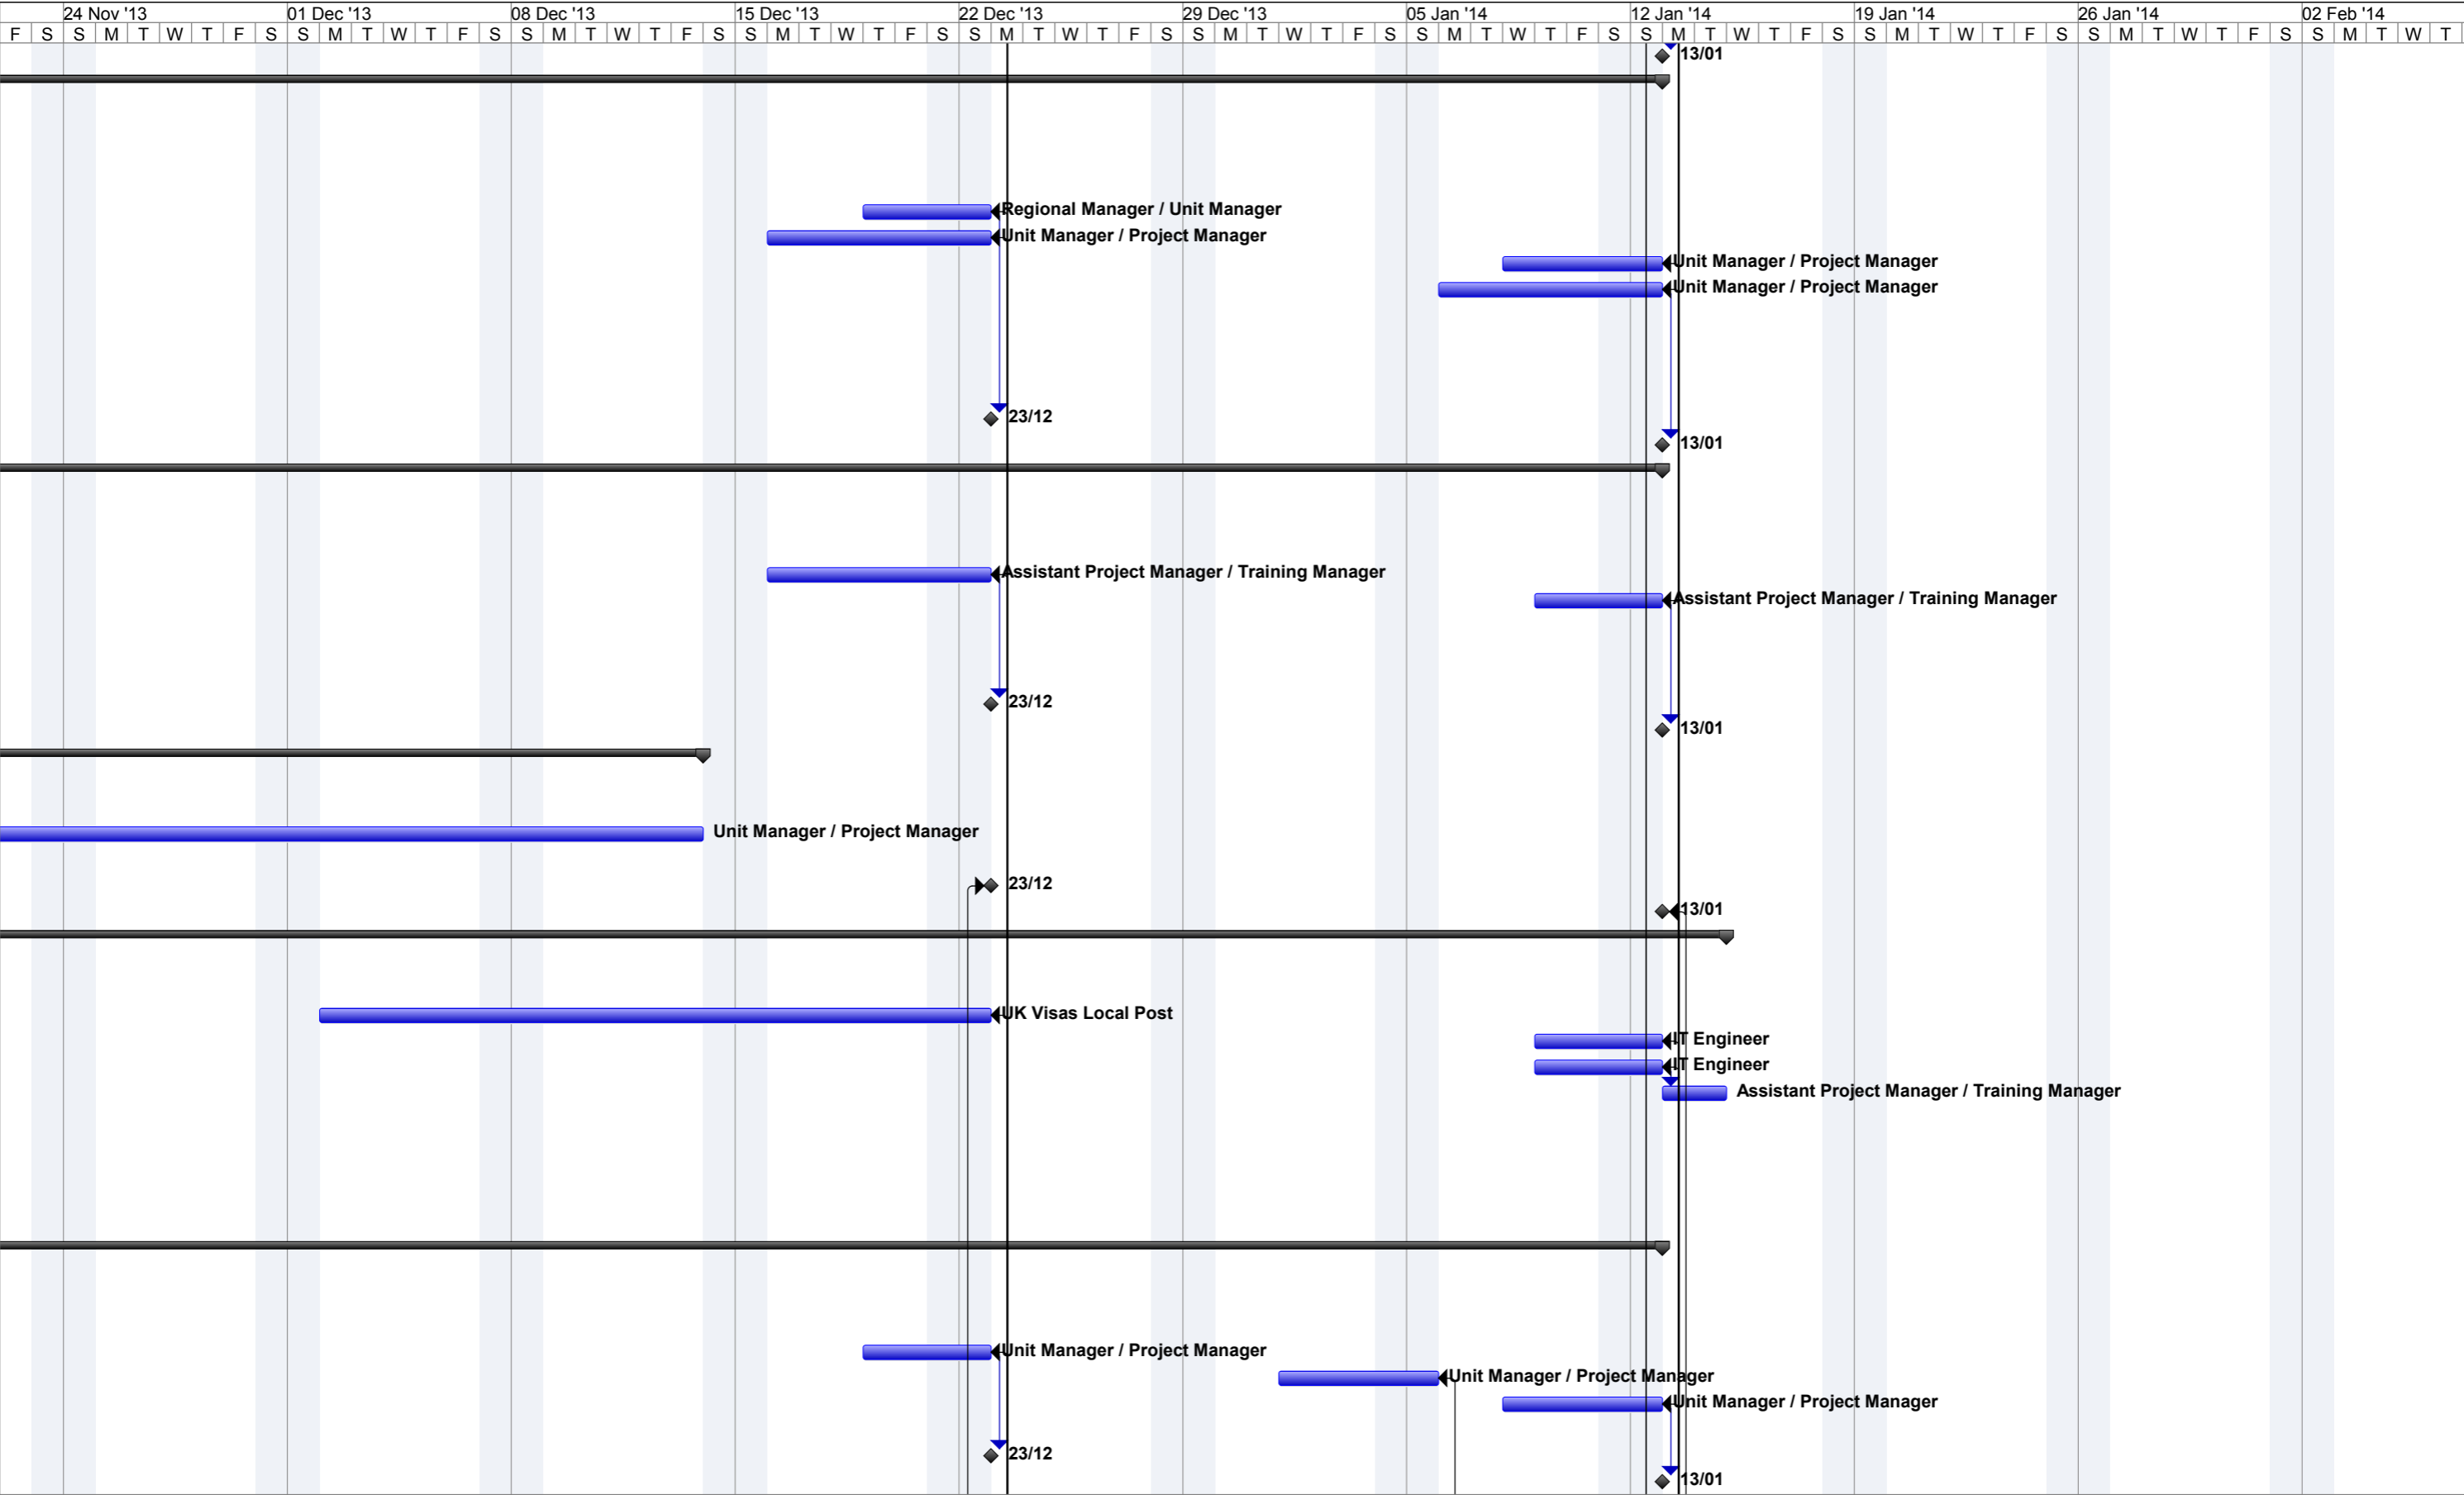

Project: Sample GANTT Chart
Date: Tue 30/04/13

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup


Manual Summary

Start-only

Finish-only

Progress

Deadline

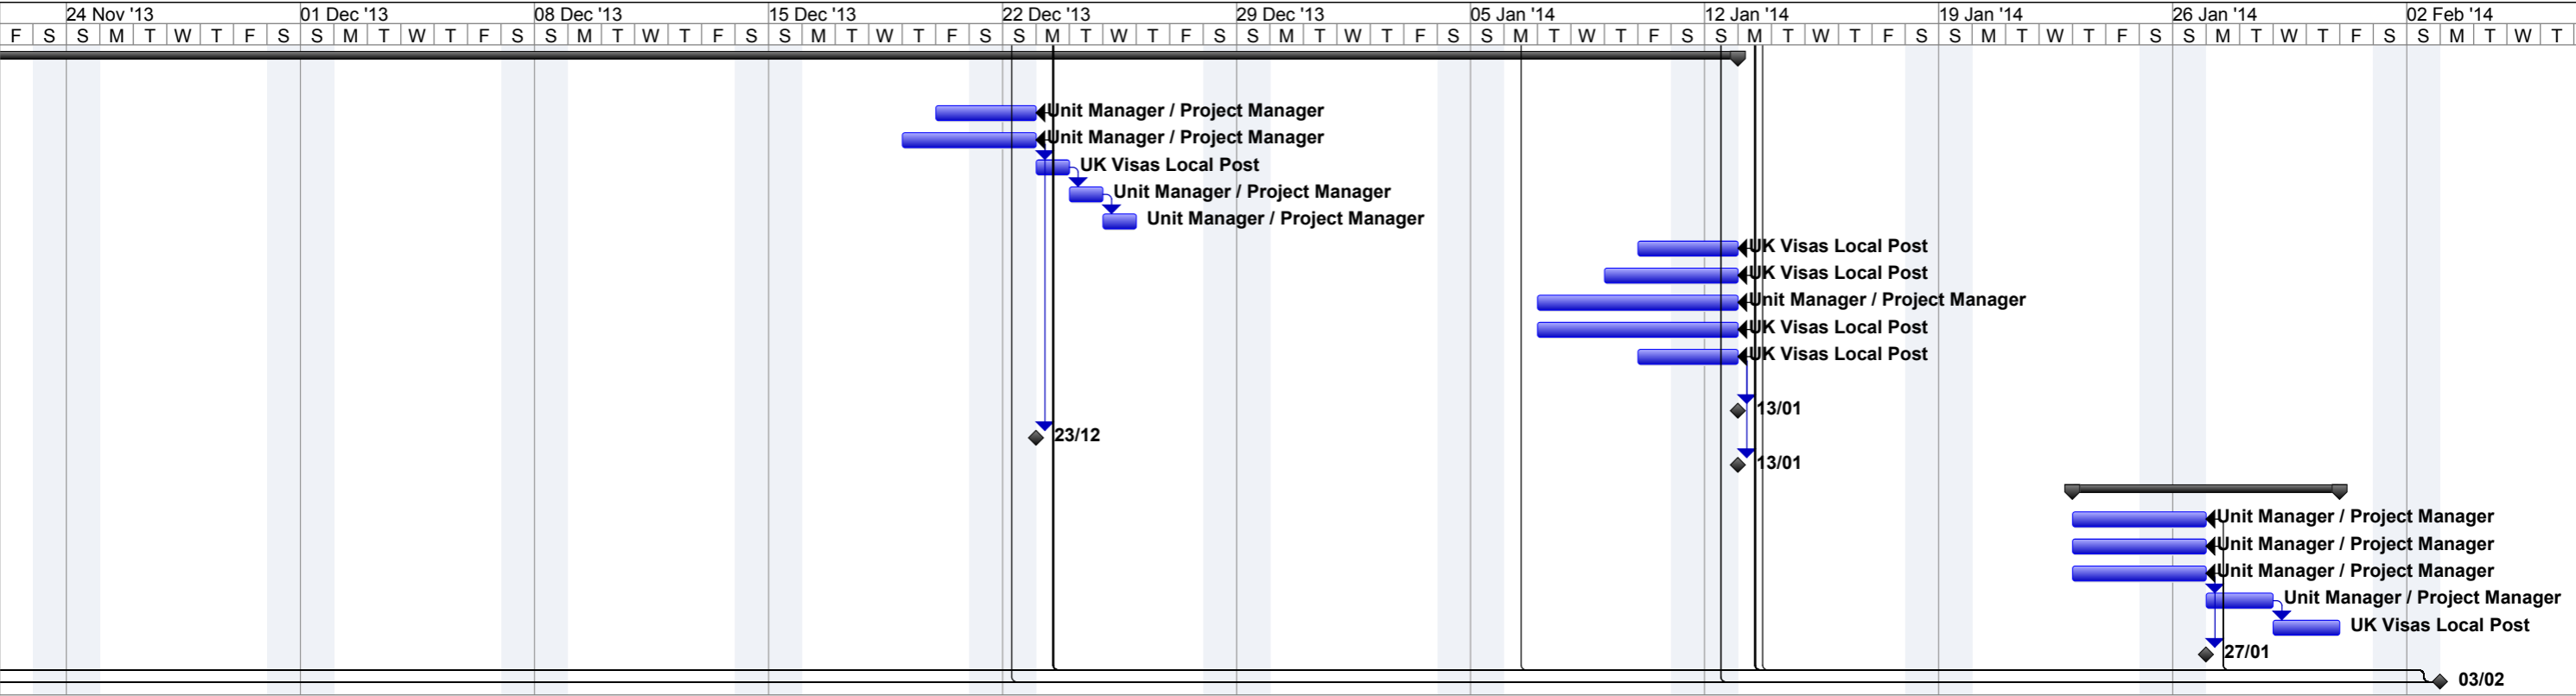

Project: Sample GANTT Chart Date: Tue 30/04/13	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
