NEC4 Engineering and Construction Short Contract				
Property Flood Resilience Framework 2024 Lot 2				
The Environment Agency				
Flood Control (NI) Ltd				
Warwick Bridge Holme Eden Gardens PFR				
Contract Forms - Contract Data - The Contractor's Offer and Client's Acceptance - Price List - Scope - Site Information				

Contract Data

The Client's Contract Data

	The Client is		
Name	Environment Agency		
Address for communications			
Address for electronic	F		
communications			
The works are	Provision and installation of Property Floor for 16 properties	d resilience me	easures (PFR)
The site is	Warwick Bridge, Cum	bria	
The starting date is	24 th March 2025		
The completion date is	24 th March 2026		
The delay damages are		Per day	
The <i>period</i> for reply is	2		weeks
The defects date is	52	weeks after (Completion
The defects correction period is	4	weeks	
The assessment day is	the last working day	of each mont	h
The retention is	to be decided for each call off from framework		
The United Kingdom Housin	ng Grants, Construction and Regeneration A	ct (1996) doe :	s apply.
The Adjudicator is: the person	on appointed as follows:		

In the event that a first dispute is referred to adjudication, the referring Party at the same time applies to the Institution of Civil Engineers to appoint an *Adjudicator*. The application to the Institution includes a copy of this definition of the *Adjudicator*. The referring Party pays the administrative charge made by the Institution. The person appointed is also *Adjudicator* for later disputes.

The tribunal is

The Client's Contract Data

The interest rate on late payment is		% per complete week of delay.	
For any one event, the liability of the Contractor to the Client for loss of or damage to the Client's property is limited to			
The Client provides this insurance	None		

Only enter details here if the Client is to provide insurance.

	Insurance Table	
Event	Cover	Cover provided until
Loss of or damage to the works	The cover is 1.2 times the replacement cost	The Client's certificate of Completion has been issued
Loss of or damage to Equipment, Plant and Materials	The cover is 1.2 times the replacement cost	The Defects Certificate has been issued
The Contractor's liability for loss of or damage to property (except the works, Plant and Materials and Equipment) and for bodily injurt to or death of a person (not an employee of the Contractor) arising from or in connection with the Contractor's Providing the Works	respect of every claim without limit to the number of claims	
Liability for death of or bodily injury to employees of the <i>Contractor</i> arising out of and in the course of their employment in connection with this contract	the applicable law. Each	
Failure of the Contractor to use the skill and care normally used by professionals providing works similar to the works		6 years following Completion of the whole of the works or earlier termination
Loss of, damage to or failure of any Productused in Installation.	Minimum £1,000,000 in respect of every claim without limit to the number of claims	The Defects Certificate has been issued
The Adjudicator nominating body is The	e Institution of Civil Engineers	

litigation in the courts

2020 aiii	endments and the following additional conditions
Only ente	er details here if additional conditions are required.
Z1.0	Sub-contracting
Z1.1	The Contractor submits the name of each proposed sub-contractor to the Client for acceptance. A reason for not accepting the sub-contractor is that their appointment will not allow the Contractor to Provide the Works. The Contractor does not appoint a proposed subcontractor until the Client has accepted him.
Z1.2	Payment to subcontractors and suppliers will be no more than 30 days from receipt of invoice.
Z2.0	Environment Agency as a regulatory authority
Z2.1	The Environment Agency's position as a regulatory authority and as <i>Client</i> under the contract is separate and distinct. Actions taken in one capacity are deemed not to be taken in the other.
Z2.2	Where statutory consents must be obtained from the Environment Agency in its capacity as a regulatory authority, the <i>Contractor</i> is responsible for obtaining these and paying fees. The <i>Client's</i> acceptance of a tender and the <i>Client's</i> instruction or variation of the works does not constitute statutory approval or consent.
Z2.3	An action by the Environment Agency as regulatory authority is not in its capacity as <i>Client</i> and is not a compensation event.
Z3.0	Confidentiality & Publicity
Z3.1	The Contractor may publicise the works only with the Client's written agreement
Z4.0	Correctness of Site Information
Z4.1	Site Information about the ground, subsoil, ducts, cables, pipes and structures is provided in good faith by the <i>Client</i> but is not warranted correct. The <i>Contractor</i> checks the correctness of any sucl Site Information they rely on for the purpose of Providing the Works.
Z5.0	The Contracts (Rights of Third Parties) Act 1999
Z 5.1	For the purposes of the Contracts (Rights of Third Parties) Act 1999, nothing in this contract confers or purports to confer on a third party any benefit or any right to enforce a term of this contract.
Z6.0	Design
Z6.1	Where design is undertaken, it is the obligation of the <i>Contractor</i> to ensure the use of skill and care normally used by professionals providing similar design services.
Z7.0	Change to Compensation Events
Z7.1	Delete the text of Clause 60.1(11) and replace by:
	The works are affected by any one of the following events
	War, civil war, rebellion revolution, insurrection, military or usurped power
	 Strikes, riots and civil commotion not confined to the employees of the Contractor and sub contractors
	 Ionising radiation or radioactive contamination from nuclear fuel or nuclear waste resulting fron the combustion of nuclear fuel
	Radioactive, toxic, explosive or other hazardous properties of an explosive nuclear device
	Natural disaster
	Fire and explosion
	Impact by aircraft or other device or thing dropped from them
Z8.0	Framework Agreement
Z8.1	The Contractor shall ensure at all times during this contract it complies with all the obligations and conditions of the Framework Agreement made with the Client.
Z9.0	Termination
Z9.1	Payment on Termination

	Replace Clause 92.3 with "If the <i>Contractor</i> terminates for Reason 1 or 6, the amount due on termination also includes 5% of any excess of a forecast of the amount due at Completion had there been no termination over the amount due on termination assessed as for normal payments".
Z10	Data Protection
Z10.1	Schedule 14 – Data Protection Schedule of the Deed of Agreement shall be incorporated into this Agreement.
Z10.2	A request or instruction pursuant to Schedule 14 by the <i>Project Manager</i> shall be treated as being a request or instruction by the <i>Client</i> .
Z10.3	For the avoidance of doubt, reference to Supplier in Schedule 14 is reference to the Contractor.
Z11	Liabilities and Insurance
Z11.1	Civil data protection claims and regulatory fines for breaches of Data Protection Legislation are excluded from any limit of liability stated.
Z12	Inflation
	At the Contract Date the Client set total of the Prices does not include a sum to cover inflation.
	The total of the Prices [at the Contract Date] shall be adjusted by a fixed number of Price Adjustments.
	The number of Price Adjustments shall be equal to:
	The number of months between the Completion Date included at the Contract Date and the Contract Date.
	The proportion of Price Adjustment shall be equal to:
	The Client set total of the Prices at the Contract Date / The number of Price Adjustments
	Each time the amount due is assessed, the Price Adjustment shall be:
	The proportion of Price Adjustment x [80% x Construction Output Price, Non-Housing Repair & Maintenance index – month rate]
	The Construction Output Price, Non-Housing Repair & Maintenance index – month rate shall be the value determined by the Office of National Statistics for the applicable month of the amount due assessment
	Provided always that the fixed number of Price Adjustments has NOT been exceeded.
	The Price Adjustment adjusts the [Client set] total of the Prices.
	If a compensation event under this contract omits original Scope covered by the total of the Prices at the Contract Date the Price Adjustments made under this clause shall be corrected accordingly.

Contract Data

The percentage for adjustment for Equipment is

The Contractor's Contract Data The Contractor is Flood Control (NI) Ltd Name Address for communications Address for electronic communications The fee percentage is The people rates are category of person unit rate The published list of Equipment is

Contract Data

The *Contractor's* Offer and *Client's* Acceptance

The Contractor offers to Provide the Work determined in accordance with these contracts.	forks in accordance with these conditions of contract for an amount to be conditions of contract.
The offered total of the Prices is	
	Enter the total of the Prices from the Price List.
Signed on behalf of the Contractor	
Name	
Position	
Signature	

Date	
	,
The Client accepts the Contractor's Off	er to Provide the Works
Signed on behalf of the Client	
Name	
Position	
Signature	
Date	

Price List


Entries in the first four columns in this Price List are made either by the Client or the tenderer.


If the *Contractor* is to be paid an amount for the item which is not adjusted if the quantity of work in the item changes, the tenderer enters the amount in the Price Column only: the Unit, Quantity and rate columns being left blank.


If the Contractor is to be paid an amount for the item of work which is the rate for the work multiplied by the quantity completed, the tenderer enters the rate which is then multiplied by the expected quantity to produce the Price, which is also entered.


ltem Number	Description	Unit	Quantity	Rate	Price (£)
1	Homeowner Engagement of all property owners				
2	Works inspections				
3	Homeowner agreements				
4	Prelims as per prelims tab on supplied pricing schedule v6				
5	Order, supply and installation of PFR products				
6	Order, supply and installation of PFR products				
7	Order, supply and installation	The state of the s			
8	Completion of Wet testing				
9	Develop handover packs for products with operational instructions and warranties etc. (hard copy and digital)				
10	Sign off and completion				
		 			
		L	J	1	.1
	The t	otal of	the Prices		

The method and rules used to compile the Price List are PFR 2024 Framework pricing schedule. Any items not listed on the schedule will be priced separately.
Scope
Scope
The Scope should be a complete and precise statement of the <i>Client's</i> requirements. If it is incomplete or imprecise there is a risk that the <i>Contractor</i> will interpret it differently from the <i>Client's</i> intention.
1. Description of the works
The scope of works is the provision of Property Flood Resilience (PFR) to reduce flood risk

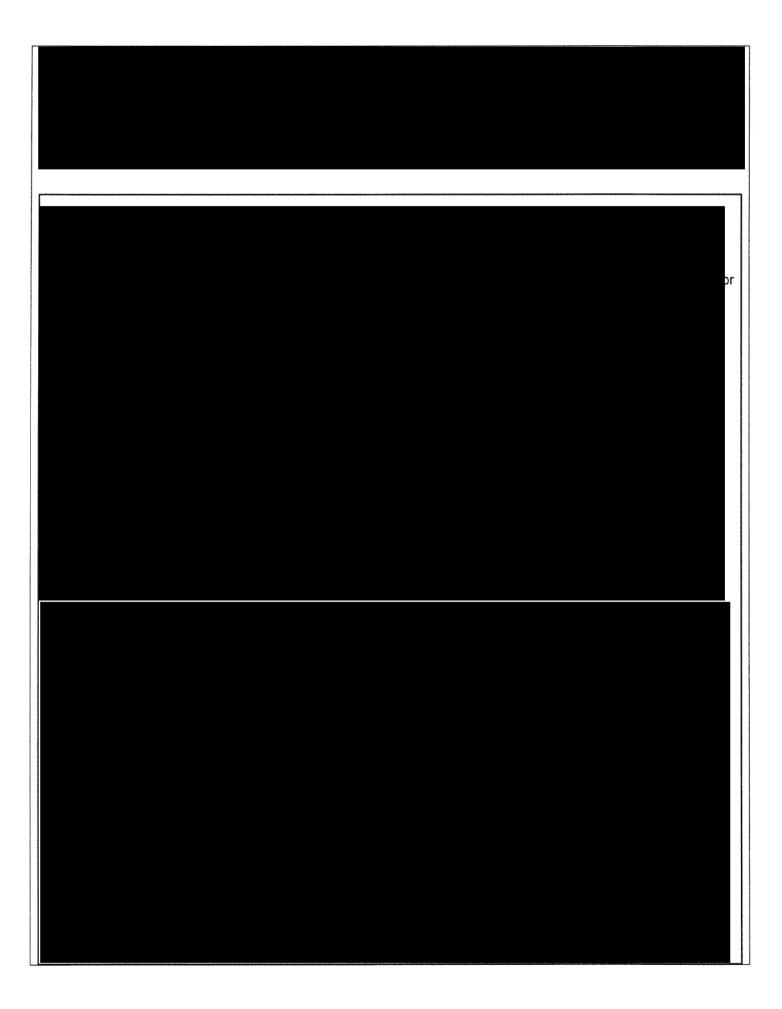

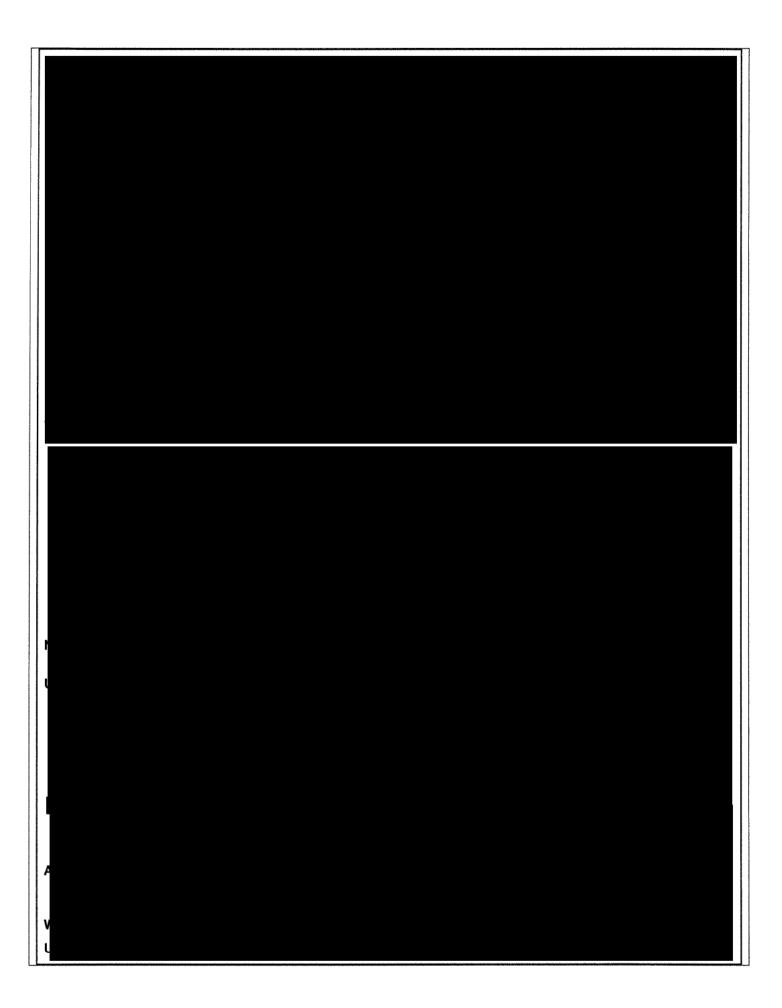

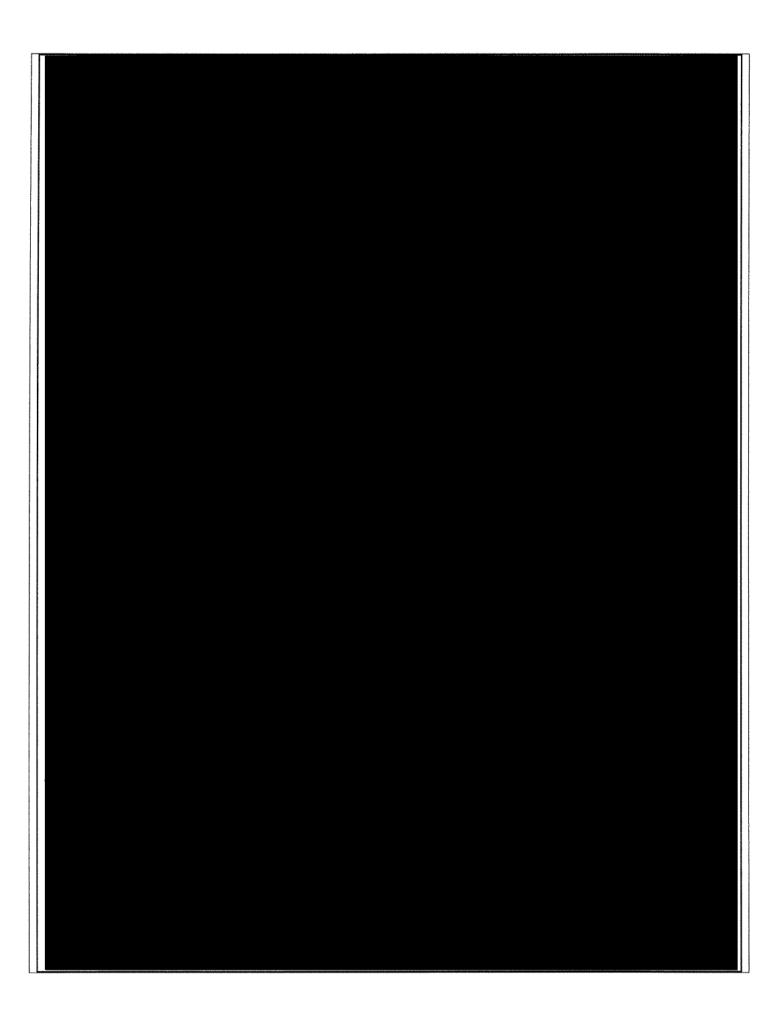

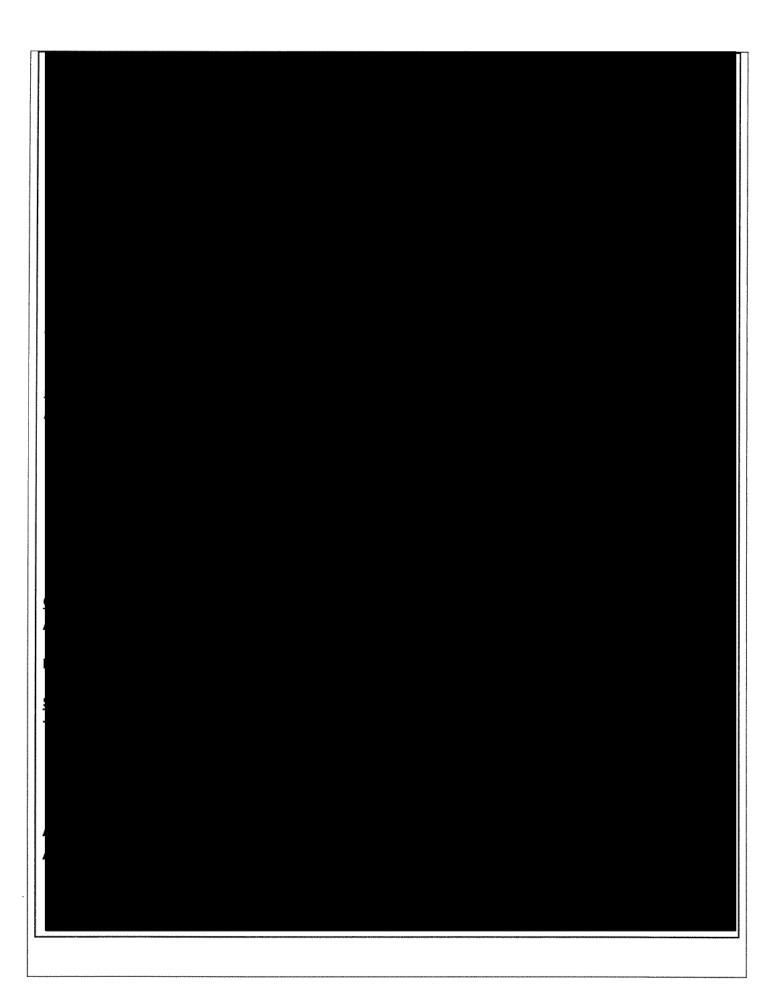

2. Drawings & documents?					
List the drawings that apply to the contract.					
Drawing Number	Revision	Title			

	~~~				
3. Specifications					
List the specifications which apply to the contract.					
				<del></del>	
Title		Date	e or	Tick	if
1100		Duc		1 1011	
		Rev	rision	publicly availab	y
Minimum Technical Requirements		V12	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements		V12	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements		V12 Dec	Dated		y
Minimum Technical Requirements  4. Constraints on how the Contractor Provides the Works		V12 Dec	Dated		y
	ne methods	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the <i>Contractor</i> Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the <i>Client</i> .	ne methods	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the <i>Contractor</i> Provides the Works  State any constraints on the sequence and timing of work and on the	VALUE AND A SECURITY OF THE SE	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECURITY OF THE SE	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECURITY OF THE SE	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECOND SECO	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECOND SECO	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECOND SECO	V12 Dec 202	Dated cember 1	availab	y le
4. Constraints on how the Contractor Provides the Works  State any constraints on the sequence and timing of work and on the requirements for any work by the Client.  Compound, welfare, access,	VALUE AND A SECOND SECO	V12 Dec 202	Dated cember 1	availab	y le

Working times	
The Contractor will be permitted to work between 7.30am and 6.00pm on weekdays (Monday to Frid	lay).
This can be negotiated with residents on site	
5. Requirements for the programme	
State whether a programme is required and, if it is, state what form it is to be in, what informa on it, when it is to be submitted and when it is to be updated.	tion is to be shown
State what the use of the works is intended to be at their Completion as defined in clause 11.	2(1).
The Contractor submits his programme with the Contractor's Offer for acceptance. The Contractor programme which he submits for acceptance on a monthly basis (in form of Gantt chart showing the corder and timing to undertake the works and proposed plant and labour resources) the following:	ctor shows on each ritical path, proposed
(a) Period required for mobilisation/ planning & post contract award	
(b) starting date	
(c) Each of the activities listed within the Price List	
(d) Any key third party interfaces: lead in periods for materials and sub-contractors; time required to ol permits; stated constraints; <i>Contractor's</i> risks.	otain consents/waste
(e) Completion date	
Describe what the <i>Client</i> will provide, such as services (including water and electricity) and and Materials and equipment.	l "free issue" Plant
Item	Date by which it
	will be provided
	<u> </u>
7. Site Information	

Proposed sub-contractors.			
	Name and address of proposed subcontractor	Nature and extent of work	
1.			
2.			
3.			
4.			
