



Ministry
of Justice



Home Office



CPS

Establishment: HMCTS Hove Trial Centre

Project: Mechanical and Electrical Package

BPRN: 145/20/6469

COMMENCEMENT AGREEMENT

OFFICIAL

CONTENTS

Commencement Agreement	
<i>Appendix</i>	<i>Title</i>
A	Project Timetable
B	Construction Phase Health and Safety Information Pack
C	Pre-commencement surveys
D	Planning issues
E	Developed Project Brief and Project Proposals Including: <ul style="list-style-type: none"> Signed DPP Form of Tender Summary scope of works Drawing Register Specifications and Drawings Sustainability Statement Quality Management Plan Statement of Derogations from MOJ Standard Specifications BIM Execution Plan
F	List of Specialists
G	Agreed Maximum Price and Price Framework Including: <ul style="list-style-type: none"> Summary of the AMP Risk Register Cashflow
H	Site Waste Management Plan
J	Evidence of insurance
K	Key Performance Indicators
L	Queries raised by the Technical Assessors and the responses to these queries: <ul style="list-style-type: none"> TA Report – Structures P01 TA Acoustic Design MEP DPP Report MEP Upgrade Construction Phase Plan Rev 2 MEP upgrade Construction Phase Plan with TD Comments Letter of Acknowledgement – TA Reports 2023.11.24 AtkinsRéalis responses to TD letter dated 2023.11.27

OFFICIAL

The Partnering Team members, as named below, in accordance with and subject to the terms of a partnering contract dated the 17th December 2020 (the 'Partnering Contract') made between them in relation to:

Project: Mechanical and Electrical Package

Site: Hove Trial Centre, Lansdowne Rd, Hove BN3 3BN

The Partnering Team members:

Client	Secretary of State for Justice
Constructor and Lead Designer	Tilbury Douglas Construction Limited
Client Representative	AtkinsRéalis PPS Ltd (formerly known as Faithful + Gould Ltd) t/a AtkinsRéalis
Cost Consultant	Gleeds Advisory Limited
Principal Designer	Tilbury Douglas Construction Limited

Agree under this Commencement Agreement that:

1. Words and expressions used in this Commencement Agreement shall have the same meanings as in the Partnering Contract.
2. To the best of their knowledge the Project is ready to commence on Site.
3. The following details shall apply by reference to the listed clauses of the Partnering Terms:

OFFICIAL

Agree under this Commencement Agreement that: (Continued)*Reference in
Partnering Term*

Clause 6.2	The Project Timetable is included in the Developed Project Proposals attached as Appendix A
Clause 6.2	Date of Possession 18 th March 2024
Clause 6.2	Date for Completion 30 th July 2024
Clause 6.3	Project in sections As per the Partnering Timetable and Project Timetable and Special Term 28.11 of the Project Partnering Agreement.
Clauses 6.4 and 15.3 (i)	Parts of site in exclusive or non-exclusive possession: As per the Partnering Timetable and Project Timetable and Special Term 28.11 of the Project Partnering Agreement.
Clauses 6.4 and 15.3 (i)	Constraints on Site possession/access All in accordance with Special Term 28.11 of the Project Partnering Agreement. Arrangements for Client access to be agreed.
Clauses 6.4 and 15.3 (i)	Arrangements for deferred or interrupted Site possession As per the Partnering Timetable and Project Timetable and Special Term 28.11 of the Project Partnering Agreement.
Clause 7.1	The Construction Phase Plan is within the Health and Safety Information Pack which is included in Appendix B
Clause 8	Project Brief and Project Proposals are included in Appendix E

Agree under this Commencement Agreement that: (Continued)*Reference in
Partnering Terms*

Clause 12	The Agreed Maximum Price is £4,106,525.83 (exclusive of VAT)
Clause 12	The Price Framework is included in Appendix G
Clause 18.2	The risk sharing arrangements are detailed in the Appendix G
Clause 18.3(iii)	Third party consents entitling claim for extension of time None other than those items identified as Client Risk items within the Risk Register
Clause 18.3(xvi)	Additional events entitling claim for extension of time None other than those items identified as Client Risk items within the Risk Register
Clause 18.5	Adjusted extensions of time entitling additional Site Overheads None other than those items identified as Client Risk items within the Risk Register
Clause 18.6	Adjusted extensions of time entitling claim for unavoidable work/expenditure None other than those items identified as Client Risk items within the Risk Register
Clause 18.9	Exceptions to Constructor risk as to Site None other than those items identified as Client Risk items within the Risk Register

Agree under this Commencement Agreement that: (Continued)

*Reference in
Partnering Terms*

Clause 19.1

Insurance of the Project shall be taken out by the Constructor

Insurance of all existing structures (and their contents) shall either be taken out by the Client and or the Client shall bear the risk of loss or damage thereto.

With waiver of rights of subrogation against:

Not applicable

With the following percentage addition for fees:



With the following additional or adjusted risks:

None required

Agree under this Commencement Agreement that: (Continued)*Reference in
Partnering Terms*

- | | |
|-------------|--|
| Clause 19.1 | Insurance third party property damage by the Constructor in the sum of: None required. |
| Clause 19.5 | Environmental Risk Insurance by:

None required |
| Clause 19.6 | Latent Defects Insurance by:

None required |
| Clause 19.7 | Whole Project Insurance by:

None required |
| Clause 19.9 | Amount and form of any advance payment guarantee/performance bond/parent company guarantee/retention bond:

None required. |
| Clause 27.2 | Problem-Solving Hierarchy is as attached to the Partnering Contract |
| Clause 28 | Special Terms additional to those set out in or attached to the Partnering Contract:

There are no additional Special Terms other than those previously included within the Project Partnering Agreement |

THE SECRETARY OF STATE FOR JUSTICE

of

Ministry of Justice

10th Floor,

102 Petty France

London SW1H 9AJ


(the “**Client**”)

EXECUTED AS A DEED by the **Client** by affixing
hereto its common seal in the presence of

or Acting by

Authorised signatory

Authorised signatory



Dated the 15th day of December 2023

AtkinsRéalis PPS Ltd (formerly known as Faithful + Gould Ltd) t/a AtkinsRéalis whose registered office is situated at Woodcote Grove, Ashley Road, Epsom, Surrey, KT18 5BW

(the “**Client Representative**”)


EXECUTED AS A DEED by the **Client Representative**

by affixing hereto its common seal in the presence of

or Acting by Andrew Constable

Director

Witness _____

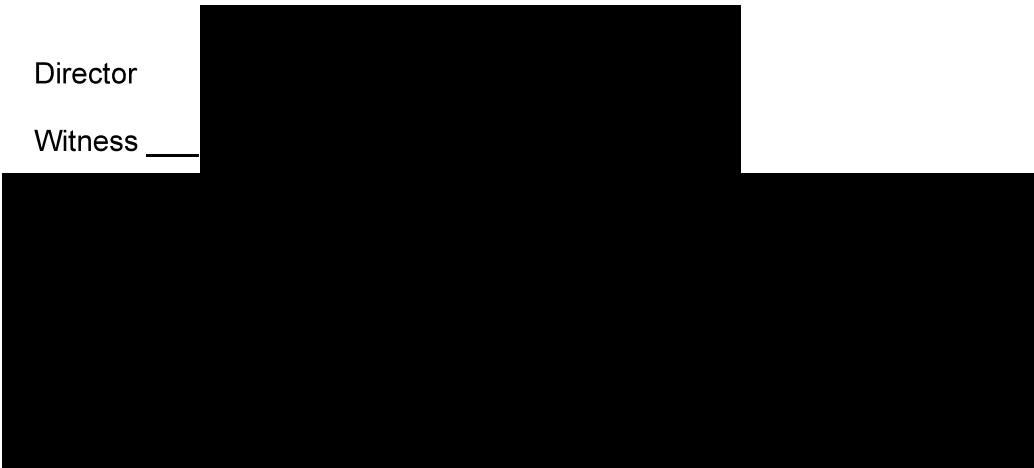

Tilbury Douglas Construction Limited whose registered office is situated at 30-40 Eastcheap,
London, EC3M 1HD

(the "Constructor" and "Lead Designer")


EXECUTED AS A DEED by the **Constructor and Lead Designer**

by affixing hereto its common seal in the presence of

or Acting by

Director

Director/Secretary



Gleeds Advisory Limited whose registered office is situated at 95 New Cavendish Street,
London, W1W 6XF

(the “**Cost Consultant**”)


EXECUTED AS A DEED by the **Cost Consultant**

by affixing hereto its common seal in the presence of

or Acting by

Director

Director/Secretary



Tilbury Douglas Construction Limited whose registered office is situated at 30-40 Eastcheap,
London, EC3M 1HD

(the "**Principal Designer**")

EXECUTED AS A DEED by the **Principal Designer**

by affixing hereto its common seal in the presence of

or Acting by

Director _____

Director/Secretary _____

