ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
1			**National Oceanography Centre (NOC) Roof Project**	**790 days**	**Mon 29/06/20**	**Fri 07/07/23**		**0%**
2			**Design (Technical Authority led)**	**65 days**	**Mon 29/06/20**	**Fri 25/09/20**		**0%**
3			**WS4 - Detail Design and Tender**	**65 days**	**Mon 29/06/20**	**Fri 25/09/20**		**0%**
4			**Pre-Construction Stage Agreement (PCSA)**	**65 days**	**Mon 29/06/20**	**Fri 25/09/20**		**0%**
5			Mobilisation of Contractor's design team	2 wks	Mon 29/06/20	Fri 10/07/20		0%
6			NOC submit F10 to HSE	1 day	Mon 29/06/20	Mon 29/06/20	5SS	0%
7			Detailed design	8 wks	Mon 29/06/20	Fri 21/08/20	5SS	0%
8			Contractor final pricing (incl. sub-contractor quc	6 wks	Mon 29/06/20	Fri 07/08/20	7SS	0%
9			Descision gateway: continue with PCSA Contrac	0 days	Fri 21/08/20	Fri 21/08/20	7,8	0%
10			Negotiations and construction contract award	3 wks	Mon 10/08/20	Fri 28/08/20	8	0%
11			Share contract sum and design package with NC	4 wks	Mon 31/08/20	Fri 25/09/20	10	0%
12			Project Board approve construction contract	0 days	Fri 25/09/20	Fri 25/09/20	11	0%
13			Main contract award	0 days	Fri 25/09/20	Fri 25/09/20	12	0%
14			**Construction**	**725 days**	**Mon 28/09/20**	**Fri 07/07/23**		**0%**
15			**WS5 - Main Construction**	**445 days**	**Mon 28/09/20**	**Fri 10/06/22**		**0%**
16			Mobilisation and Procurement (5 weeks duration a	5 wks	Mon 28/09/20	Fri 30/10/20	13	0%
17			Construction period (84 weeks duration assumed)	84 wks	Mon 02/11/20	Fri 10/06/22	16	0%
18			**WS6 - Completion and Handover**	**20 days**	**Mon 13/06/22**	**Fri 08/07/22**		**0%**
19			Construction completion and handover	4 wks	Mon 13/06/22	Fri 08/07/22	17	0%
20			**WS7 - Defects**	**260 days**	**Mon 11/07/22**	**Fri 07/07/23**		**0%**
21			Defects period	260 days	Mon 11/07/22	Fri 07/07/23	19	0%
22			**WS8 - Financial completion and handover**	**230 days**	**Mon 11/07/22**	**Fri 26/05/23**		**0%**
23			Financial completion and handover	230 days	Mon 11/07/22	Fri 26/05/23	19	0%

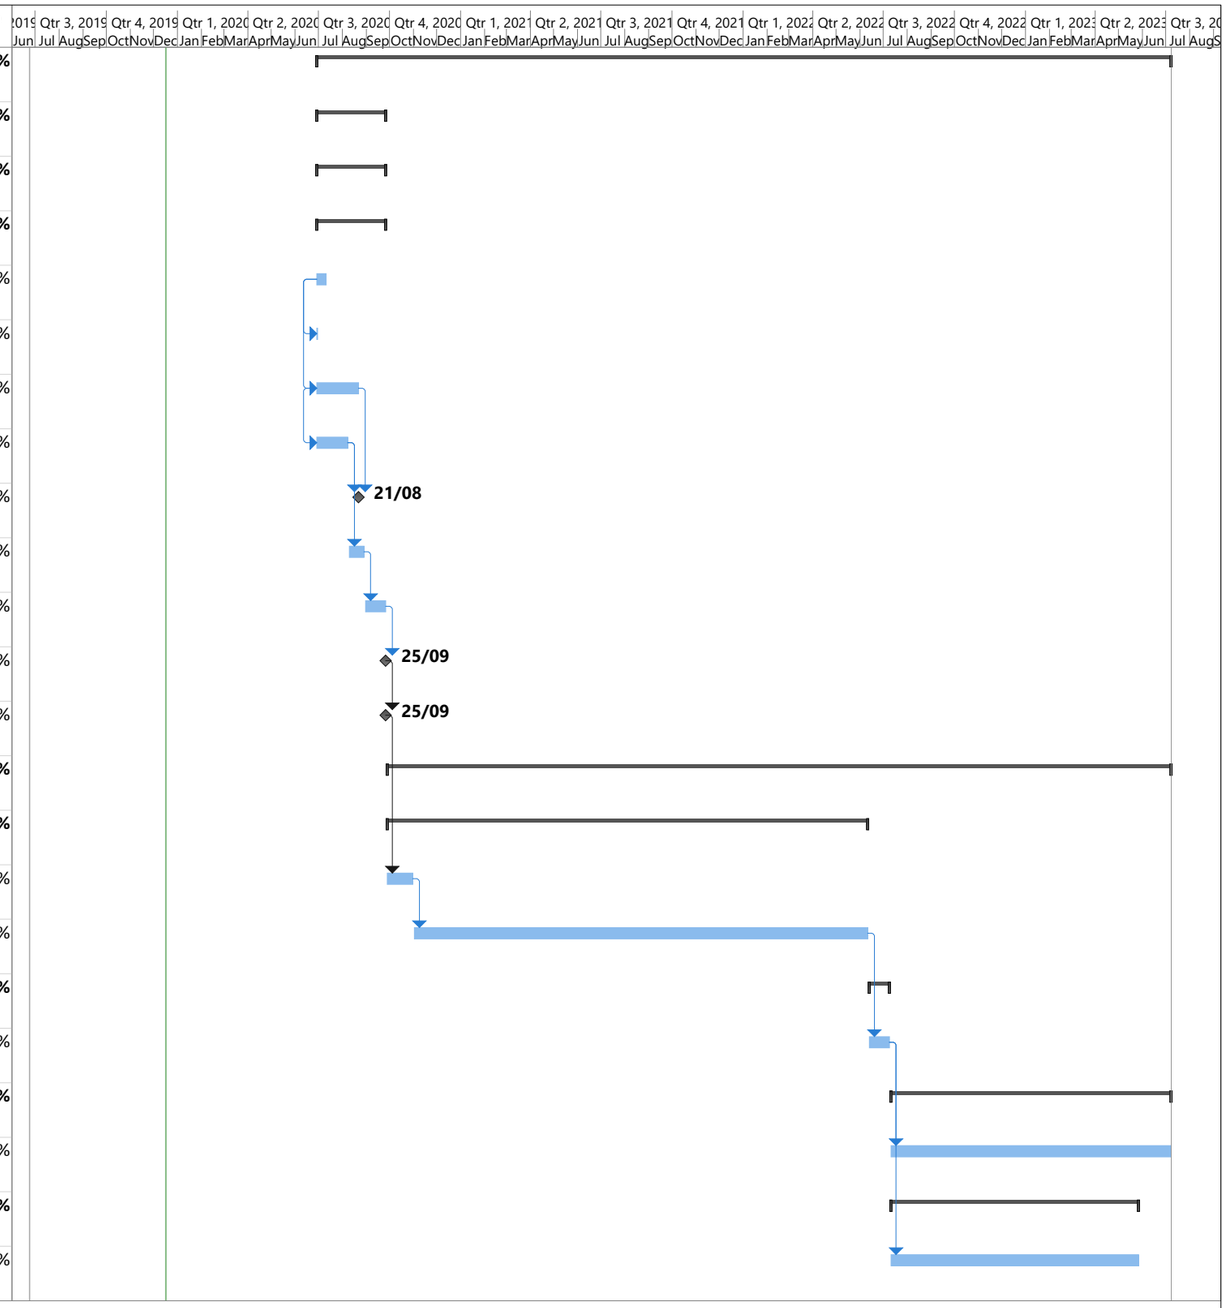

Project: National Oceanograph
Date: October 2019

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
