



Framework:	Mapping & Modelling Framework
------------	-------------------------------

Supplier:

Company Number:

Geographical Area: National

Project Name: MMF FE05 Hydrological Assessment of Winter Flood Events

Project Number:

Contract Type: Professional Service Contract

Option: Option C

Contract Number:

Stage: All\_Work\_Types

Revision	Status	Originator	Reviewer	Date

#### PROFESSIONAL SERVICE CONTRACT under the Mapping and Modelling Framework **CONTRACT DATA**

#### **Project Name**



This contract is made on between the Client and the Consultant


- This Contract is made pursuant to the Framework Agreement (the "Agreement") dated 16th day of May 2019 between the Client and the Consultant in elation to the NGSA Mapping and Modelling Support Framework. The entire Agreement and the following schedules are incorporated into this Contract by reference
- · Schedules 1 to 22 inclusive
- The following documents are incorporated into this contract by reference Invitation to tender, Project proposal proforma, Tender Evaluation Criteria, PSC\_WinterFloods\_TechScope, Services Activity Schedule, Inception Report, Appendix 1 - Spreadsheets, Appendix 2 - Reporting Templates.

#### Part One - Data provided by the Client

#### Statements given in all Contracts

1 General

The conditions of contract are the core clauses and the clauses for the following main Option, the Option for resolving and avoiding disputes and secondary Options of the NEC4 Professional Service Contract June 2017.

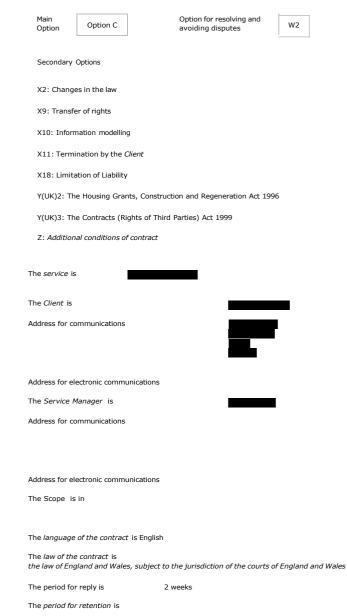

6 years following Completion or earlier termination

The following matters will be included in the Early Warning Register

2

3

Early warning meetings are to be held at intervals no longer than

2 weeks

#### 2 The Consultant's main responsibilities

The  $\ensuremath{\textit{key dates}}$  and  $\ensuremath{\textit{conditions}}$  to be met are

conditions to be met
'none set'
'none set'

key date 'none set' 'none set' 'none set'

The *Consultant* prepares forecasts of the total Defined Cost plus Fee and *expenses* at intervals no longer than

4 weeks

#### 3 Time

The starting date is

The Client provides access to the following persons, places and things

access date

The Consultant submits revised programmes at intervals no longer than

4 weeks

The  $\it completion\ date\ for\ the\ whole\ of\ the\ \it service\ is$ 

The period after the Contract Date within which the  ${\it Consultant}$  is to submit a first programme for acceptance is

4 weeks

### 4 Quality management

The period after the Contract Date within which the  ${\it Consultant}$  is to submit a quality policy statement and quality plan is

4 weeks

The period between Completion of the whole of the service and the  $defects\ date$  is

26 weeks

#### 5 Payment

The  $\it currency of the contract$  is the

£ sterling

The assessment interval is

Monthly

The expenses stated by the Client are as stated in Schedule 9

The interest rate is



Bank of England

All UK Offices

The locations for which the *Consultant* provides a charge for the cost of support people and office overhead are

The Consultant's share percentages and the share ranges are share range

 less than
 80 %

 from
 80 %
 to
 120 %

 greater than
 120 %

Consultant's share percentage

0 % 50 % 100 %

### 6 Compensation events

These are additional compensation events

1. 'not used'

2. 'not used'

'not used'
 'not used'


5. 'not used'

#### 8 Liabilities and insurance

These are additional Client's liabilities

- 'not used'
- 'not used'
- 'not us

The minimum amount of cover and the periods for which the Consultant maintains insurance are



#### Resolving and avoiding disputes

The tribunal is Litigation in the courts The Adjudicator is 'to be confirmed' 'to be confirmed' Address for communications to be confirmed Address for electronic communications

The Adjudicator nominating body is The Institution of Civil Engineers

#### Z Clauses

#### Z1 Disputes

Delete existing dause W2.1

### **Z2** Prevention

The text of clause 18 Prevention is deleted.

Delete the text of clause 60.1(12) and replaced by:

- Delete the text of clause 60.1(12) and repraced by:
  The service is are affected by any of the following events
  War, civil war, rebellion, revolution, insurrection, military or usurped power;
  Strikes, riots and civil commotion not confined to the employees of the Consultant and sub consultants,
  Ionising radiation or radioactive contamination from nuclear fuel or nuclear waste resulting from the combustion of nuclear fuel,
  Radioactive, toxic, explosive or other hazardous properties of an explosive nuclear device,
- Natural disaster,
- Fire and explosion,
   Impact by aircraft or other aerial device or thing dropped from them.

#### **Z3** Disallowed Costs

Add the following in second bullet of 11.2 (18) add:

(including compensation events with the sub contractor, i.e. payment for work that should not have been undertaken). Add the following additional bullets after 'and the cost of ':

- Add the following additional bullets after 'and the cost of ':

   Mistakes or delays caused by the Consultant's failure to follow standards in Scopes/quality plans.
- Reorganisation of the Consultant's project team.
- Additional costs or delays incurred due to Consultant's failure to comply with published and known guidance or document formats.
- . Exceeding the Scope without prior instruction that leads to abortive cost
- Re-working of documents due to inadequate QA prior to submission, i e. grammatical, factual arithmetical or design errors.
- Production or preparation of self-promotional material.
  Excessive charges for project management time on a commission for secondments or full time appointments (greater than 5% of commission value)
  Any hours exceeding 8 per day unless with prior written agreement of the Service Manager
- Any hours for travel beyond the location of the nearest consultant office to the project unless previously agreed with the Service Manager
   Attendance of additional individuals to meetings/ workshops etc who have not been previously invited by the Service Manager
- Costs associated with the attendance at additional meetings after programmed completion, if delay is due to Consultant performance.
   Costs associated with rectifications that are due to Consultant error or omission.
- Costs associated with the identification of opportunities to improve our processes and procedures for project delivery through the Consultant's involvement
   Was incurred due to a breach of safety requirements, or due additional work to comply with safety requirements
   Was incurred as a result of the Client issuing a Yellow or Red Card to prepare a Performance Improvement Plan
   Was incurred as a resulting of rectifying a non-compliance with the Framework Agreement and/or any call off contracts following an audit

## **Z4** Share on termination

Delete existing clause 93.3 and 93.4 and replace with: 92.3 In the event of termination in respect of a contract relating to services there is no *Consultant's* share'

### **Z6 The Schedule of Cost Components**

The Schedule of Cost Components are as detailed in the Framework Schedule 9.

### **Z24** Requirement for Invoice

Add the following sentence to the end of clause 51.1:

The Party to which payment is due submits an invoice to the other Party for the amount to be paid within one week of the Service Manager's approval of a fee note.

Delete existing clause 51.2 and replace with:

51.2 Each certified payment is made within one week after the paying Party receives an invoice from the other Party and

If a certified payment is late, interest is paid on the late payment. Interest is assessed from the date by which the late payment should have been made until the date when the late payment is made, and is included in the first assessment after the late payment is made

# **Secondary Options**

### **OPTION X2: Changes in the law**

The *law of the project* is the law of England and Wales, subject to the jurisdiction of the courts of England and Wales

# **OPTION X10: Information modelling**

The period after the Contract Date within which the *Consultant* is to submit a first Information Execution Plan for acceptance is 2 weeks

## **OPTION X18: Limitation of Liability**

The Consultant's liability to the Client for indirect or consequential loss is limited to

The *end of liability date is*Completion of the whole of the *service* 

### Y(UK2): The Housing Grants, Construction and Regeneration Act 1996

The period for payment is 14 days after the date on which payment becomes due

# Y(UK3): The Contracts (Rights of Third Parties Act) 1999

term *beneficiary* 

### Part Two - Data provided by the Consultant


Completion of the data in full, according to the Options chosen, is essential to create a complete contract.

#### 1 General

The Consultant is

Name

Address for communications



The following matters will be included in the Early Warning Register

5 Payment	The activity schedule is			
	The tendered total of the Prices is			
Resolving and avoiding disputes				
	The Senior Representatives of the Consultant are			
	Address for communications			
	Address for electronic communications			
	Name (2)			
	Address for communications			

X10: Information Modelling

The information execution plan identified in the Contract Data is

Address for electronic communications

# **Contract Execution**

Client execution

Signed Underhand by [PRINT NAME]

for and on behalf of the Environment Agency



# **Consultant** execution

Signed Underhand by [PRINT NAME]

for and on behalf of

